

Sharon Town Hall

Sharon, MA



COLANTONIO INC.
PROJECT # 18-3835

BKA

ARCHITECTS



DAEDALUS

samiotes



ARCHITECTURAL
ENGINEERS

TRAVERSE
landscape architects

The Sharon Standing Building Committee

COLANTONIO
40 YEARS OF BUILDING RELATIONSHIPS

Weekly Activity Update Friday November 30, 2018 Report #13

Current Week – Activities

- . Receive Steel Decking
- . Place First Floor Slab on Grade
- . Place Exterior Patio Depressed Slab
- . Place Vestibule Recessed Slab
- . Strip Forms and Column Box Outs
- . Backfill K.2 Footings and Piers
- . Federal Concrete Demobilize
- . Receive Lull and Jib

Next Week – Activities

- . Receive Structural Steel
- . Begin Steel Erection

Subcontractor	Trade	# of Workers Onsite
Briggs Engineering	Soil Testing	02
Titan Contractors Inc.	Site Work	01
Reed Land Surveying	Engineering	00
Federal Concrete	Foundations	02
Griffin Electric	Electrical	02
G.P East Steel	Steel Erector	00
Marguerite	Flat Work	12
United Site Services	Site Sanitary	01
Colantonio Inc	Labor	02
Police	Detail	01
BKA	Architect	02
Daedalus	Owner Representative	02
Colantonio Inc.	Construction Manager	03
TOTAL # Onsite This Week		30

Safety

- Safety Orientation for New Jobsite Workers Performed First Day of Work. Total Number of Onsite Workers/Visitors Orientated = 53
- All Workers Wear 100% Hard Hats and Reflective Clothing.
- Colantonio Inc. Site Specific Safety Officer on Site Full Time.
- Stone Laid Down at Bradford St. Entrance for Tracking
- Weekly Toolbox Talks are Conducted Within Each Trade And a Copy is Submitted to Colantonio Inc.
- Each Contractor Completes a Daily Work Report which Is Kept On File
- Construction Progress Meeting are Held Tuesday at 1PM.
- 67 Days With Zero Worker Accident
- 67 Days Without a Lost Time Accident

Quality Control

- Materials Delivered To The Site Cross Referenced Against Drawings, Submittals and Specifications prior to installation.
- Colantonio Inc and Subcontractor Review of Drawings and Specification Compliance Prior to Work Commencing
- 74 Random Quality Control Inspection Reports have been completed, of those: 0 remain as “Open” and “Non-Conforming”

Miscellaneous

- Additional Unknown Soils Removed from the Site.
- No Parking During Construction Time Posted on Bradford Avenue
- 1st Floor Slab Placement Completed. FF/FL – 36/27
- Briggs On Site for Concrete, Compaction and Rebar inspections



Steel Deck Delivery



Steel Deck Unload




Vapor Barrier and Reinforcing




Concrete Pump Truck



Slab Placement

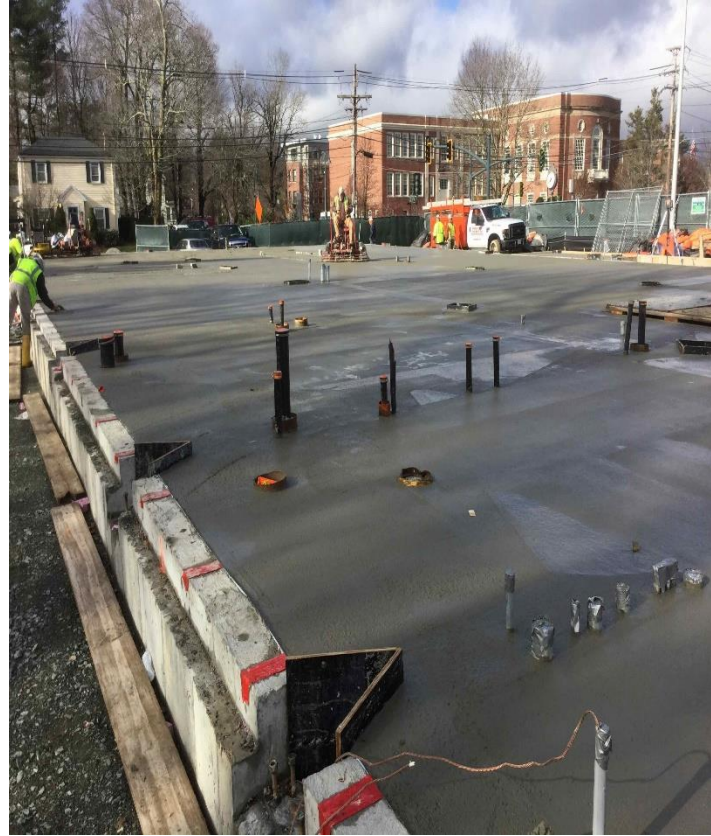

Slab Placement

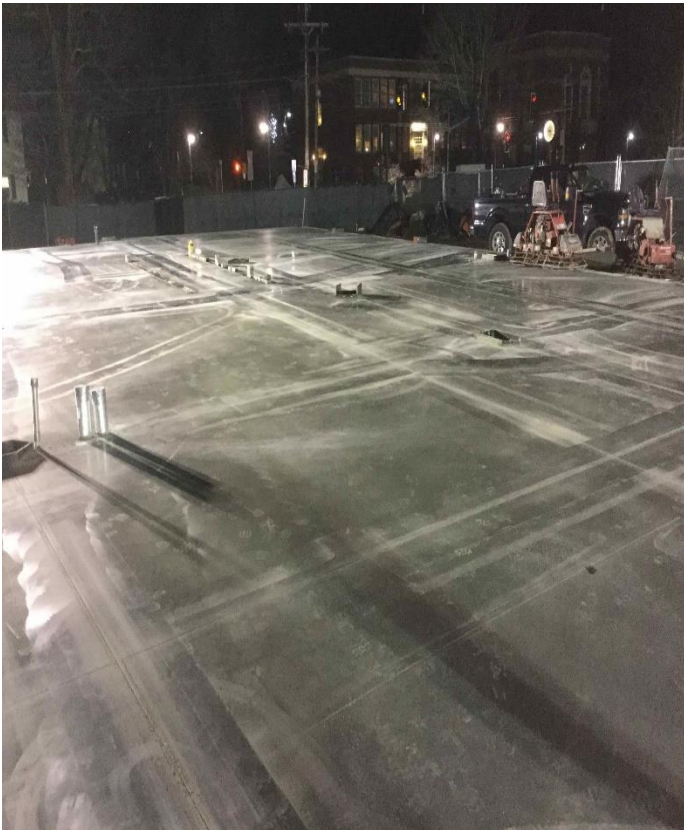

Concrete Finishing



Apply Cure and Seal
