

Sharon Town Hall Sharon, MA



COLANTONIO INC.
PROJECT # 18-3835

BKA

ARCHITECTS



DAEDALUS

samiotes

ARCHITECTURAL
ENGINEERS

TRAVERSE
landscape architects

The Sharon Standing Building Committee

COLANTONIO
40 YEARS OF BUILDING RELATIONSHIPS

Weekly Activity Update Saturday December 21, 2018 Report #16

Current Week – Activities

- . Complete Low Roof Detail and Bridging
- . Install Roof Frames
- . Install Roof Deck and Weld
- . Briggs Roof Deck Inspection
- . Delivery of Temporary Stair Material
- . Excavate for Temporary Electric
- . Install Underground Temp Electric
- . Back Fill Temporary Electric
- . Temporary Power Energized to Building

Next Week – Activities

- . Install 2nd Floor Deck and Weld
- . Install Shear Studs
- . Install Pour Stop
- . Turnover Roof Deck
- . Build Temporary Stair Platform to 2nd Floor
- . Begin Forming Column Box Outs
- . Install temporary Lighting
- . Heater Delivery

Weekly Activity Update Saturday December 21,2018 Report #16

Subcontractor	Trade	# of Workers Onsite
Briggs Engineering	Soil Testing	00
Titan Contractors Inc.	Site Work	00
Reed Land Surveying	Engineering	00
Federal Concrete	Foundations	00
Griffin Electric	Electrical	02
G.P East Steel	Steel Erector	05
Colantonio Inc.	Carpenter	01
United Site Services	Site Sanitary	01
Colantonio Inc.	Earth Work	02
BJA	Architect	02
Daedalus	Owner Representative	01
Colantonio Inc.	Construction Manager	02
TOTAL # Onsite This Week		16

Safety

- **Safety Orientation for New Jobsite Workers Performed First Day of Work. Total Number of Onsite Workers/Visitors Orientated = 57**
- **All Workers Wear 100% Hard Hats and Reflective Clothing.**
- **Fencing and Scrim Reviewed Each Week for Safety and Appearance**
- **Weekly Toolbox Talks are Conducted Within Each Trade And a Copy is Submitted to Colantonio Inc.**
- **Each Contractor Completes a Daily Work Report which Is Kept On File**
- **Construction Progress Meeting are Held Tuesday at 1PM.**
- **83 Days With Zero Worker Accident**
- **83 Days Without a Lost Time Accident**

Quality Control

- **Materials Delivered To The Site Cross Referenced Against Drawings, Submittals and Specifications prior to installation.**
- **Colantonio Inc and Subcontractor Review of Drawings and Specification Compliance Prior to Work Commencing**
- **75 Random Quality Control Inspection Reports have been completed, of those: 1 remain as “Open” and “Non-Conforming”**

Miscellaneous

- **No Parking During Construction Time Posted on Bradford Avenue**
- **2nd Floor Slab on Deck Pre-Placement Meeting January 2nd**
- **Roof Deck Inspection – Thursday December 20th,2018**
- **Tentative Slab on Deck Placement – Week of January 7th, 2019**



Roof Deck



Roof Deck




Frame and Deck



Joists and Deck



2nd Floor Framing

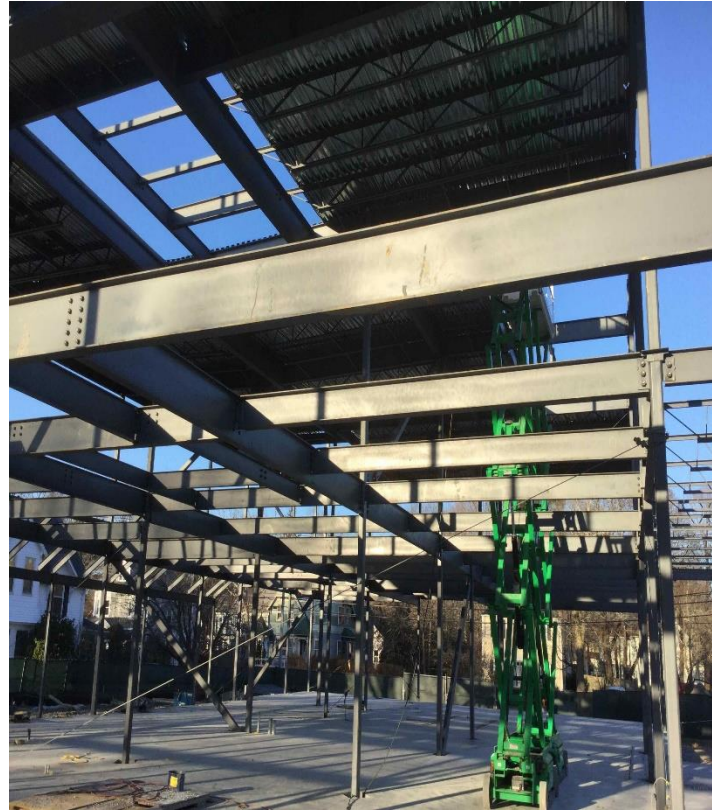

2nd Floor Framing



Underground Temp. Electric



Temporary Electric
