

Sharon Town Hall

Sharon, MA



COLANTONIO INC.
PROJECT # 18-3835

BKA

ARCHITECTS



DAEDALUS

samiotes



ARCHITECTURAL
ENGINEERS

TRAVERSE
landscape architects

The Sharon Standing Building Committee

COLANTONIO
40 YEARS OF BUILDING RELATIONSHIPS

Weekly Activity Update Saturday January 26, 2019 Report #19

Current Week – Activities

- Continue Second Floor Exterior Framing
- Continue Exterior Sheathing
- Continue Roof Framing – Clerestory
- Continue Roof Sheathing
- Begin Elevator CMU Shaft
- Begin Roof Blocking

Next Week – Activities

- Complete Roof Framing
- Complete Roof Blocking
- Continue Exterior Framing
- Continue Exterior Sheathing
- Receive Steel Door Frames

Subcontractor	Trade	# of Workers Onsite
Briggs Engineering	Concrete Testing	00
Titan Contractors Inc.	Site Work	01
Reed Land Surveying	Engineering	00
Marmello	Masonry	04
Griffin Electric	Electrical	01
G.P East Steel	Steel Erector	00
Colantonio Inc.	Carpenter	02
United Site Services	Site Sanitary	01
Colony Drywall	Framing	08
BJA	Architect	02
Daedalus	Owner Representative	02
Colantonio Inc.	Construction Manager	03
TOTAL # Onsite This Week		24

Safety

- **Safety Orientation for New Jobsite Workers Performed First Day of Work. Total Number of Onsite Workers/Visitors Orientated = 68**
- **All Workers Wear 100% Hard Hats and Reflective Clothing.**
- **Fencing and Scrim Reviewed Each Week for Safety and Appearance**
- **Weekly Toolbox Talks are Conducted Within Each Trade And a Copy is Submitted to Colantonio Inc.**
- **Each Contractor Completes a Daily Work Report which Is Kept On File**
- **Construction Progress Meeting are Held Tuesday at 1PM.**
- **109 Days With Zero Worker Accident**
- **109 Days Without a Lost Time Accident**

Quality Control

- **Materials Delivered To The Site Cross Referenced Against Drawings, Submittals and Specifications prior to installation.**
- **Colantonio Inc and Subcontractor Review of Drawings and Specification Compliance Prior to Work Commencing**
- **83 Random Quality Control Inspection Reports have been completed, of those: 3 remain as “Open” and “Non-Conforming”**

Miscellaneous

- **No Parking During Construction Time Posted on Bradford Avenue**
- **Colantonio Inc. subcontractor meeting to be held on Tuesdays at 10AM**




2nd Floor Slab Placement



2nd Floor Slab Placement



2nd Floor Slab Finishing

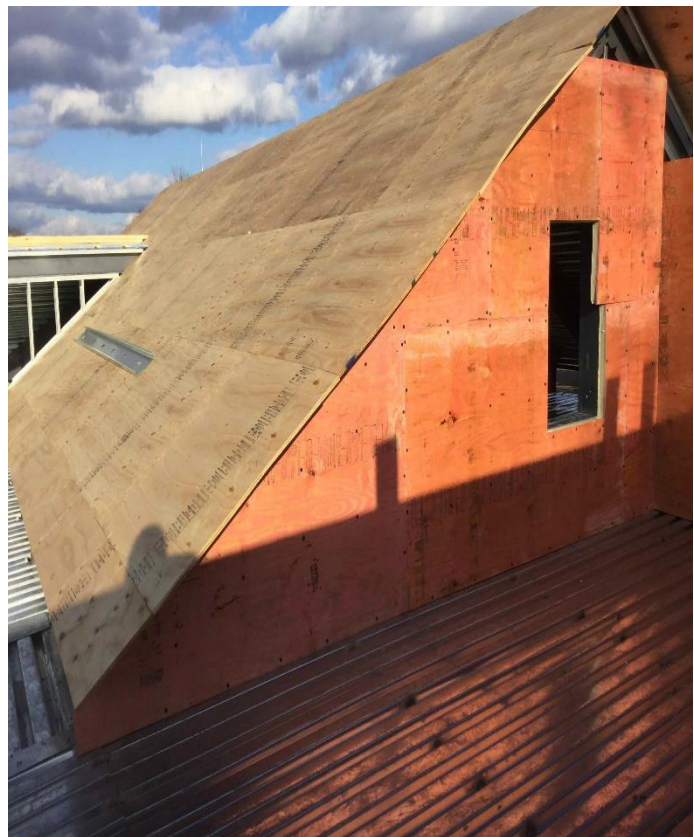


2nd Floor Slab Finish



Signed Beam In Place



Roof Sheathing

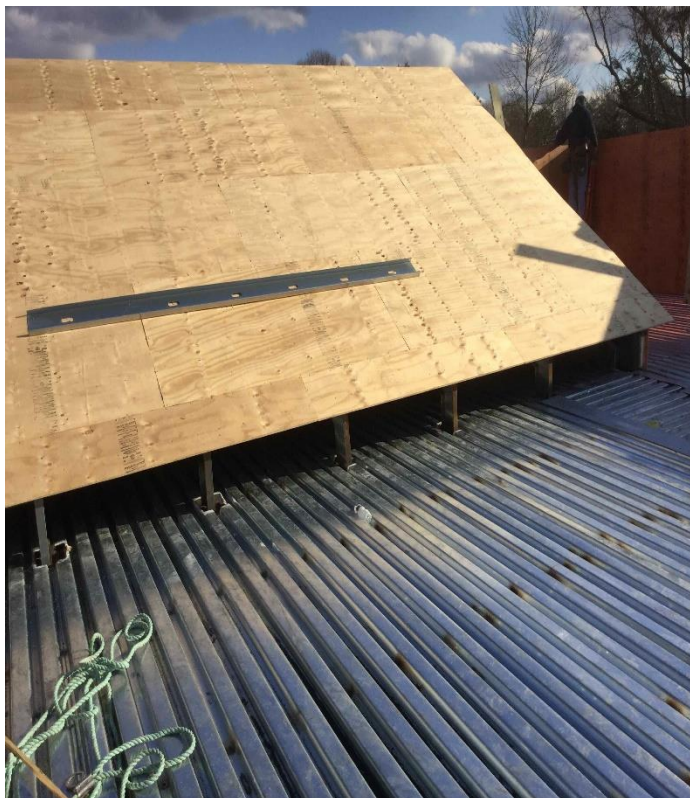

Roof Framing



Roof Sheathing
