

Sharon Town Hall Sharon, MA



**COLANTONIO INC.
PROJECT # 18-3835**

BKA

ARCHITECTS



DAEDALUS

samiotes



ARCHITECTURAL
ENGINEERS

TRAVERSE
landscape architects

The Sharon Standing Building Committee

COLANTONIO
40 YEARS OF BUILDING RELATIONSHIPS

Weekly Activity Update

Friday February 1, 2019 Report #20

Current Week – Activities

- . Continue Elevator Shaft
- . Continue Elevator Machine Room
- . Receive Steel Doors and Frames
- . Continue Exterior Framing
- . Continue Exterior Sheathing
- . Receive Interior Framing
- . Install Roof Blocking
- . Clean Roofing Debris
- . Continue Above Ceiling Coordination
- . Erect Temporary Roof Ladders

Next Week – Activities

- . Continue Exterior Framing South Elevation
- . Continue Exterior Framing West Elevation
- . Continue Exterior Sheathing – West
- . Continue Exterior Sheathing – East
- . Receive Roof Drain Piping
- . Receive Roofing Materials
- . Install Tyvek Building Wrap
- . Layout Mechanical Curbs
- . Complete Roof Blocking
- . Building Envelope Meeting

Subcontractor	Trade	# of Workers Onsite
Briggs Engineering	Concrete Testing	00
Titan Contractors Inc.	Site Work	00
Reed Land Surveying	Engineering	00
Marmello	Masonry	04
Griffin Electric	Electrical	01
G.P East Steel	Steel Erector	00
Colantonio Inc.	Carpenter	03
United Site Services	Site Sanitary	01
Colony Drywall	Framing	08
BJA	Architect	02
Daedalus	Owner Representative	02
Colantonio Inc.	Construction Manager	03
TOTAL # Onsite This Week		24

Safety

- **Safety Orientation for New Jobsite Workers Performed First Day of Work. Total Number of Onsite Workers/Visitors Orientated = 68**
- **All Workers Wear 100% Hard Hats and Reflective Clothing.**
- **Fencing and Scrim Reviewed Each Week for Safety and Appearance**
- **Weekly Toolbox Talks are Conducted Within Each Trade And a Copy is Submitted to Colantonio Inc.**
- **Each Contractor Completes a Daily Work Report which Is Kept On File**
- **Construction Progress Meeting are Held Tuesday at 1PM.**
- **114 Days With Zero Worker Accident**
- **114 Days Without a Lost Time Accident**

Quality Control

- **Materials Delivered To The Site Cross Referenced Against Drawings, Submittals and Specifications prior to installation.**
- **Colantonio Inc and Subcontractor Review of Drawings and Specification Compliance Prior to Work Commencing**
- **90 Random Quality Control Inspection Reports have been completed, of those: 2 remain as “Open” and “Non-Conforming”**

Miscellaneous

- **No Parking During Construction Time Posted on Bradford Avenue**
- **Colantonio Inc. subcontractor meeting to be held on Tuesdays at 10AM**
- **Building Envelope Meeting Scheduled for Tuesday February 5th, 2019**



Exterior Sheathing




North Elevation




Exterior Sheathing



Clerestory Sheathing

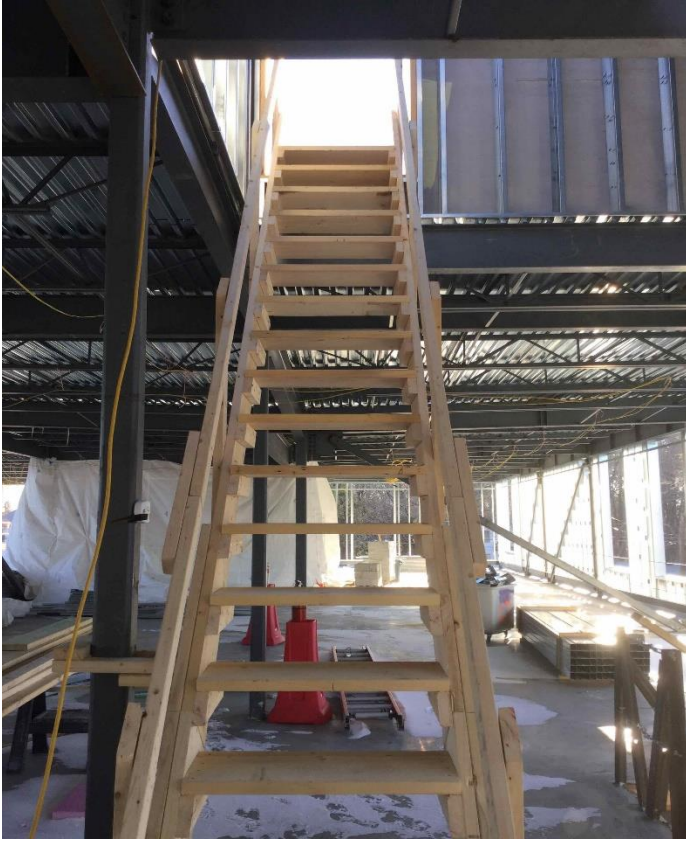

Temp. Roof Access

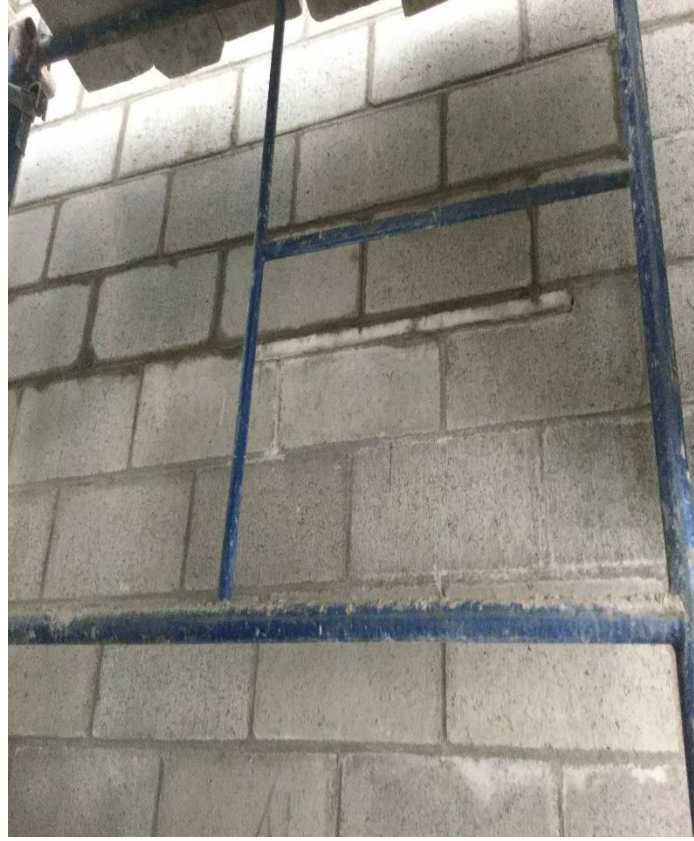

Elevator Rail Bracket



Gable Blocking



South Elevation
