

Sharon Town Hall Sharon, MA



COLANTONIO INC.
PROJECT # 18-3835

BA

ARCHITECTS



DAEDALUS

samiotes

ARCHITECTURAL
ENGINEERS

TRAVERSE
landscape architects

The Sharon Standing Building Committee

COLANTONIO
40 YEARS OF BUILDING RELATIONSHIPS

Weekly Activity Update

Saturday March 30, 2019 Report #27

Current Week – Activities

- . Continue Window Installation
- . Continue Window Flashing
- . Continue Cupola Windows and Trim
- . Begin Lap Siding
- . Receive Exterior Door Hardware
- . Continue Fire Alarm/Elec Rough- 2nd
- . Begin Electric Rough 1st Floor
- . Continue Vent and Water Rough – 2nd
- . Continue Water Rough – 1st Floor
- . Continue Clerk and Shared Vault
- . Continue Shingle and Gutter Membrane
- . Frame Exterior Soffits
- . Lighting Rough Exterior Ceilings
- . Field Measure Clerestory Windows
- . Receive 2nd Floor Drywall
- . Top off Walls – 2nd Floor
- . Install In Wall Blocking
- . Meeting Room Spray Foam Insul
- . Begin Fire Protection Rough

Next Week – Activities

- . Continue Lap Siding Installation
- . Begin Shingle Siding Installation
- . Window Testing
- . Finish Cupola Trim
- . HVAC Rough – 1st Floor
- . Continue Mech. Piping – 2nd Floor
- . Continue 1st Floor Electric Rough
- . Continue 1st Floor Water Pipe Install
- . Continue Fire Protection Rough
- . 2nd Floor Electrical Inspection
- . 2nd Floor Cast Iron Plumbing Inspection
- . Request Framing Inspection – 2nd Floor
- . Continue Top of Wall 2nd Floor
- . Electric Rough Elev. Machine Room
- . Install Elev. Pit Membrane
- . Begin Shingle Installation – Low Roof

Subcontractor	Trade	# of Workers Onsite
InterTek	Window Testing	02
Titan Contractors Inc.	Site Work	00
Carlysle	Fire Protection	02
Marmello	Masonry	00
Griffin Electric	Electrical	04
SMJ Inc	Misc. Metals	00
Colantonio Inc.	Carpenter	05
United Site Services	Site Sanitary	01
Colony Drywall	Framing	06
Colantonio	Labor	01
LaPan Mechanical	Plumbing	02
Division 15	HVAC	04
Greenwood Industries	Roofing	04
Sharon Police	Detail	01
NE Foam	Insulation	02
Andersen	Window Representative	00
FireLock	Vault Installer	05
Color Concepts	Painting	01
BKA	Architect	02
Daedalus	Owner Representative	02
Colantonio Inc.	Construction Manager	02
TOTAL # Onsite This Week		46

Safety

- **Safety Orientation for New Jobsite Workers Performed First Day of Work. Total Number of Onsite Workers/Visitors Orientated = 102**
- **All Workers Wear Proper PPE At All Times**
- **Fencing and Scrim Reviewed Each Week for Safety and Appearance**
- **Weekly Toolbox Talks are Conducted Within Each Trade And a Copy is Submitted to Colantonio Inc.**
- **Each Contractor Completes a Daily Work Report which Is Kept On File**
- **Construction Progress Meeting are Held Tuesday at 1PM.**
- **159 Days With Zero Worker Accident**
- **159 Days Without a Lost Time Accident**

Quality Control

- **Materials Delivered To The Site Cross Referenced Against Drawings, Submittals and Specifications prior to installation.**
- **Colantonio Inc and Subcontractor Review of Drawings and Specification Compliance Prior to Work Commencing**
- **130 Random Quality Control Inspection Reports have been completed, of those: 02 remain as “Open” and “Non-Conforming”**

Miscellaneous

- **No Parking During Construction Time Posted on Bradford Avenue**
- **Colantonio Inc. subcontractor meeting to be held on Tuesdays at 10AM**
- **Coordination Drawings – 2nd Floor 100%, 1st Floor 80%**
- **Workers Utilizing Deb Sampson Parking Lot**
- **Window Test Thursday April 4, 2019**




Shingle and Venting



Cupola Trim Installation



Attic Spray Foam Insulation

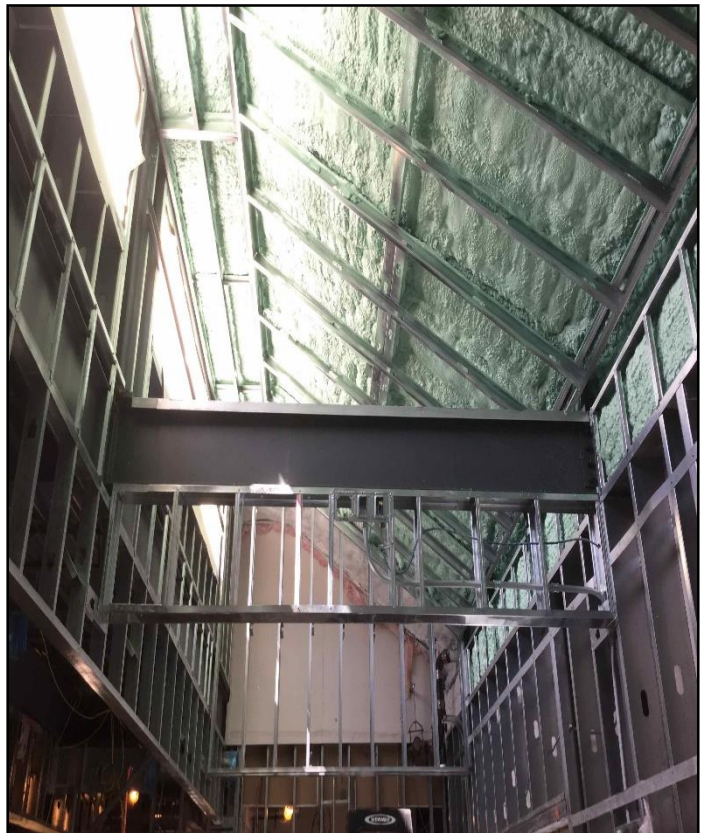

Meeting Room Insulation




GWB Ceiling Framing



In Wall Blocking



Exterior Ceiling Lights

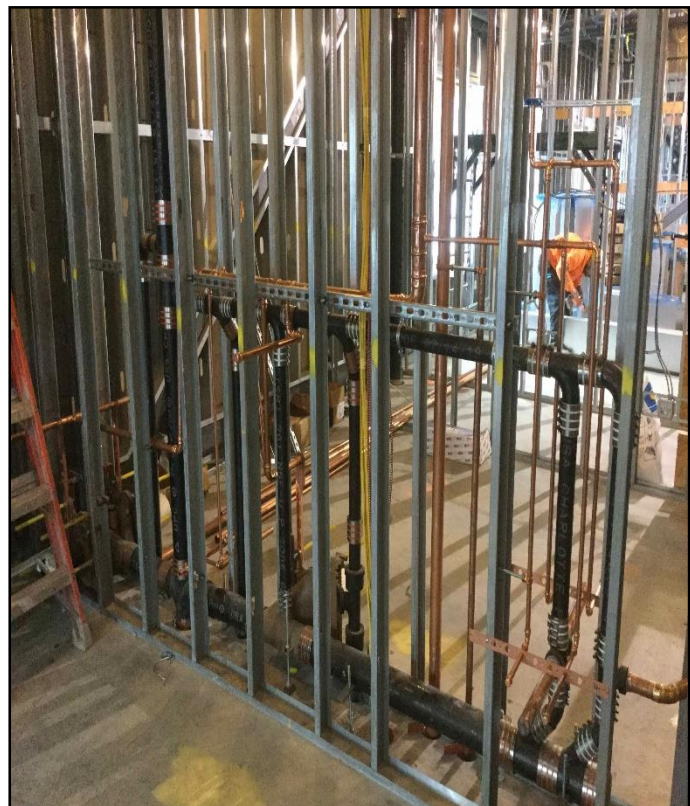

Bathroom Plumbing Rough
