

Sharon Town Hall Sharon, MA



COLANTONIO INC.
PROJECT # 18-3835

BKA

ARCHITECTS



DAEDALUS

samiotes



ARCHITECTURAL
ENGINEERS

TRAVERSE
landscape architects

The Sharon Standing Building Committee



Weekly Activity Update

Friday April 05, 2019 Report #28

Current Week – Activities

- . Continue 2nd Floor Sprinkler Rough
- . Begin 1st Floor Electric Rough
- . Wiring Inspection – 2nd Floor
- . Plumbing Inspection – 2nd Floor
- . Framing Inspection – 2nd Floor
- . Install Insulation and Poly
- . Begin Installing Drywall
- . Install Heat Pumps
- . Install Refrigerant Lines – 2nd Floor
- . Continue Canopy Roof Shingle Install
- . Install Canopy Plywood
- . Continue Install of Fascia and Trim
- . Clerk and Shared Vault Completion
- . Continue 1st Floor Layout and Frame
- . Receive Batt Insulation
- . Receive Pipe Insulation

Next Week – Activities

- . Continue Lap Siding Installation
- . Begin Shingle Siding Installation
- . Continue Electric Rough – 1st Floor
- . Continue Plumbing Rough – 1st Floor
- . Begin Pipe Insulation – 2nd Floor
- . Continue Drywall Install – 2nd Floor
- . Begin Mud and Tape Drywall – 2nd Floor
- . Continue 2nd Floor Sprinkler
- . Receive 1st Floor Sprinkler
- . Begin 1st Floor Sprinkler
- . Continue 1st Floor layout and Framing
- . Complete Transformer Pad
- . Complete Primary Electric Piping
- . Layout and Excavate for Septic Tanks

Subcontractor	Trade	# of Workers Onsite
InterTek	Window Testing	02
Titan Contractors Inc.	Site Work	00
Carlisle	Fire Protection	02
Marmello	Masonry	00
Griffin Electric	Electrical	05
FireLock	Vault Install	03
Colantonio Inc.	Carpenter	05
United Site Services	Site Sanitary	01
Colony Drywall	Framing	07
Colantonio	Labor	01
LaPan Mechanical	Plumbing	02
Division 15	HVAC	04
Greenwood Industries	Roofing	03
Sharon Police	Detail	01
NE Foam	Insulation	02
Andersen	Window Representative	01
BKA	Architect	02
Daedalus	Owner Representative	02
Colantonio Inc.	Construction Manager	02
TOTAL # Onsite This Week		45

Safety

- **Safety Orientation for New Jobsite Workers Performed First Day of Work. Total Number of Onsite Workers/Visitors Orientated = 106**
- **All Workers Wear Proper PPE At All Times**
- **Fencing and Scrim Reviewed Each Week for Safety and Appearance**
- **Weekly Toolbox Talks are Conducted Within Each Trade And a Copy is Submitted to Colantonio Inc.**
- **Each Contractor Completes a Daily Work Report which Is Kept On File**
- **Construction Progress Meeting are Held Tuesday at 1PM.**
- **164 Days With Zero Worker Accident**
- **164 Days Without a Lost Time Accident**

Quality Control

- **Materials Delivered To The Site Cross Referenced Against Drawings, Submittals and Specifications prior to installation.**
- **Colantonio Inc and Subcontractor Review of Drawings and Specification Compliance Prior to Work Commencing**
- **136 Random Quality Control Inspection Reports have been completed, of those: 01 remain as “Open” and “Non-Conforming”**

Miscellaneous

- **No Parking During Construction Time Posted on Bradford Avenue**
- **Colantonio Inc. subcontractor meeting to be held on Tuesdays at 10AM**
- **Coordination Drawings – 2nd Floor 100%, 1st Floor 80%**
- **Workers Utilizing Deb Sampson Parking Lot**
- **Window Test Thursday April 4, 2019 – Passed Test**



Lap Siding Installation



Sprinkler Main Install



Meeting Room Rough




Lap Siding Insatallation




Window Testing



Window Testing

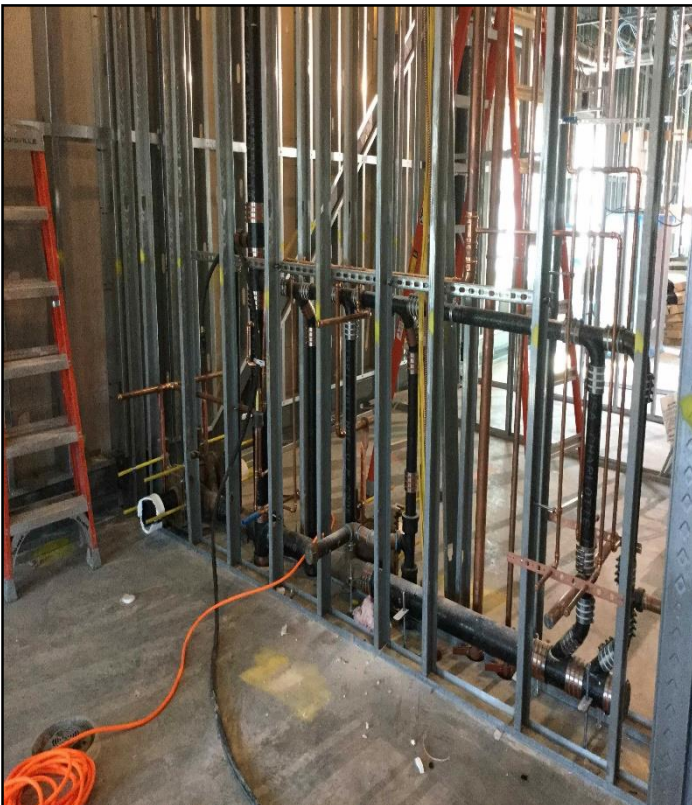

Plumbing Rough

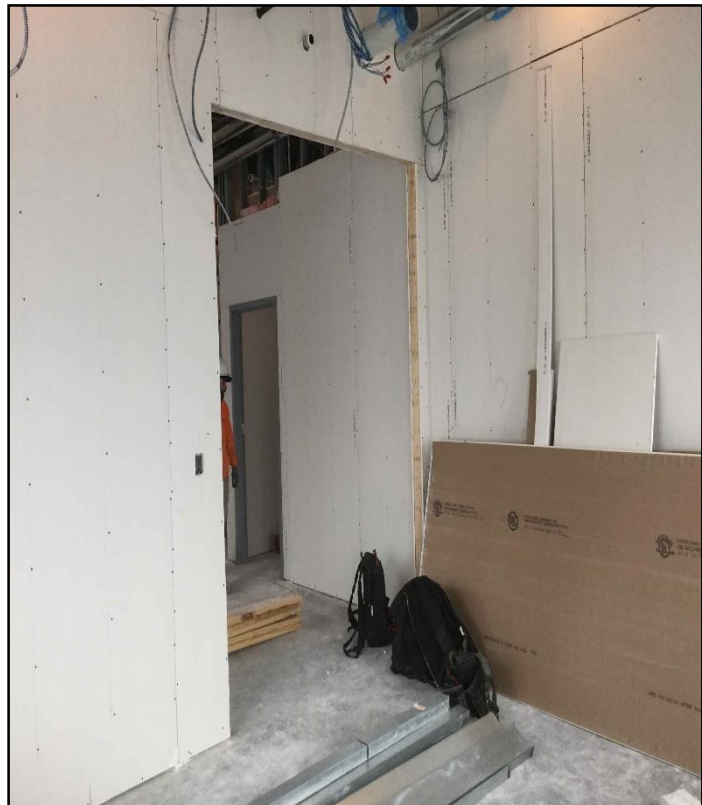

Drywall Installation
