

# Sharon Town Hall Sharon, MA



**COLANTONIO INC.**  
**PROJECT # 18-3835**

**BKA**

ARCHITECTS



**DAEDALUS**

**samiotes**

ARCHITECTURAL  
**ENGINEERS**

**TRAVERSE**  
landscape architects

## The Sharon Standing Building Committee

**COLANTONIO**  
40 YEARS OF BUILDING RELATIONSHIPS

### Weekly Activity Update

Friday May 4, 2019 Report #32

#### Current Week – Activities

- . Continue Drywall Install – 1<sup>st</sup> Floor
- . Begin Mud and Tape – 1<sup>st</sup> Floor
- . Finish Coat and Sand Walls – 2<sup>nd</sup> Floor
- . Install Acoustical Sealant – 2<sup>nd</sup> Floor
- . Begin Prime/Paint Walls – 2<sup>nd</sup> Floor
- . Continue Heat Pump Rough – 2<sup>nd</sup> Floor
- . Continue Tel/Data Rough – 2<sup>nd</sup> Floor
- . Spray Foam Deck – Stair #2
- . Insulate/Poly and Drywall Stair #2
- . Insulate and Drywall Stair #1
- . Continue HVAC Rough – 1<sup>st</sup> Floor
- . Continue Sprinkler Rough - Mech. Room
- . 1<sup>st</sup> Floor Sprinkler Pressure Test
- . Continue Lighting Rough – 2<sup>nd</sup> Floor
- . Install Shingle Siding – East Elevation
- . Install Trim and Column Blocking – North
- . Begin Cupola Metal Roof

#### Next Week – Activities

- . Continue Prime/Paint Walls – 2<sup>nd</sup> Floor
- . Begin Ceiling Grid Installation – 2<sup>nd</sup> Floor
- . Begin Bathroom Tile – 2<sup>nd</sup> floor
- . Install Mic Conduit – Meeting Room
- . Install Walls and Ceiling – Meeting Room
- . Mud/Tape Meeting Room Walls
- . Sand 2<sup>nd</sup> Floor Walls – East
- . Complete Mech. Rough – 2<sup>nd</sup> floor
- . Complete 2<sup>nd</sup> Floor Duct Wrap
- . Continue Insul Drywall – 1<sup>st</sup> Floor
- . Continue Lighting Rough – 1<sup>st</sup> Floor
- . Install Devices – 2<sup>nd</sup> Floor
- . Continue Shingle Siding – East
- . Continue Trim and Fascia – North
- . Continue Cupola Metal
- . Continue Gutter metal

Subcontractor	Trade	# of Workers Onsite
Color Concepts	Painting	01
Titan Contractors Inc.	Site Work	00
Carlysle	Fire Protection	02
Marmello	Masonry	00
Griffin Electric	Electrical	06
General Insulation	Insulator	01
Colantonio Inc.	Carpenter	05
United Site Services	Site Sanitary	01
Colony Drywall	Framing	09
Colantonio	Labor	01
LaPan Mechanical	Plumbing	02
Division 15	HVAC	05
Delta Beckwith	Elevator	01
Alum/Glass Concepts	Aluminum Openings	00
Greenwood	Roofing	02
BKA	Architect	02
Daedalus	Owner Representative	02
Colantonio Inc.	Construction Manager	03
<b>TOTAL # Onsite This Week</b>		<b>43</b>

### **Safety**

- **Safety Orientation for New Jobsite Workers Performed First Day of Work. Total Number of Onsite Workers/Visitors Orientated = 119**
- **All Workers Wear Proper PPE At All Times**
- **Fencing and Scrim Reviewed Each Week for Safety and Appearance**
- **Weekly Toolbox Talks are Conducted Within Each Trade And a Copy is Submitted to Colantonio Inc.**
- **Each Contractor Completes a Daily Work Report which Is Kept On File**
- **Construction Progress Meeting are Held Tuesday at 1PM.**
- **184 Days With Zero Worker Accident**
- **184 Days Without a Lost Time Accident**

### **Quality Control**

- **Materials Delivered To The Site Cross Referenced Against Drawings, Submittals and Specifications prior to installation.**
- **Colantonio Inc and Subcontractor Review of Drawings and Specification Compliance Prior to Work Commencing**
- **167 Random Quality Control Inspection Reports have been completed, of those: 02 remain as “Open” and “Non-Conforming”**


### **Miscellaneous**

- **Colantonio Inc. subcontractor meeting to be held on Tuesdays at 10AM**
- **Controls Integration Meeting – Tuesday May 14, 2019 12PM**
- **1<sup>st</sup> Floor Sprinkler Test Witnessed by Town and OPM**






**1st Floor Soffit**

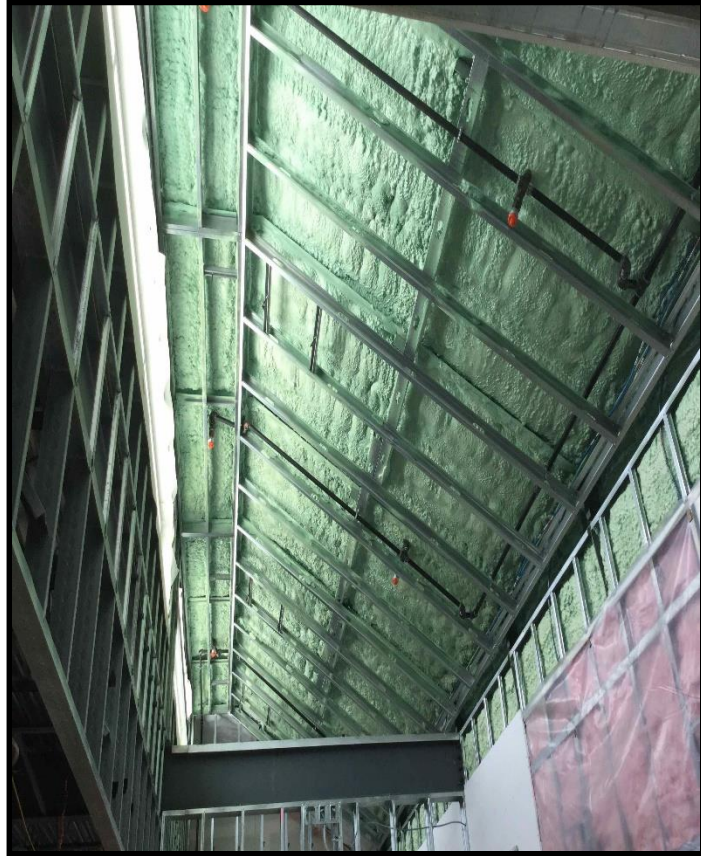

**Meeting Room Electric Rough**



**2nd Floor Mechanical Piping**

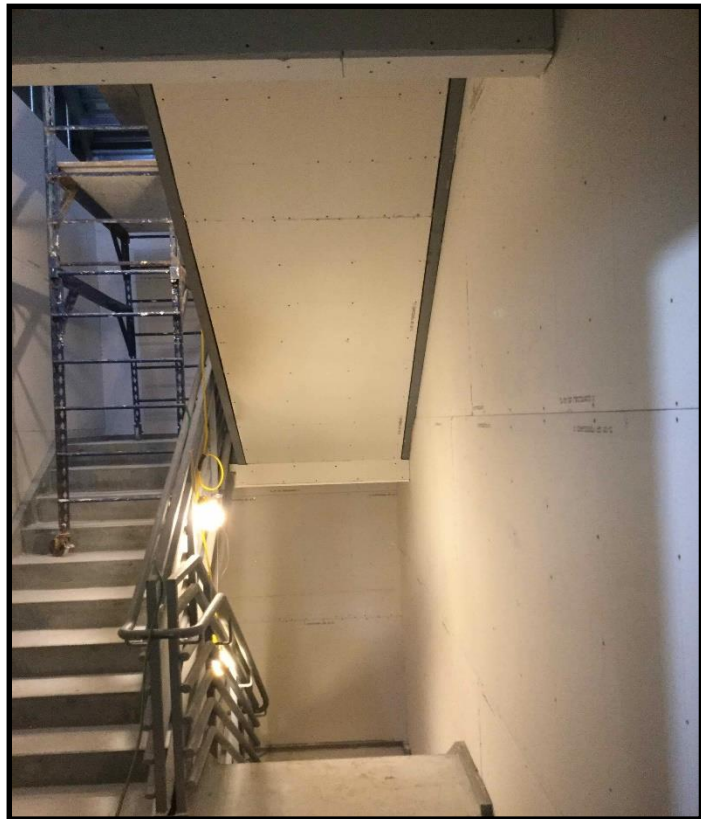


**Stair #2 Drywall**






**Cupola Work**

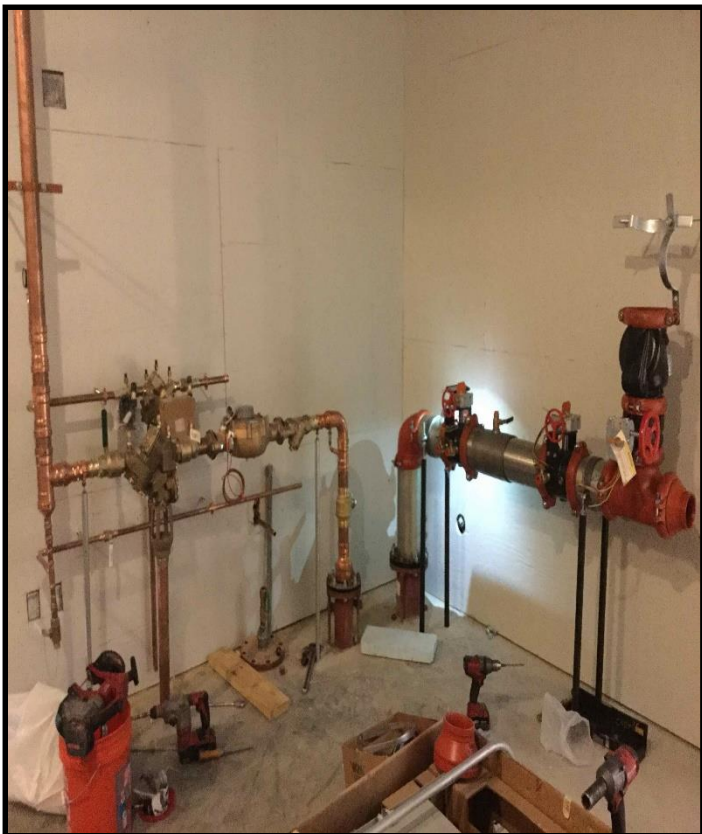

**Mechanical Room Rough**



**Railing Assembly**

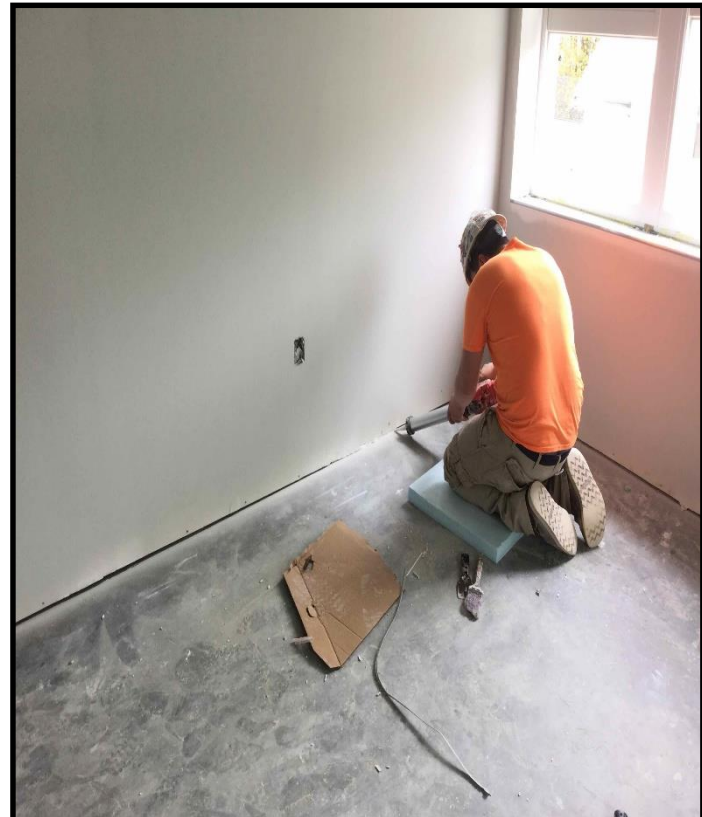

**Acoustic Sealant Installation**
