

Sharon Town Hall Sharon, MA



COLANTONIO INC.
PROJECT # 18-3835

BKA

ARCHITECTS



DAEDALUS

samiotes



ARCHITECTURAL
ENGINEERS

TRAVERSE
landscape architects

The Sharon Standing Building Committee

COLANTONIO
40 YEARS OF BUILDING RELATIONSHIPS

Weekly Activity Update

Friday June 28, 2019 Report #39

Current Week – Activities

- . Continue Septic Leech Field
- . As- Built Septic and Leech Field
- . Begin Gravel Fill – Leech Field
- . Rough Electric to Generator
- . Permanent Power
- . Continue Piping Roof Top Units
- . Install Mop Sinks
- . Water Chlorination Test
- . Continue Lighting Installation
- . Continue Ceiling Grid Installation – 1st
- . Core Holes for Floor Boxes – Meeting
- . Prime Exterior Lap Siding
- . Begin Security Camera Install
- . Receive Ceiling Tiles – 2nd Floor
- . Prep for Re-Grade of South Sidewalk
- . Layout for North Sidewalk
- . Test Lighting and Power
- . Install Alum. Door Frames
- . Wire and Run Heat Mesh to Transformer

Next Week – Activities

- . Continue Testing Lights and Power
- . Continue Lighting Install
- . Continue Aluminum Frame Install
- . Begin Carpet Floor Install
- . Install VCT and Linoleum
- . Install Vinyl Base
- . Begin Wood Ceiling
- . Continue Ceiling Grid – 1st Floor
- . Install Ceiling Tiles – 2nd Floor
- . Install Gas Line
- . Continue Ceiling Tile Install – 2nd Floor
- . Continue Ceiling Grid 1st Floor
- . Relocate Fencing North
- . Grade for South Sidewalk
- . Finish Paint Lap Siding
- . Continue Finish Paint – 1st Floor
- . Punch List Paint – 2nd Floor

Subcontractor	Trade	# of Workers Onsite
Color Concepts	Painting	02
Titan Contractors Inc.	Site Work	02
Carlysle	Fire Protection	02
Marmello	Masonry	00
Griffin Electric	Electrical	04
General Insulation	Insulator	00
Colantonio Inc.	Carpenter	04
United Site Services	Site Sanitary	01
Colony Drywall	Framing	00
Colantonio	Labor	01
LaPan Mechanical	Plumbing	02
Division 15	HVAC	07
Delta Beckwith	Elevator	00
Alum/Glass Concepts	Aluminum Openings	02
Greenwood	Roofing	00
Cheviot	Ceilings	01
Superior	Caulking	00
Capital Carpet	Tile	00
A.P. Dailey	Millwork	01
Mac Koul	Electric	04
BJA	Architect	02
Daedalus	Owner Representative	01
Colantonio Inc.	Construction Manager	03
TOTAL # Onsite This Week		39

Safety

- **Safety Orientation for New Jobsite Workers Performed First Day of Work. Total Number of Onsite Workers/Visitors Orientated = 130**
- **All Workers Wear Proper PPE At All Times**
- **Fencing and Scrim Reviewed Each Week for Safety and Appearance**
- **Weekly Toolbox Talks are Conducted Within Each Trade And a Copy is Submitted to Colantonio Inc.**
- **Each Contractor Completes a Daily Work Report which Is Kept On File**
- **Construction Progress Meeting are Held Tuesday at 1PM.**
- **224 Days With Zero Worker Accident**
- **224 Days Without a Lost Time Accident**

Quality Control


- **Materials Delivered To The Site Cross Referenced Against Drawings, Submittals and Specifications prior to installation.**
- **Colantonio Inc and Subcontractor Review of Drawings and Specification Compliance Prior to Work Commencing**
- **186 Random Quality Control Inspection Reports have been completed, of those: 02 remain as “Open” and “Non-Conforming”**

Miscellaneous


- **Colantonio Inc. subcontractor meeting held on Tuesdays at 11AM**
- **Columbia Gas Underground Service – 07/03/2019**
- **Primary Power to the Building**
- **Emergency Generator Relocation Complete**




Septic Leech Field

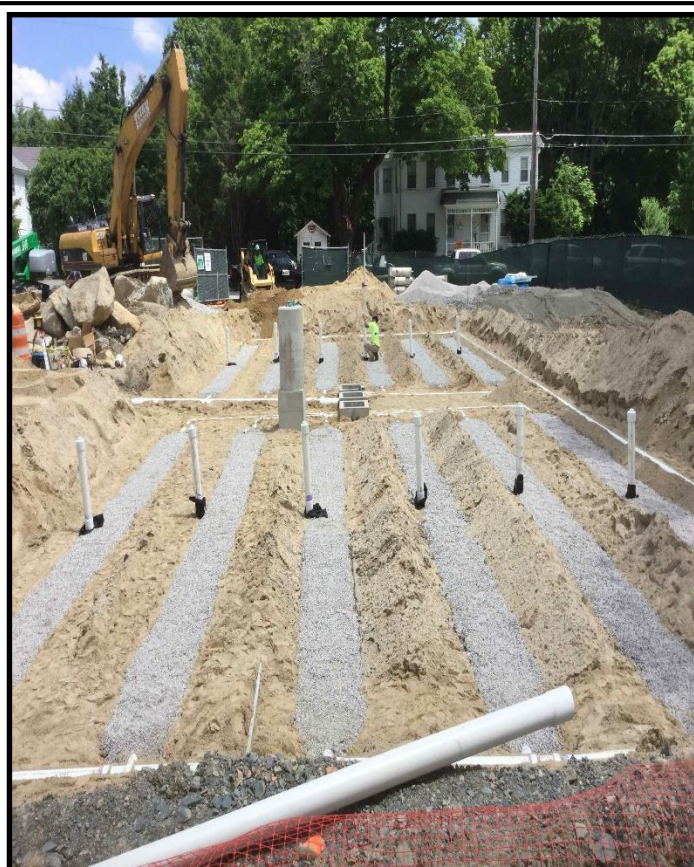

Septic Leech Field

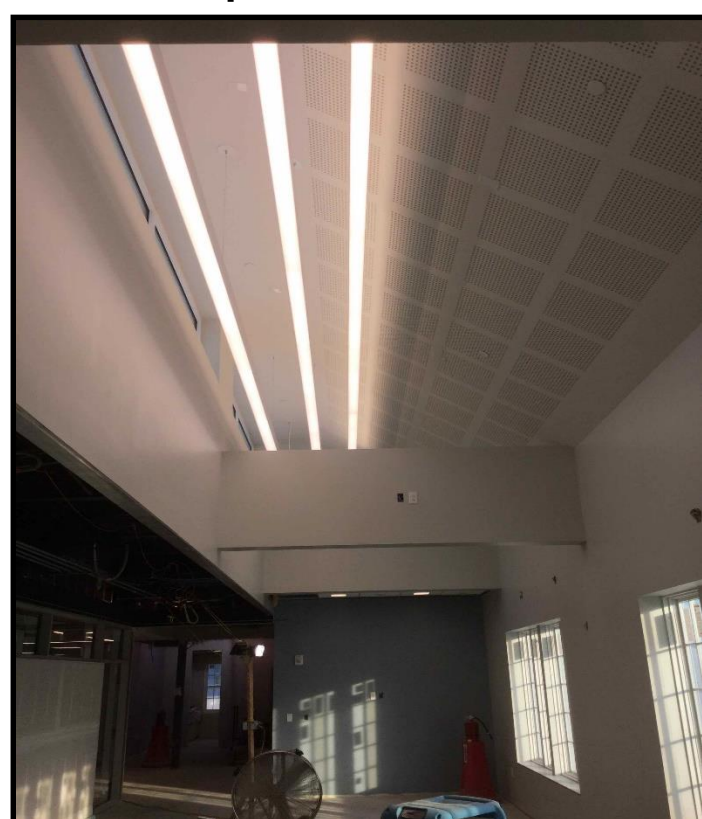

Meeting Room Lighting

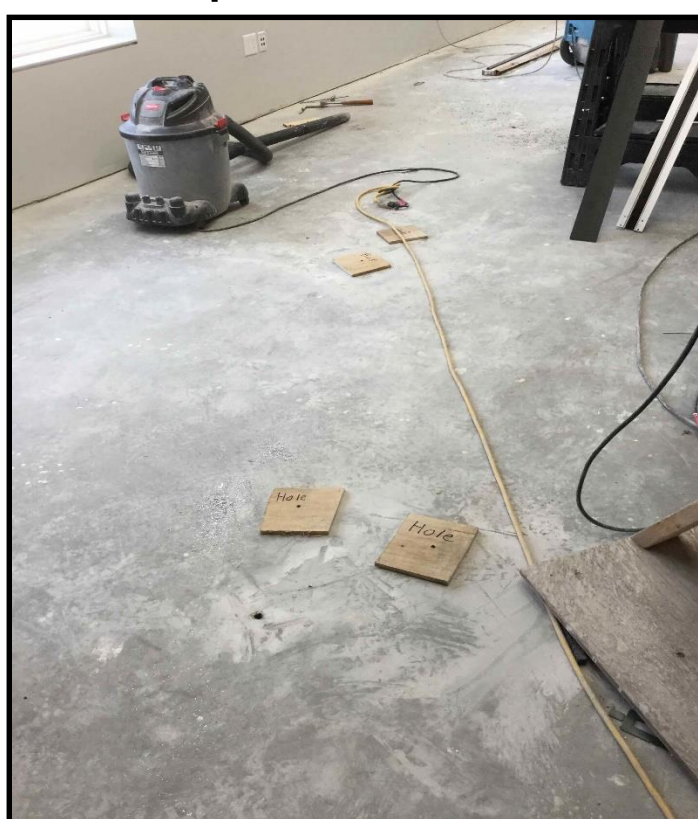

Meeting Room Cores



Moisture Testing



Network Room



Staff Room Millwork



AC Unit Electrical
