

# Sharon Town Hall Sharon, MA



**COLANTONIO INC.**  
**PROJECT # 18-3835**

**BKA**

ARCHITECTS



**DAEDALUS**

**samiotes**

ARCHITECTURAL  
**ENGINEERS**

**TRAVERSE**  
landscape architects

## The Sharon Standing Building Committee

**COLANTONIO**  
40 YEARS OF BUILDING RELATIONSHIPS

### Weekly Activity Update

Friday July 5, 2019 Report #40

#### Current Week – Activities

- . Backfill Septic Leech Field
- . Excavate and Install Gas Line
- . Prep North for Sidewalks/Planters
- . Haul Rocks and Asphalt Off Site
- . Relocate Fencing
- . Continue Ceiling Grid – 1<sup>st</sup> Floor
- . Begin Wood Ceiling – 2<sup>nd</sup> Floor
- . Begin Ceiling Tile Installation – 2<sup>nd</sup> Floor
- . Continue Lighting Installation – 1<sup>st</sup> Floor
- . Install Window Sills – 1<sup>st</sup> Floor
- . Continue Prime/Paint – Exterior
- . Continue Prime/Paint – Interior
- . Pipe and Wire Roof Top Units
- . Install Sprinkler Heads- 1<sup>st</sup> Floor
- . Install Aluminum Frames – 2<sup>nd</sup> Floor
- . Continue Lineset installation – 1<sup>st</sup> Floor
- . Commissioning Meeting

#### Next Week – Activities

- . Continue Testing Lights and Power
- . Continue Lighting -1<sup>st</sup> Floor
- . Continue Fire Alarm Rough
- . Install Ceiling Tiles – 2<sup>nd</sup> Floor
- . Begin Carpet installation- 2<sup>nd</sup> floor
- . Receive Lobby Floor Tile
- . Continue Aluminum Frames – 2<sup>nd</sup> Floor
- . Install Glass – 2<sup>nd</sup> Floor
- . Continue Ceiling Grid – 1<sup>st</sup> Floor
- . Install Lighting – 1<sup>st</sup> Floor
- . Above Ceiling Inspection – 1<sup>st</sup> Floor
- . Prep North/South Sidewalks
- . Begin Form North/South Sidewalks
- . Continue Gravel East Parking Lot

<b>Subcontractor</b>	<b>Trade</b>	<b># of Workers Onsite</b>
<b>Color Concepts</b>	<b>Painting</b>	<b>02</b>
<b>Titan Contractors Inc.</b>	<b>Site Work</b>	<b>02</b>
<b>Carlysle</b>	<b>Fire Protection</b>	<b>01</b>
<b>Marmello</b>	<b>Masonry</b>	<b>01</b>
<b>Griffin Electric</b>	<b>Electrical</b>	<b>04</b>
<b>General Insulation</b>	<b>Insulator</b>	<b>00</b>
<b>Colantonio Inc.</b>	<b>Carpenter</b>	<b>04</b>
<b>United Site Services</b>	<b>Site Sanitary</b>	<b>01</b>
<b>Colony Drywall</b>	<b>Framing</b>	<b>00</b>
<b>Colantonio</b>	<b>Labor</b>	<b>01</b>
<b>LaPan Mechanical</b>	<b>Plumbing</b>	<b>02</b>
<b>Division 15</b>	<b>HVAC</b>	<b>07</b>
<b>Delta Beckwith</b>	<b>Elevator</b>	<b>00</b>
<b>Alum/Glass Concepts</b>	<b>Aluminum Openings</b>	<b>02</b>
<b>Greenwood</b>	<b>Roofing</b>	<b>00</b>
<b>Cheviot</b>	<b>Ceilings</b>	<b>02</b>
<b>Superior</b>	<b>Caulking</b>	<b>00</b>
<b>Capital Carpet</b>	<b>Tile</b>	<b>00</b>
<b>A.P. Dailey</b>	<b>Millwork</b>	<b>01</b>
<b>BJA</b>	<b>Architect</b>	<b>02</b>
<b>Daedalus</b>	<b>Owner Representative</b>	<b>02</b>
<b>Colantonio Inc.</b>	<b>Construction Manager</b>	<b>03</b>
<b>TOTAL # Onsite This Week</b>		<b>37</b>

### **Safety**

- **Safety Orientation for New Jobsite Workers Performed First Day of Work. Total Number of Onsite Workers/Visitors Orientated = 134**
- **All Workers Wear Proper PPE At All Times**
- **Fencing and Scrim Reviewed Each Week for Safety and Appearance**
- **Weekly Toolbox Talks are Conducted Within Each Trade And a Copy is Submitted to Colantonio Inc.**
- **Each Contractor Completes a Daily Work Report which Is Kept On File**
- **Construction Progress Meeting are Held Tuesday at 1PM.**
- **228 Days With Zero Worker Accident**
- **228 Days Without a Lost Time Accident**

### **Quality Control**

- **Materials Delivered To The Site Cross Referenced Against Drawings, Submittals and Specifications prior to installation.**
- **Colantonio Inc and Subcontractor Review of Drawings and Specification Compliance Prior to Work Commencing**
- **194 Random Quality Control Inspection Reports have been completed, of those: 02 remain as “Open” and “Non-Conforming”**

### **Miscellaneous**

- **Colantonio Inc. subcontractor meeting held on Tuesdays at 11AM**
- **Columbia Gas Underground Service Installed – 07/03/2019**
- **Granite Paver Delivery – July 18<sup>th</sup>**
- **Commissioning Meeting Held July 2<sup>nd</sup>, 2019**






**Underground Gas Service**



**Gas Line Back Fill**



**Wood Ceiling Installation**

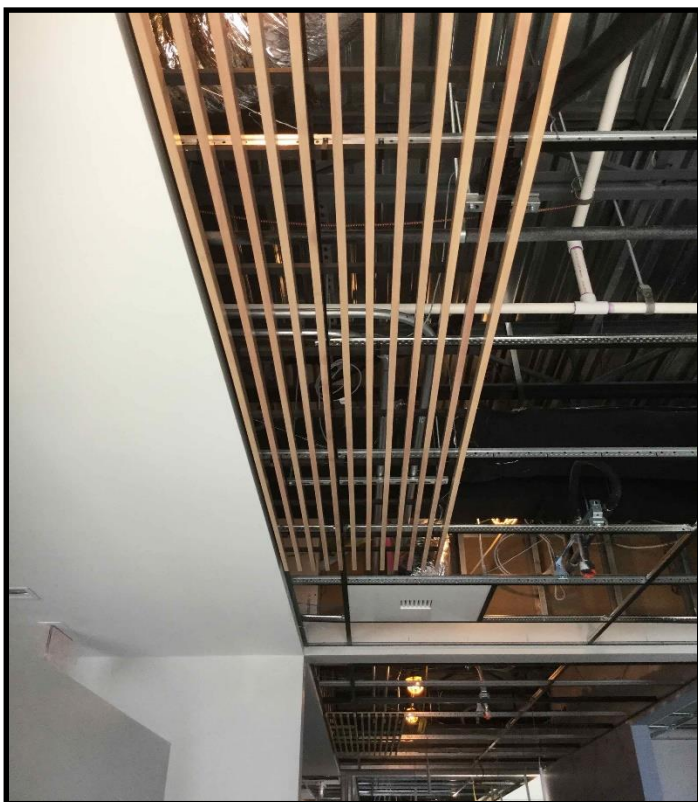

**Wood Ceiling Installation**





**West Elevation**



**Roof AC Unit Connections**



**Aluminum Frame Installation**



**Power Lockout/Tagout**
