

# Sharon Town Hall Sharon, MA



**COLANTONIO INC.**  
**PROJECT # 18-3835**

**BKA**

ARCHITECTS



**DAEDALUS**

**samiotes**

ARCHITECTURAL  
**ENGINEERS**

**TRAVERSE**  
landscape architects

## The Sharon Standing Building Committee

**COLANTONIO**  
40 YEARS OF BUILDING RELATIONSHIPS

### Weekly Activity Update

Saturday July 13, 2019 Report #41

#### Current Week – Activities

- . Prep Sidewalks
- . Form Sidewalks
- . Install Light Pole Bases
- . Install UG Conduit
- . Continue Paint of Trim and Siding
- . Install ACT Tiles – 2<sup>nd</sup> Floor
- . Install ACT Cuts – 1<sup>st</sup> Floor
- . 2<sup>nd</sup> Floor on Permanent Power
- . Install Elevator Exhaust
- . Continue Wood Ceiling – 2<sup>nd</sup> Floor
- . Install Registers – 1<sup>st</sup> Floor
- . Install Lobby Lighting – 1<sup>st</sup> Floor
- . Install Carpet tile – 2<sup>nd</sup> Floor
- . Install LVP – 2<sup>nd</sup> Floor
- . Install Base – 2<sup>nd</sup> Floor
- . Finish ACT Install – 2<sup>nd</sup> Floor
- . Finish Bathroom Tile
- . Load in Lobby Tile
- . Remove Temp Electric – 2<sup>nd</sup> Floor

#### Next Week – Activities

- . Continue Testing Lights and Power
- . Continue Fire Alarm Device Install
- . Place Sidewalk – South
- . Back Fill UGE for Site Lighting
- . Install Granite Curbing East
- . Gravel for Parking Lot
- . Install Lobby Tile
- . Received and Install Granite Pavers
- . Install VCT - 2<sup>nd</sup> Floor
- . Continue Wood Ceiling Installation
- . Install 1<sup>st</sup> Floor Millwork
- . Install ACT Cuts – 1<sup>st</sup> Floor
- . Paint Stairwell Walls and Railings
- . Install Gas Meter
- . Install Stairwell Light – Stair #2
- . Heat Pump Start Ups
- . Install Toilet Partitions
- . Install Aluminum Doors/Glass

<b>Subcontractor</b>	<b>Trade</b>	<b># of Workers Onsite</b>
<b>Color Concepts</b>	<b>Painting</b>	<b>02</b>
<b>Titan Contractors Inc.</b>	<b>Site Work</b>	<b>03</b>
<b>Carlysle</b>	<b>Fire Protection</b>	<b>00</b>
<b>Marmello</b>	<b>Masonry</b>	<b>02</b>
<b>Griffin Electric</b>	<b>Electrical</b>	<b>04</b>
<b>General Insulation</b>	<b>Insulator</b>	<b>02</b>
<b>Colantonio Inc.</b>	<b>Carpenter</b>	<b>04</b>
<b>United Site Services</b>	<b>Site Sanitary</b>	<b>01</b>
<b>Colony Drywall</b>	<b>Framing</b>	<b>01</b>
<b>Colantonio</b>	<b>Labor</b>	<b>01</b>
<b>LaPan Mechanical</b>	<b>Plumbing</b>	<b>00</b>
<b>Division 15</b>	<b>HVAC</b>	<b>07</b>
<b>Delta Beckwith</b>	<b>Elevator</b>	<b>01</b>
<b>Alum/Glass Concepts</b>	<b>Aluminum Openings</b>	<b>03</b>
<b>Greenwood</b>	<b>Roofing</b>	<b>00</b>
<b>Cheviot</b>	<b>Ceilings</b>	<b>03</b>
<b>Superior</b>	<b>Caulking</b>	<b>00</b>
<b>Capital Carpet</b>	<b>Tile</b>	<b>02</b>
<b>Pavilion Floor</b>	<b>Carpet Tile</b>	<b>02</b>
<b>Santangelo Floors</b>	<b>VCT/LVP/Base</b>	<b>03</b>
<b>BJA</b>	<b>Architect</b>	<b>02</b>
<b>Daedalus</b>	<b>Owner Representative</b>	<b>02</b>
<b>Colantonio Inc.</b>	<b>Construction Manager</b>	<b>03</b>
<b>TOTAL # Onsite This Week</b>		<b>48</b>

### **Safety**

- **Safety Orientation for New Jobsite Workers Performed First Day of Work. Total Number of Onsite Workers/Visitors Orientated = 136**
- **All Workers Wear Proper PPE At All Times**
- **Fencing and Scrim Reviewed Each Week for Safety and Appearance**
- **Weekly Toolbox Talks are Conducted Within Each Trade And a Copy is Submitted to Colantonio Inc.**
- **Each Contractor Completes a Daily Work Report which Is Kept On File**
- **Construction Progress Meeting are Held Tuesday at 1PM.**
- **234 Days With Zero Worker Accident**
- **234 Days Without a Lost Time Accident**

### **Quality Control**

- **Materials Delivered To The Site Cross Referenced Against Drawings, Submittals and Specifications prior to installation.**
- **Colantonio Inc and Subcontractor Review of Drawings and Specification Compliance Prior to Work Commencing**
- **199 Random Quality Control Inspection Reports have been completed, of those: 02 remain as “Open” and “Non-Conforming”**

### **Miscellaneous**

- **Colantonio Inc. subcontractor meeting held on Tuesdays at 11AM**
- **Columbia Gas Underground Service Installed – 07/03/2019**
- **Granite Paver Delivery – July 18<sup>th</sup>**
- **Security Camera Install and Adjust – Monday July15 9:30am**






**Wood Ceiling Installation**



**Wood Ceiling Installation**



**Staff Break Room**

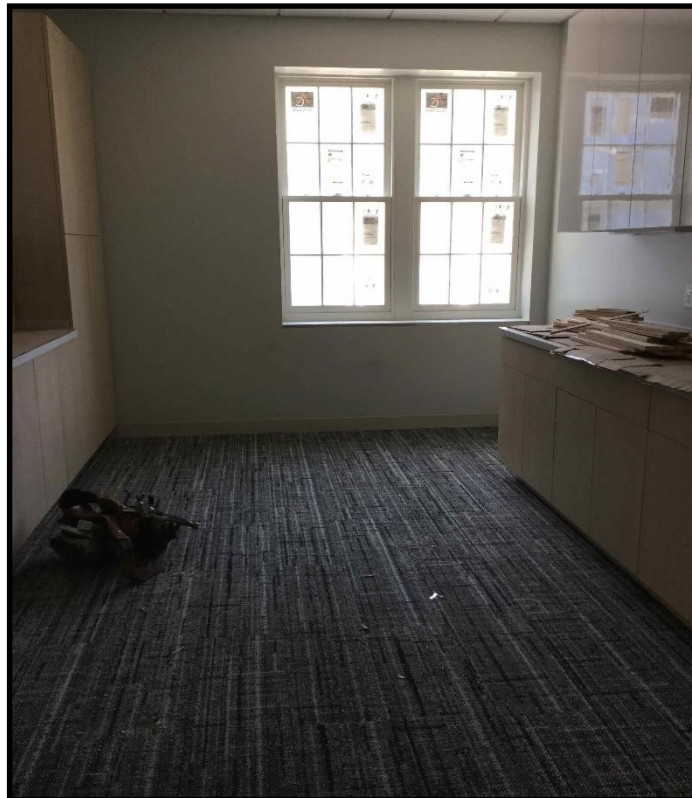

**Work Storage Office 210B**





**Carpet Installation**



**Carpet Installation**



**Elevator Exhaust Install**



**Washed Granite**
