

Sharon Town Hall Sharon, MA



COLANTONIO INC.
PROJECT # 18-3835

BKA

ARCHITECTS



DAEDALUS

samiotes

ARCHITECTURAL
ENGINEERS

TRAVERSE
landscape architects

The Sharon Standing Building Committee

COLANTONIO
40 YEARS OF BUILDING RELATIONSHIPS

Weekly Activity Update

Saturday July 20, 2019 Report #42

Current Week – Activities

- . Building on Permanent Power
- . Remove Temporary Wiring
- . Install Lighting 1st Floor
- . Test Electrical Devices – 1st Floor
- . Continue Fire Alarm Device Install
- . Complete Duct work
- . Continue Testing and Balancing
- . Install Carpet – 2nd Floor
- . Install Lobby Tile
- . Install Generator Transfer Switch
- . Install 1st Floor Mill work
- . Install Doors and Glass – 2nd Floor
- . Install Lobby Linear Diffusers
- . Install Wood Ceiling – 2nd Floor
- . Install Granite Pavers
- . Continue Parking Lot Grading
- . Excavate for Granite Curbing – East

Next Week – Activities

- . Fire Alarm Testing
- . Install Rubber Base – 2nd Floor
- . Install Carpet Flooring – 1st Floor
- . Grout Lobby Tile
- . Install Hall Tile – 1st Floor
- . Complete Wood Ceiling – 2nd Floor
- . Install Wood Ceiling – 1st Floor
- . Install Ceiling Tiles -1st Floor
- . Install Gas Meter
- . Install Granite Pavers
- . Install Granite Curbing – East
- . Continue Parking Lot Grading
- . Place East Sidewalk
- . Complete Elevator and Test
- . Continue Testing and Balancing
- . Mitsubishi Commissioning

Subcontractor	Trade	# of Workers Onsite
Color Concepts	Painting	01
Titan Contractors Inc.	Site Work	02
Carlysle	Fire Protection	01
Labidini	Landscape	02
Griffin Electric	Electrical	05
General Insulation	Insulator	00
Colantonio Inc.	Carpenter	05
United Site Services	Site Sanitary	01
Colony Drywall	Framing	00
Colantonio	Labor	01
LaPan Mechanical	Plumbing	01
Division 15	HVAC	05
Delta Beckwith	Elevator	00
Alum/Glass Concepts	Aluminum Openings	03
Greenwood	Roofing	00
Cheviot	Ceilings	01
Superior	Caulking	00
Capital Carpet	Tile	02
Pavilion Floor	Carpet Tile	02
Santangelo Floors	VCT/LVP/Base	02
BKA	Architect	02
Daedalus	Owner Representative	02
Colantonio Inc.	Construction Manager	03
TOTAL # Onsite This Week		41

Safety

- Safety Orientation for New Jobsite Workers Performed First Day of Work. Total Number of Onsite Workers/Visitors Orientated = 136
- All Workers Wear Proper PPE At All Times
- Fencing and Scrim Reviewed Each Week for Safety and Appearance
- Weekly Toolbox Talks are Conducted Within Each Trade And a Copy is Submitted to Colantonio Inc.
- Each Contractor Completes a Daily Work Report which Is Kept On File
- Construction Progress Meeting are Held Tuesday at 1PM.
- 240 Days With Zero Worker Accident
- 240 Days Without a Lost Time Accident

Quality Control

- Materials Delivered To The Site Cross Referenced Against Drawings, Submittals and Specifications prior to installation.
- Colantonio Inc and Subcontractor Review of Drawings and Specification Compliance Prior to Work Commencing
- 210 Random Quality Control Inspection Reports have been completed, of those: 01 remain as “Open” and “Non-Conforming”

Miscellaneous

- Colantonio Inc. subcontractor meeting held on Tuesdays at 11AM
- Columbia Gas Meter Install - TBD
- Entrance Door and Frame Delivery – July 25, 2019
- Granite Curbing Delivery – July 22, 2019




Floor Lobby Tile



Toilet Partition



Millwork Install

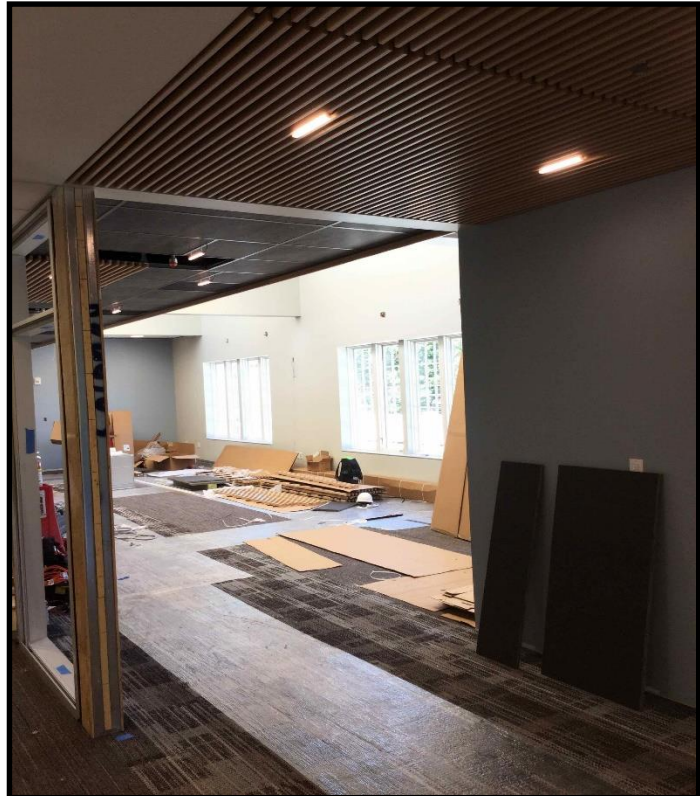

Meeting Room



2nd Floor Hallway



Aluminum Frame Installation



Staff Break Room



Site Grading
