

Sharon Town Hall Sharon, MA



COLANTONIO INC.
PROJECT # 18-3835

BJA

ARCHITECTS



DAEDALUS

samiotes



ARCHITECTURAL
ENGINEERS

TRAVERSE
landscape architects

The Sharon Standing Building Committee

COLANTONIO
40 YEARS OF BUILDING RELATIONSHIPS

Weekly Activity Update

Saturday July 27, 2019 Report #43

Current Week – Activities

- . Complete 1st Floor Tile Floor
- . Install Ceiling Tiles – 1st Floor
- . Begin Wood Ceiling – 1st Floor
- . Complete Wood Ceiling – 2nd Floor
- . Install Rubber Base – 2nd Floor
- . Test Fire Sprinkler Fire Alarm Switches
- . Pre-Test Fire Alarm
- . Install Clerk Office Cabinets
- . Install Collector's Office Cabinets
- . Install Assessors Office Cabinets
- . Adjust Coiling Doors
- . Template for Quartz Counter Tops
- . Receive Additional Aluminum Frames
- . Set Granite East Sidewalk
- . Install Underground Irrigation Sleeves
- . Paint Canopy Ceiling South – 1st Coat
- . Finish Granite Pavers – Porch
- . Sub Grade Parking Lot

Next Week – Activities

- . Fine Grade Parking Lot Area
- . Install Asphalt Binder Coat
- . Form and Place East Sidewalk
- . Install Granite Curbing
- . Pull Electric and Set Light Poles
- . Install Aluminum Frames and Glass
- . Receive and Install Wood Panels – 2nd Floor
- . Install Window Shades
- . 2nd Floor Pre-Punch List
- . Install Ceiling Tiles
- . Install Carpet Flooring
- . Install Entrance Mats
- . Install Lobby Frame and Doors
- . Adjust Elevator and Pre-Test
- . Continue Paint Canopy Ceilings
- . Prep for Plantings

Subcontractor	Trade	# of Workers Onsite
Color Concepts	Painting	01
Titan Contractors Inc.	Site Work	05
Carlysle	Fire Protection	02
Labidini	Landscape	03
Griffin Electric	Electrical	05
General Insulation	Insulator	00
Colantonio Inc.	Carpenter	04
United Site Services	Site Sanitary	01
Colony Drywall	Framing	01
Colantonio	Labor	01
LaPan Mechanical	Plumbing	02
Division 15	HVAC	05
Delta Beckwith	Elevator	01
Alum/Glass Concepts	Aluminum Openings	03
Greenwood	Roofing	00
Cheviot	Ceilings	02
Superior	Caulking	02
Capital Carpet	Tile	03
Pavilion Floor	Carpet Tile	02
Santangelo Floors	VCT/LVP/Base	02
BJA	Architect	02
Daedalus	Owner Representative	02
Colantonio Inc.	Construction Manager	03
TOTAL # Onsite This Week		51

Safety

- Safety Orientation for New Jobsite Workers Performed First Day of Work. Total Number of Onsite Workers/Visitors Orientated = 138
- All Workers Wear Proper PPE At All Times
- Fencing and Scrim Reviewed Each Week for Safety and Appearance
- Weekly Toolbox Talks are Conducted Within Each Trade And a Copy is Submitted to Colantonio Inc.
- Each Contractor Completes a Daily Work Report which Is Kept On File
- Construction Progress Meeting are Held Tuesday at 1PM.
- 246 Days With Zero Worker Accident
- 244 Days Without a Lost Time Accident

Quality Control


- Materials Delivered To The Site Cross Referenced Against Drawings, Submittals and Specifications prior to installation.
- Colantonio Inc and Subcontractor Review of Drawings and Specification Compliance Prior to Work Commencing
- 210 Random Quality Control Inspection Reports have been completed, of those: 00 remain as “Open” and “Non-Conforming”

Miscellaneous

- Colantonio Inc. subcontractor meeting held on Tuesdays at 11AM
- Columbia Gas Meter Install - TBD
- Generator Load Test – Tentative August 5th, 2019
- Asphalt Binder Date: Tuesday July 30, 2019



Install Granite Curbing

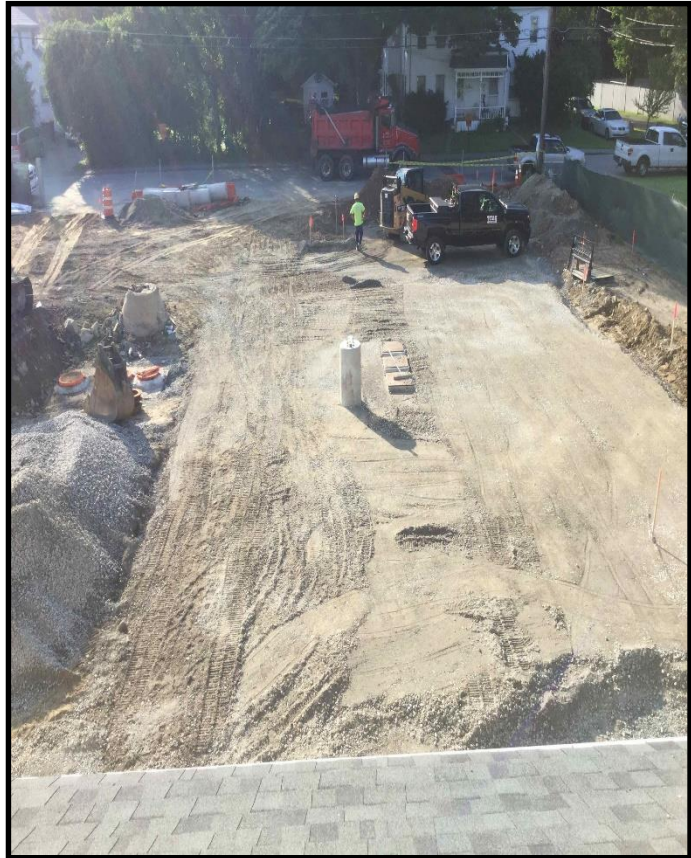

Parking Lot Subgrade



Granite Paver Install



South Canopy Ceiling



Assessor's Millwork



1st Floor Hall Tile



Lobby Ceiling



Elevator Cab Controls
