

Sharon Town Hall Sharon, MA



COLANTONIO INC.
PROJECT # 18-3835

BKA

ARCHITECTS



samiotes

ARCHITECTURAL
ENGINEERS

TRAVERSE
landscape architects

The Sharon Standing Building Committee



Weekly Activity Update

Sunday August 18, 2019 Report #46

Current Week – Activities

- . Install Vault Shelving
- . Install Stair #1 Carpet
- . Install Bathroom Mirrors
- . Paint Vestibule
- . Paint Exterior Columns and Railings
- . Program Lighting Controls
- . Generator Start Up and Testing
- . Set Final Camera Views
- . Continue Wood Panel Install 2nd Floor
- . Install Angled Frame and Glass
- . Install Quartz Counter Tops
- . Install Transaction Frames and Glass
- . Install Plantings, Loam and Mulch
- . Remove Office Trailers
- . Strip and Wax Floors
- . Clean Glass, Bathrooms and Vacuum
- . Install Water Bubblers

Next Week – Activities

- . Final Plumbing Inspection
- . State Inspection of Elevator
- . Complete Parking Lot Binder
- . Install Vestibule Frame and Mat
- . Install Vestibule Tile
- . Touch up Paint
- . Caulk Frames and Sidewalks
- . Clean and Vacuum
- . File Cabinet Delivery
- . Begin 1st Floor Wood Panels
- . Install Glass Film
- . Install Entrance Door Controllers
- . Relocate Fencing
- . Begin Phase III Drainage

Subcontractor	Trade	# of Workers Onsite
Color Concepts	Painting	01
Titan Contractors Inc.	Site Work	01
Carlysle	Fire Protection	02
Labidini	Landscape	03
Griffin Electric	Electrical	05
Montes	Counter Tops	02
Colantonio Inc.	Carpenter	04
United Site Services	Site Sanitary	01
Colony Drywall	Framing	02
Colantonio	Labor	01
LaPan Mechanical	Plumbing	01
Division 15	HVAC	01
Delta Beckwith	Elevator	01
Alum/Glass Concepts	Aluminum Openings	04
Santangelo	Flooring	01
Cheviot	Ceilings	01
Superior	Caulking	00
Capital Carpet	Tile	00
Pavilion Floor	Carpet Tile	01
Donnegan Systems	Shelving	03
BJA	Architect	02
Daedalus	Owner Representative	03
Colantonio Inc.	Construction Manager	03
TOTAL # Onsite This Week		42

Safety

- **Safety Orientation for New Jobsite Workers Performed First Day of Work. Total Number of Onsite Workers/Visitors Orientated = 143**
- **All Workers Wear Proper PPE At All Times**
- **Fencing and Scrim Reviewed Each Week for Safety and Appearance**
- **Weekly Toolbox Talks are Conducted Within Each Trade And a Copy is Submitted to Colantonio Inc.**
- **Each Contractor Completes a Daily Work Report which Is Kept On File**
- **Construction Progress Meeting are Held Tuesday at 1PM.**
- **267 Days With Zero Worker Accident**
- **267 Days Without a Lost Time Accident**

Quality Control

- **Materials Delivered To The Site Cross Referenced Against Drawings, Submittals and Specifications prior to installation.**
- **Colantonio Inc and Subcontractor Review of Drawings and Specification Compliance Prior to Work Commencing**
- **218 Random Quality Control Inspection Reports have been completed, of those: 01 remain as “Open” and “Non-Conforming”**

Miscellaneous

- **Colantonio Inc. subcontractor meeting held on Tuesdays at 11AM**
- **State Inspection of Elevator – August 20, 2019**
- **Final Plumbing Inspection – August 19, 2019**
- **Phase 3 Fence Relocation – August 22, 2019**



Staff Break Room



Meeting Room Wall Panels



Vault Shelving




Transaction Frame / Glass




Central Storage



Bradford Ave. Entrance

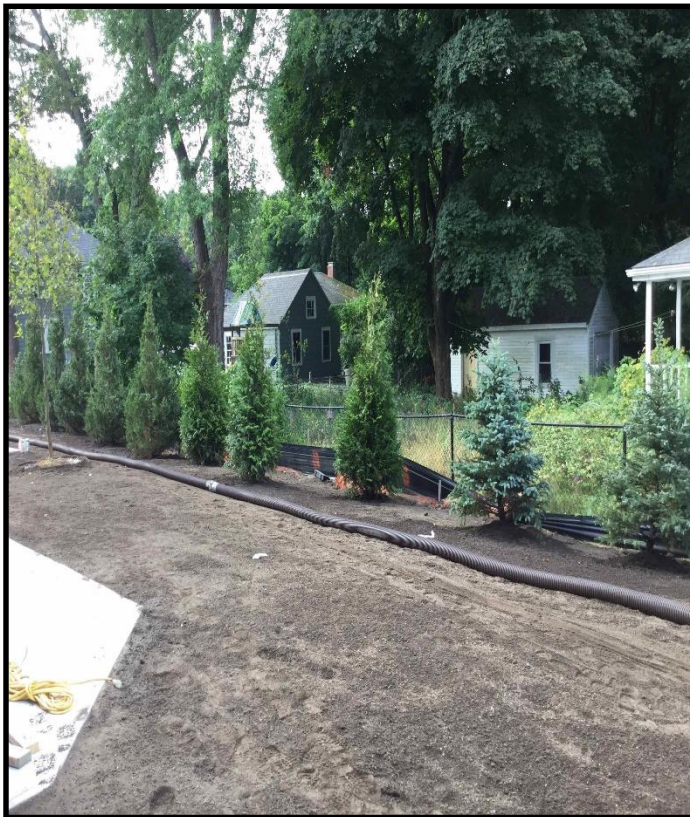

South Landscape

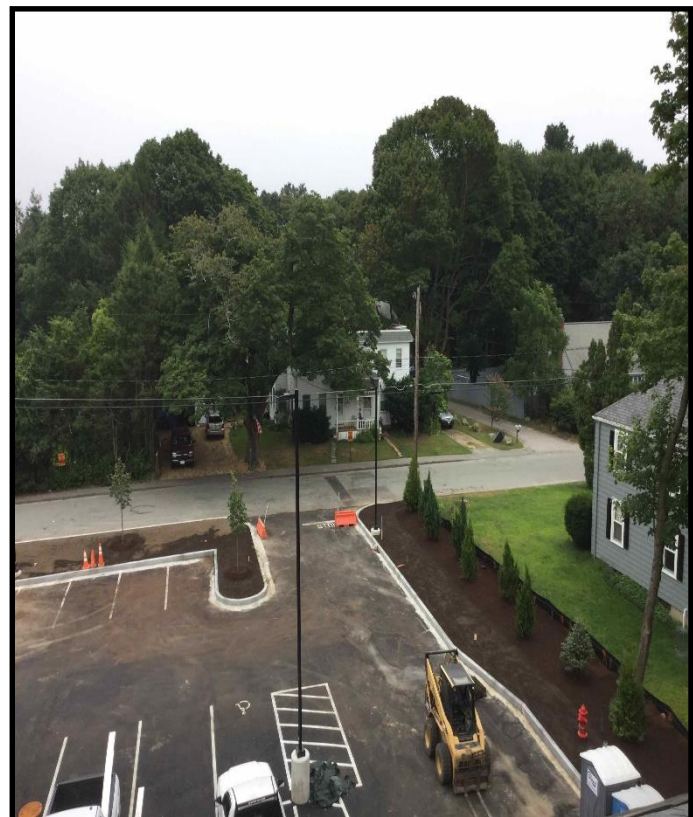

Bradford Ave. Entrance
