

Sharon Town Hall Sharon, MA



COLANTONIO INC.
PROJECT # 18-3835

BAK

ARCHITECTS



samiotes

ARCHITECTURAL
ENGINEERS

TRAVERSE
landscape architects

The Sharon Standing Building Committee



Weekly Activity Update

Saturday August 31, 2019 Report #48

Current Week – Activities

- . Delivery and Install of Furniture
- . Installation of Media Wall
- . Sharon TV Install
- . Complete Wall Panels
- . Install Phase 3 Fencing
- . Punch List
- . Temp Certificate of Occupancy

Next Week – Activities

- . Continue Punch List
- . Continue Phase 3 Set Up
- . Install Permanent Door Locks
- . Furniture Relocation
- . Clear and Grub Phase 3
- . Saw Cut for Phase 3 Utility Disconnect

Subcontractor	Trade	# of Workers Onsite
Color Concepts	Painting	01
Titan Contractors Inc.	Site Work	00
Carlysle	Fire Protection	00
Labidini	Landscape	02
Griffin Electric	Electrical	02
Montes	Counter Tops	00
Colantonio Inc.	Carpenter	03
United Site Services	Site Sanitary	01
Colony Drywall	Framing	00
Colantonio	Labor	01
LaPan Mechanical	Plumbing	01
Division 15	HVAC	01
Delta Beckwith	Elevator	00
Alum/Glass Concepts	Aluminum Openings	00
Santangelo	Flooring	00
Cheviot	Ceilings	00
Superior	Caulking	00
Capital Carpet	Tile	02
Pavilion Floor	Carpet Tile	01
BJA	Architect	02
Daedalus	Owner Representative	03
Colantonio Inc.	Construction Manager	03
TOTAL # Onsite This Week		23

Safety


- **Safety Orientation for New Jobsite Workers Performed First Day of Work. Total Number of Onsite Workers/Visitors Orientated = 143**
- **All Workers Wear Proper PPE At All Times**
- **Fencing and Scrim Reviewed Each Week for Safety and Appearance**
- **Weekly Toolbox Talks are Conducted Within Each Trade And a Copy is Submitted to Colantonio Inc.**
- **Each Contractor Completes a Daily Work Report which Is Kept On File**
- **Construction Progress Meeting are Held Tuesday at 1PM.**
- **278 Days With Zero Worker Accident**
- **278 Days Without a Lost Time Accident**

Quality Control

- **Materials Delivered To The Site Cross Referenced Against Drawings, Submittals and Specifications prior to installation.**
- **Colantonio Inc and Subcontractor Review of Drawings and Specification Compliance Prior to Work Commencing**
- **220 Random Quality Control Inspection Reports have been completed, of those: 04 remain as “Open” and “Non-Conforming”**

Miscellaneous

- **WB Mason Furniture Delivery and Install**
- **Workstation And Cabinet Delivery**
- **Occupancy Walk Through with Building Department**
- **Phase 3 Scheduled to Commence September 10, 2019**

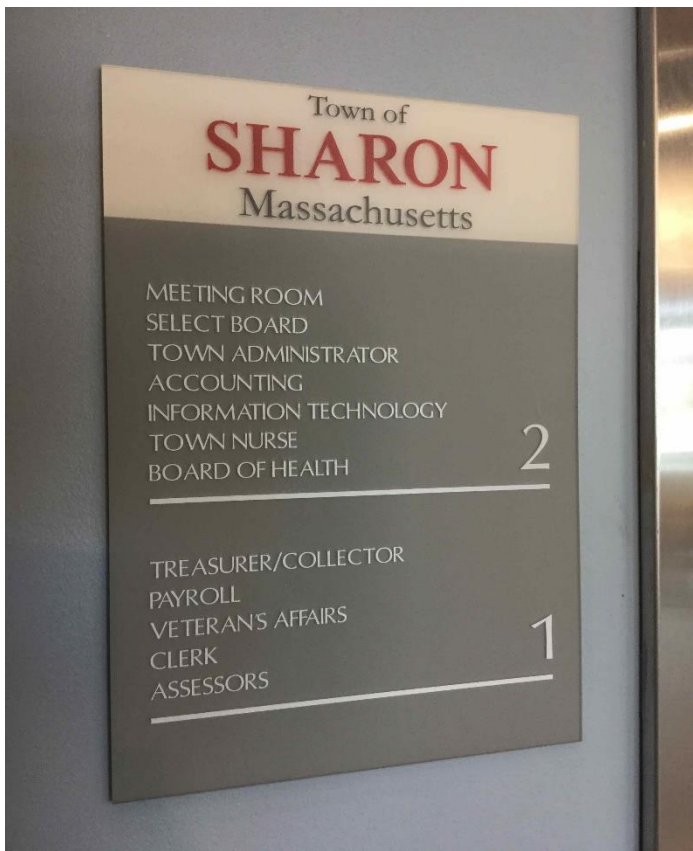

New Directory Board



2nd Floor Hall



New Office Space



Town Hall Lobby




Main Stair



New meeting Room



South Landscape

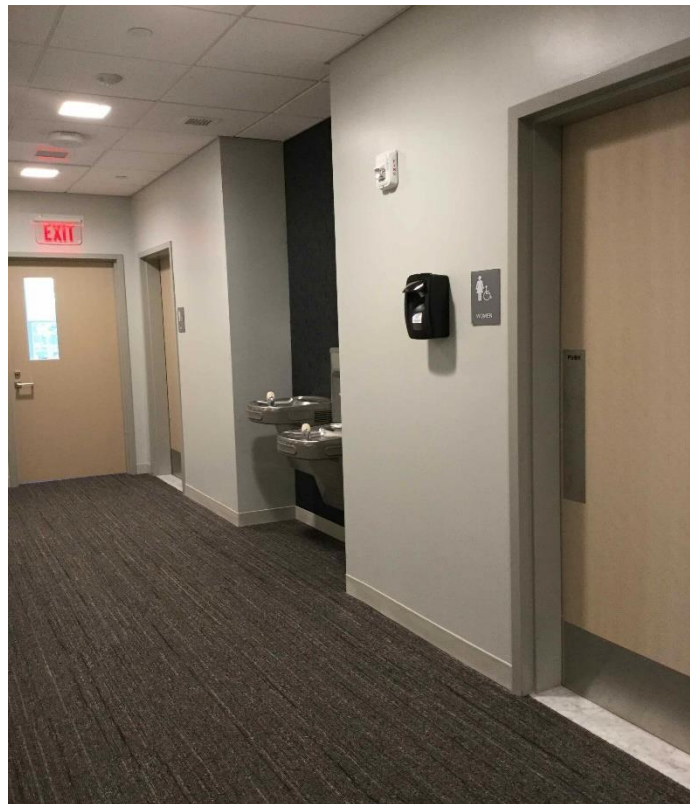

1st Floor Hall
