

Sharon Town Hall Sharon, MA



COLANTONIO INC.
PROJECT # 18-3835

BJA

ARCHITECTS



samiotes

ARCHITECTURAL
ENGINEERS

TRAVERSE
landscape architects

The Sharon Standing Building Committee



Weekly Activity Update

Friday October 11, 2019 Report #52

Current Week – Activities

- . Complete OTH Abatement
- . Complete OTH Demolition and Removal
- . Install Cedar Fencing
- . Slope Depression – OTH Basement
- . Verification of Gutter Guard Usage

Next Week – Activities

- . Install Door Film New Town Hall
- . Begin East Chestnut Street Drainage
- . Infill OTH Depression
- . Excavate for Site Bollards
- . Final Grade Entrance Sidewalk
- . Install Flagpole Sleeve
- . Install ESB Sonotubes

Subcontractor	Trade	# of Workers Onsite
Color Concepts	Painting	00
Titan Contractors	Site	03
JR Vinagro	Abatement	03
Universal	Testing	01
Griffin Electric	Date/Electric	01
Aluminum Glass	Glass and Frames	00
Division 15	HVAC	01
Colantonio	Labor	00
J.R. Vinagro	Demolition	04
Labidini	Landscaping	03
BKA	Architect	02
Daedalus	Owner Representative	03
Colantonio Inc.	Construction Manager	03
TOTAL # Onsite This Week		24

Safety

- **Safety Orientation for New Jobsite Workers Performed First Day of Work. Total Number of Onsite Workers/Visitors Orientated = 161**
- **All Workers Wear Proper PPE At All Times**
- **Fencing and Scrim Reviewed Each Week for Safety and Appearance**
- **Weekly Toolbox Talks are Conducted Within Each Trade And a Copy is Submitted to Colantonio Inc.**
- **Each Contractor Completes a Daily Work Report which Is Kept On File**
- **Construction Progress Meeting are Held Tuesday at 1PM.**
- **308 Days With Zero Worker Accident**
- **308 Days Without a Lost Time Accident**

Quality Control


- **Materials Delivered To The Site Cross Referenced Against Drawings, Submittals and Specifications prior to installation.**
- **Colantonio Inc and Subcontractor Review of Drawings and Specification Compliance Prior to Work Commencing**
- **228 Random Quality Control Inspection Reports have been completed, of those: 00 remain as “Open” and “Non-Conforming”**

Miscellaneous

- **New Drainage Structures/Pipe Scheduled for October 14, 2019**
- **Old Town Hall Demolition 100% complete**
- **Labadini to Replace 2 plantings from Phase 2**



OTH Demolition

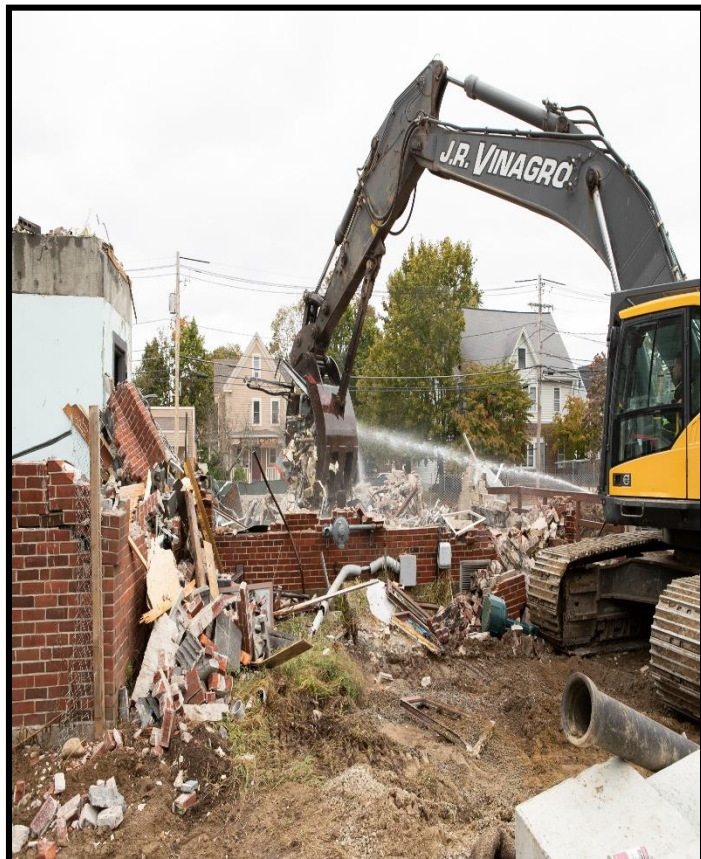


OTH Demolition




OTH Demolition



Sidewalk Placement

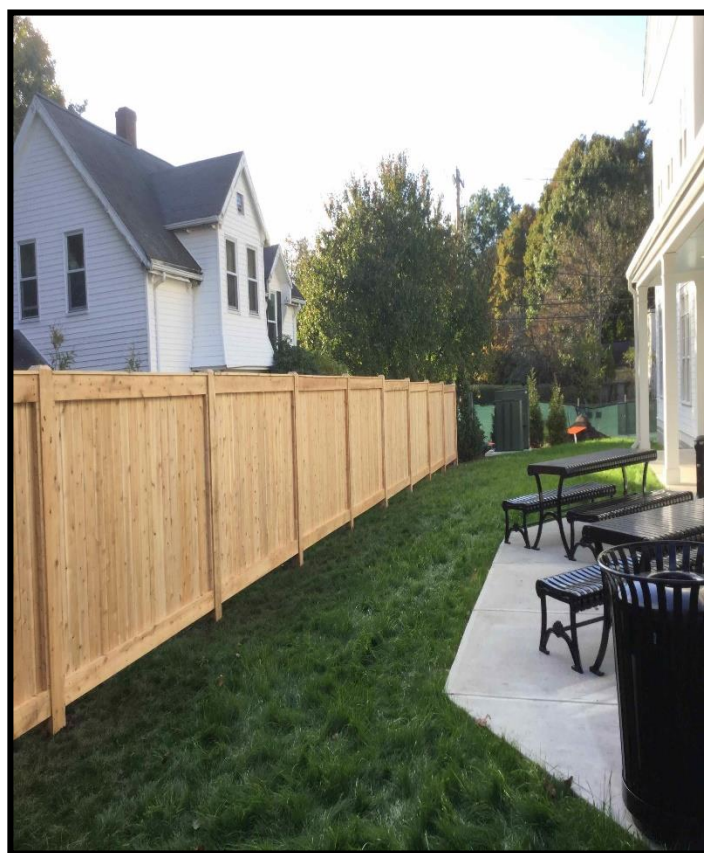

Fence Installation

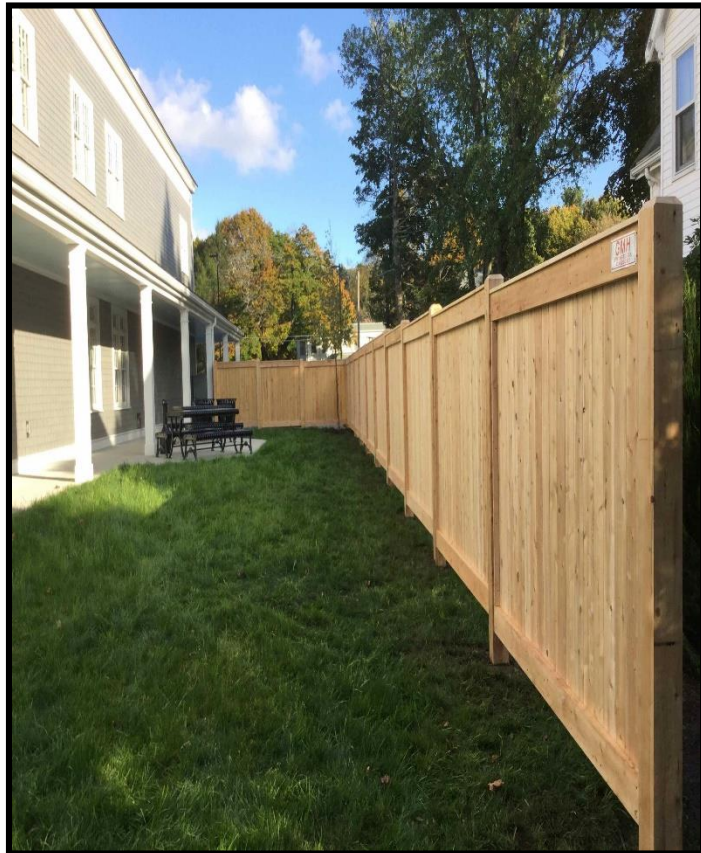

Fence Installation



Basement Sloping



Sidewalk Prep
