

Sharon Town Hall Sharon, MA



COLANTONIO INC.
PROJECT # 18-3835

BAK

ARCHITECTS



samiotes

ARCHITECTURAL
ENGINEERS

TRAVERSE
landscape architects

The Sharon Standing Building Committee



Weekly Activity Update

Saturday October 26, 2019 Report #54

Current Week – Activities

- . Install Door Film New Town Hall
- . Excavate for UGE Conduit
- . Install Site Bollard Bases
- . Backfill and Sub grade West
- . Strip South Main Street Forms
- . Install and Place Concrete for Flagpole
- . Continue Site Drainage
- . Prep Entrance Sidewalks
- . Install Granite Curbing
- . Install Plantings West and Northwest
- . Install Loam and Seed West
- . Relocate South Main Street Fencing
- . Install Select Board Door Hardware
- . Deliver Plantings

Next Week – Activities

- . Remove Fencing East Chestnut Street
- . Subgrade Parking Lot for Asphalt Binder
- . Prep Entrance Sidewalks
- . Prep for Granite Bench Supports
- . West Elevation Landscaping
- . Install of EMB Granite Bollards
- . Install Granite Curbing
- . Pull Wiring for Site Lighting
- . Install Flagpole

Subcontractor	Trade	# of Workers Onsite
Reed Associates	Surveying	02
Titan Contractors	Site	05
Briggs	Testing	01
Federal	Concrete	02
Aluminum Glass	Glass Partitions	01
Griffin Electric	Electrical	02
Labadini	Landscaping	01
GMH Fence	Cedar Fence	01
BJA	Architect	02
Daedalus	Owner Representative	03
Colantonio Inc.	Construction Manager	03
TOTAL # Onsite This Week		23

Safety

- **Safety Orientation for New Jobsite Workers Performed First Day of Work. Total Number of Onsite Workers/Visitors Orientated = 161**
- **All Workers Wear Proper PPE At All Times**
- **Fencing and Scrim Reviewed Each Week for Safety and Appearance**
- **Weekly Toolbox Talks are Conducted Within Each Trade And a Copy is Submitted to Colantonio Inc.**
- **Each Contractor Completes a Daily Work Report which Is Kept On File**
- **Construction Progress Meeting are Held Tuesday at 1PM.**
- **319 Days With Zero Worker Accident**
- **319 Days Without a Lost Time Accident**

Quality Control

- **Materials Delivered To The Site Cross Referenced Against Drawings, Submittals and Specifications prior to installation.**
- **Colantonio Inc and Subcontractor Review of Drawings and Specification Compliance Prior to Work Commencing**
- **234 Random Quality Control Inspection Reports have been completed, of those: 02 remain as “Open” and “Non-Conforming”**

Miscellaneous


- **Fencing To Be Removed Along East Chestnut**
- **Site Prep for Asphalt Binder Course October 31, 2019**



Set and Form Flagpole Sleeve



UGE Installation

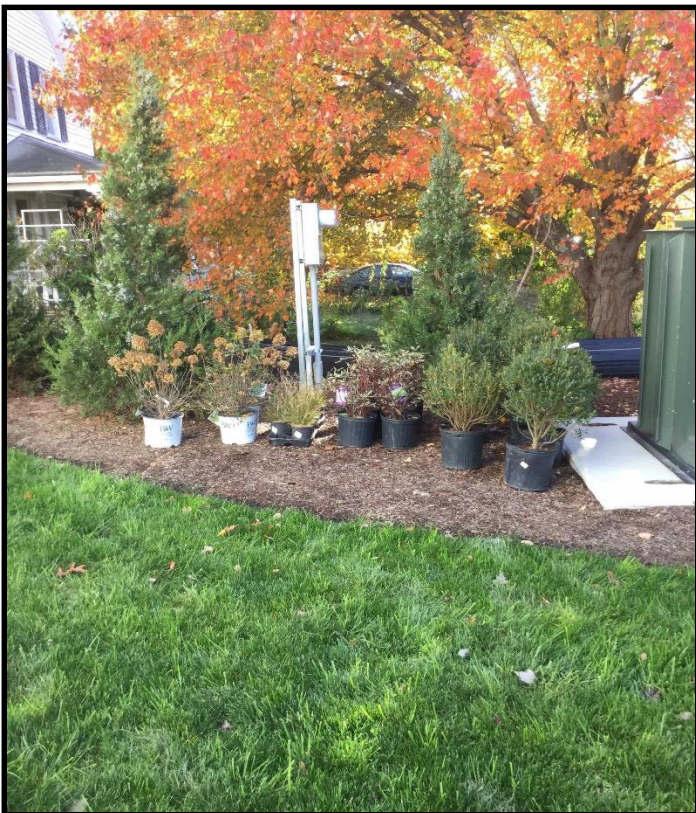

Delivery of West Plantings



Form and rebar for Flagpole
