

# Sharon Town Hall

## Sharon, MA



**COLANTONIO INC.**  
**PROJECT # 18-3835**



Weekly Activity Update

Friday October 05, 2018 Report #05

---

### **Current Week – Activities**

- . Install Temporary Electric to Trailers
- . Excavate for Footings
- . Install Structural Fill for Footing Subgrade
- . Install Temporary Septic Man Hole
- . Install Temporary Septic Piping
- . Make Safe and Remove Light Pole
- . Install 4' Gate for Town Hall Access
- . Strip Loam and Asphalt
- . Testing of Structural Fill Subgrade
- . DPW Meeting for Temp. Septic Work
- . Pin Center of Column A Line

### **Next Week – Activities**

- . Continue Footing Excavation
- . Continue Subgrade Testing
- . Backfill Septic Man Hole
- . Receive Form Material and Rebar
- . Form A Line Footings
- . For 1 Line and 8 Line Footings
- . Haul Loam, Stone and Stumps Off Site
- . Load in Structural Fill
- . Continue Strip Loam and Curb
- . Receive Anchor Bolts

Subcontractor	Trade	# of Workers Onsite
Briggs Engineering	Soil Testing	01
Titan Contractors Inc.	Site Work	03
Wood and Wire	Fencing	02
Federal Concrete	Foundations	02
Piquette & Howard	Electrical	02
Glen Reed Assoc.	Surveyor	02
Daedalus	Owner Representative	01
Colantonio Inc.	Construction Manager	01
TOTAL # Onsite This Week		14

**Safety**

- Safety Orientation for New Jobsite Workers Performed First Day of Work. Total Number of Onsite Workers/Visitors Trained = 19
- All Workers Wear 100% Hard Hats and Reflective Clothing.
- Colantonio Inc. Site Specific Safety Officer on Site Full Time.
- Weekly Toolbox Talks are Conducted Within Each Trade And a Copy is Submitted to Colantonio Inc. and kept on File.
- Each Contractor Completes a Daily Work Safety Plan of Action which Is Kept On File On Site.
- Construction Progress Meeting are Held Tuesday at 1PM.
- Fence Damaged by Moving Vehicle. Report Filed with Sharon Police.
- 24 Days With Zero Worker Accident
- 24 Days Without a Lost Time Accident

**Quality Control**

- Materials Delivered To The Site Cross Referenced Against Drawings, Submittals and Specifications.
- Colantonio Inc and Subcontractor Review of Drawings and Specification Compliance Prior to Work Commencing
- 14 Random Quality Control Inspection Reports have been completed, of those: 1 remain as "Open" and "Non-Conforming"

**Miscellaneous**

- Temp Power Complete and Awaiting Town Inspection
- Temporary Reroute of Existing Sanitary Complete
- Titan and Colantonio Inc. On Site Monday October 8<sup>th</sup>





**Temporary Electric**



**Strip Asphalt and Loam**



**Excavate for Footings**



**Structural Fill Subgrade**






**Temporary Sanitary Line**



**Temporary Sanitary Line**

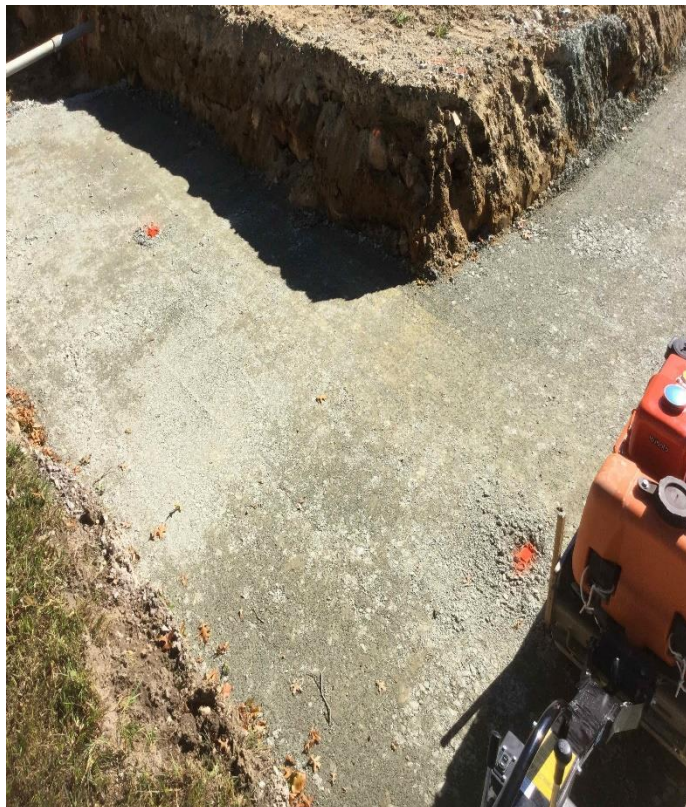

**Center of Column Layout**



**Light Pole for Salvage**
