

# Sharon Town Hall

## Sharon, MA



**COLANTONIO INC.**  
**PROJECT # 18-3835**

BJA

ARCHITECTS



samiotes

ARCHITECTURAL  
ENGINEERS

TRAVERSE  
landscape architects

# Standing Building Committee



Weekly Activity Update

Friday October 26, 2018 Report #08

## Current Week – Activities

- . Strip Foundation Walls
- . Receive Foundation Insulation
- . Backfill Footings and Foundation Walls
- . Compaction Testing
- . On Site Meeting with Steel Fabricator
- . Excavate for Interior Piers
- . Form Footings 1 and 0.5 Line
- . Rebar and Concrete Testing
- . Place 1 and 0.5 Footings
- . Form Footings K Line and 1 Line
- . Form Foundation Walls 1 Line and 0.5 Line
- . Set Steel Bearing Plates
- . Continue UG Water and Fire Protection
- . Inspect and Backfill Water Lines
- . Place Foundation Walls 1 and 0.5 Line
- . Install MEP Sleeves
- . Stone Bradford Avenue Entrance

## Next Week – Activities

- . Strip Foundation Walls 1 and 0.5 Line
- . Continue Bearing Plate Install
- . Backfill Footing and Foundation Walls
- . Excavate F1 Footings 8.1 Line
- . Excavate for Elevator Pit
- . Form and Place F1 Footings
- . Form Elevator Pit Slab and Sump
- . Form and Place Interior Piers
- . Continue MEP Sleeve Install
- . Excavate Footing K1 Line
- . Form and Place K1 Footing
- . On Site Meeting with Steel Erector
- . On Site Meeting with Plumbing Sub
- . Continue Slab Subgrade

<b>Subcontractor</b>	<b>Trade</b>	<b># of Workers Onsite</b>
<b>Briggs Engineering</b>	<b>Soil Testing</b>	<b>02</b>
<b>Titan Contractors Inc.</b>	<b>Site Work</b>	<b>03</b>
<b>Briggs</b>	<b>Concrete/Steel Insp.</b>	<b>02</b>
<b>Federal Concrete</b>	<b>Foundations</b>	<b>07</b>
<b>Griffin Electric</b>	<b>Electrical</b>	<b>01</b>
<b>TriMax</b>	<b>Steel Fabricator</b>	<b>01</b>
<b>S.M. Lorusso</b>	<b>Structural Fill</b>	<b>02</b>
<b>United Site Services</b>	<b>Site Sanitary</b>	<b>01</b>
<b>BKA</b>	<b>Architect</b>	<b>02</b>
<b>Daedalus</b>	<b>Owner Representative</b>	<b>03</b>
<b>Colantonio Inc.</b>	<b>Construction Manager</b>	<b>03</b>
<b>TOTAL # Onsite This Week</b>		<b>27</b>

### Safety

- Safety Orientation for New Jobsite Workers Performed First Day of Work. Total Number of Onsite Workers/Visitors Trained = 33
- All Workers Wear 100% Hard Hats and Reflective Clothing.
- Colantonio Inc. Site Specific Safety Officer on Site Full Time.
- Temporary Fence Panels Blew over During Saturday Night Wind Gusts. Fencing corrected Sunday Morning.
- Weekly Toolbox Talks are Conducted Within Each Trade And a Copy is Submitted to Colantonio Inc.
- Each Contractor Completes a Daily Work Report which Is Kept On File
- Construction Progress Meeting are Held Tuesday at 1PM.
- 40 Days With Zero Worker Accident
- 40 Days Without a Lost Time Accident

### Quality Control

- Materials Delivered To The Site Cross Referenced Against Drawings, Submittals and Specifications prior to installation.
- Colantonio Inc and Subcontractor Review of Drawings and Specification Compliance Prior to Work Commencing
- 40 Random Quality Control Inspection Reports have been completed, of those: 2 remain as "Open" and "Non-Conforming"


### Miscellaneous

- Additional Unknown Soils Stored On Site in locked Container.
- Fire Department Lock Box Replaced at South Main Street Gate
- No Parking During Construction Time Posted on Bradford Avenue
- Report of Damaged Fence on Bradford. 2 Steel Posts to be Re-set.





**Sub Grade Testing**

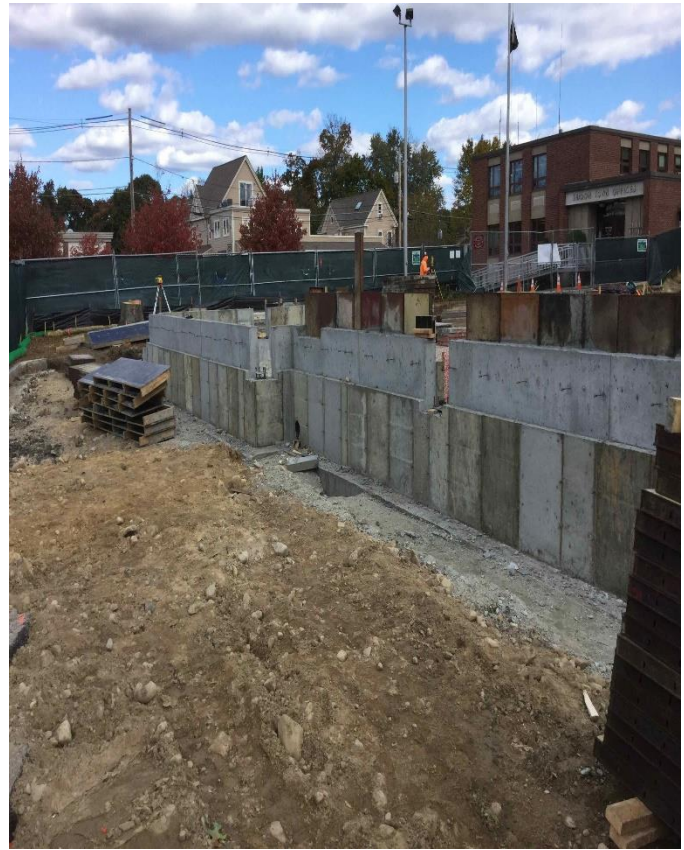

**Strip Foundation Wall**



**Back Fill Foundation Wall**



**Backfill Footings**





**UG Water and Fire Protection**



**Interior Pier Rebar**



**Foundation Placement**



**Weather Protection**
