

Sharon Town Hall

Sharon, MA



COLANTONIO INC.
PROJECT # 18-3835

BKA

ARCHITECTS



DAEDALUS

samiotes



ARCHITECTURAL
ENGINEERS

TRAVERSE
landscape architects

The Sharon Standing Building Committee

COLANTONIO
40 YEARS OF BUILDING RELATIONSHIPS

Weekly Activity Update Saturday November 03, 2018 Report #09

Current Week – Activities

- . Strip Foundation Wall
- . Strip Interior Piers
- . Place Foundation Wall 1 Line and .5 Line
- . Place Foundation Wall 1 Line and K Line
- . Form Elevator Pit
- . Install Rebar for Elevator Pit and Walls
- . Place Elevator Pit
- . Continue Building Slab Sub Grade
- . Prep Haunches for Fire Vaults
- . Backfill Foundation Walls 1 Line
- . Backfill Entry Vestibule
- . Install Rain Leader and Piping
- . Install MEP Sleeves
- . Receive Structural Fill
- . Receive Stone Sub Base

Next Week – Activities

- . Form and Place Elevator Walls
- . Form and Place K.1 Footings
- . Install Underground Electric
- . Install Underground Plumbing
- . Grout Bearing Plates
- . Continue Slab Sub Grade Prep
- . Pre-Slab Pour Conference
- . Fencing Repair and Relocation
- . Place K.1 Footing
- . Receive 1" Insulation
- . Receive Vapor Retarder
- . Receive Slab Reinforcing
- . Receive Structural Fill
- . Receive Stone Base
- . Strip Elevator Pit Walls

Weekly Activity Update Saturday November 03,2018 Report #09

Subcontractor	Trade	# of Workers Onsite
Briggs Engineering	Soil Testing	02
Titan Contractors Inc.	Site Work	03
Briggs	Concrete/Steel Insp.	02
Federal Concrete	Foundations	07
Griffin Electric	Electrical	01
G.P East Steel	Steel Erector	03
S.M. Lorusso	Structural Fill	02
United Site Services	Site Sanitary	01
LaPan Mechanical	Plumbing	02
Dynamic	Dumpster	01
Tresca	Concrete	4
BKA	Architect	02
Daedalus	Owner Representative	03
Colantonio Inc.	Construction Manager	03
TOTAL # Onsite This Week		36

Safety

- Safety Orientation for New Jobsite Workers Performed First Day of Work. Total Number of Onsite Workers/Visitors Orientated = 36
- All Workers Wear 100% Hard Hats and Reflective Clothing.
- Colantonio Inc. Site Specific Safety Officer on Site Full Time.
- Stone Laid Down at Bradford St. Entrance for Tracking
- Weekly Toolbox Talks are Conducted Within Each Trade And a Copy is Submitted to Colantonio Inc.
- Each Contractor Completes a Daily Work Report which Is Kept On File
- Construction Progress Meeting are Held Tuesday at 1PM.
- 46 Days With Zero Worker Accident
- 46 Days Without a Lost Time Accident

Quality Control

- Materials Delivered To The Site Cross Referenced Against Drawings, Submittals and Specifications prior to installation.
- Colantonio Inc and Subcontractor Review of Drawings and Specification Compliance Prior to Work Commencing
- 48 Random Quality Control Inspection Reports have been completed, of those: 3 remain as “Open” and “Non-Conforming”

Miscellaneous

- Additional Unknown Soils Stored On Site in locked Container.
- No Parking During Construction Time Posted on Bradford Avenue
- Pre-Steel Erection Meeting Being Scheduled
- Briggs On Site for Concrete, Compaction and Rebar inspections



Foundation Wall Back Fill



Prep For Foundation Forms




Entrance Foundation Wall



Entrance Insulation



Prep for Concrete Slab

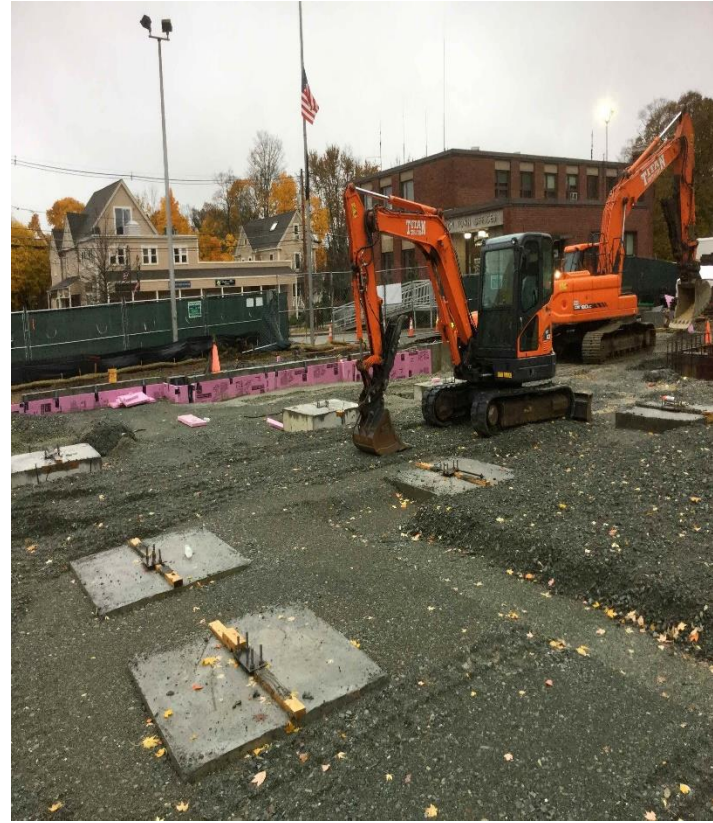

Interior Piers and Haunch



Concrete Placement



Back Fill Entrance Area
