

Sharon Town Hall

Sharon, MA



COLANTONIO INC.
PROJECT # 18-3835

BKA

ARCHITECTS



DAEDALUS

samiotes



ARCHITECTURAL
ENGINEERS

TRAVERSE
landscape architects

The Sharon Standing Building Committee

COLANTONIO
40 YEARS OF BUILDING RELATIONSHIPS

Weekly Activity Update Saturday November 10, 2018 Report #10

Current Week – Activities

- . Strip Foundation Walls
- . Place K line Footings
- . Install Underground Electric Piping
- . Install Roof Drains
- . Form K.1 Line Foundation Walls
- . Test Compaction, Rebar and Concrete
- . Place K.1 Foundation Walls
- . Install Bearing Plates
- . Backfill Building Pad
- . Backfill 1 line and 0.5 Line
- . Receive Slab Membrane and Insulation
- . Place 8.1 Piers
- . Backfill K line Foundation Wall
- . Bring Water/Fire Protection into Building
- . Wiring and Plumbing Inspection
- . Water Division Inspection
- . Strip K.1 Line Foundation Walls
- . Pre-Slab Conference

Next Week – Activities

- . Install Underground Plumbing
- . Continue Underground Electric
- . Backfill Building Sub Grade
- . Install Slab Membrane and Insulation
- . Install Column Box Outs
- . Install Slab Reinforcement
- . Place Building Slab – 1st Floor
- . Finish Building Slab – 1st Floor
- . Excavate for Permanent Power
- . Install Secondaries and Concrete
- . Excavate for Primary Conduit
- . Install Primary Conduits
- . Pre-Steel Erection Conference
- . Anchor Bolt Survey

Weekly Activity Update Saturday November 10,2018 Report #10

Subcontractor	Trade	# of Workers Onsite
Briggs Engineering	Soil Testing	01
Titan Contractors Inc.	Site Work	04
Briggs	Concrete/Steel Insp.	02
Federal Concrete	Foundations	07
Griffin Electric	Electrical	03
G.P East Steel	Steel Erector	01
S.M. Lorusso	Structural Fill	02
United Site Services	Site Sanitary	01
LaPan Mechanical	Plumbing	02
Dynamic	Dumpster	01
Tresca	Concrete	4
RSE	Structural Engineer	01
BKA	Architect	02
Daedalus	Owner Representative	02
Colantonio Inc.	Construction Manager	03
TOTAL # Onsite This Week		36

Safety

- Safety Orientation for New Jobsite Workers Performed First Day of Work. Total Number of Onsite Workers/Visitors Orientated = 38
- All Workers Wear 100% Hard Hats and Reflective Clothing.
- Colantonio Inc. Site Specific Safety Officer on Site Full Time.
- Stone Laid Down at Bradford St. Entrance for Tracking
- Weekly Toolbox Talks are Conducted Within Each Trade And a Copy is Submitted to Colantonio Inc.
- Each Contractor Completes a Daily Work Report which Is Kept On File
- Construction Progress Meeting are Held Tuesday at 1PM.
- 52 Days With Zero Worker Accident
- 52 Days Without a Lost Time Accident

Quality Control

- Materials Delivered To The Site Cross Referenced Against Drawings, Submittals and Specifications prior to installation.
- Colantonio Inc and Subcontractor Review of Drawings and Specification Compliance Prior to Work Commencing
- 54 Random Quality Control Inspection Reports have been completed, of those: 2 remain as “Open” and “Non-Conforming”

Miscellaneous

- Additional Unknown Soils Stored On Site in locked Container.
- No Parking During Construction Time Posted on Bradford Avenue
- Pre-Steel Erection Meeting Scheduled for Tuesday Nov. 13th
- Briggs On Site for Concrete, Compaction and Rebar inspections




Elevator Pit and Sump Pit



Domestic and Fire Piping




Building Slab Prep

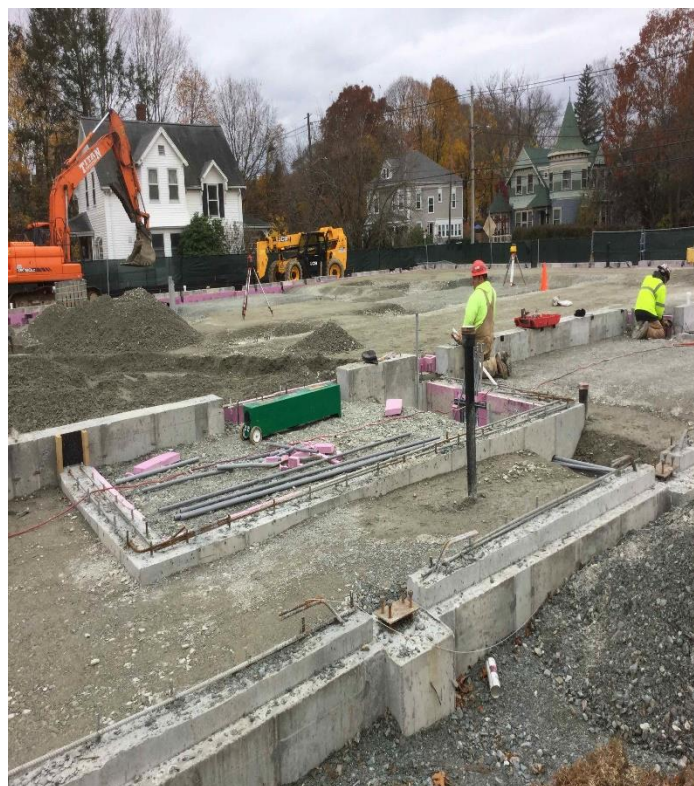

Entrance Underground Install



Main Electric Underground

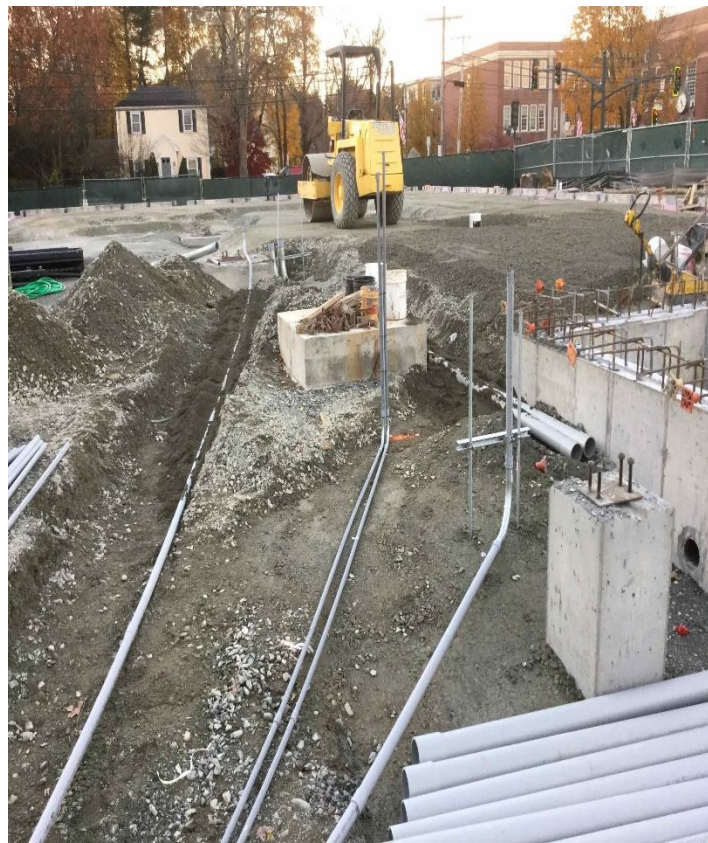

Under Slab Feeders



Foundation Wall Forms



Exterior Piers
