

# Sharon Town Hall

## Sharon, MA



**COLANTONIO INC.**  
**PROJECT # 18-3835**

**BKA**

ARCHITECTS



**DAEDALUS**

**samiotes**



ARCHITECTURAL  
**ENGINEERS**

**TRAVERSE**  
landscape architects

## The Sharon Standing Building Committee

**COLANTONIO**  
40 YEARS OF BUILDING RELATIONSHIPS

Weekly Activity Update      Friday November 16, 2018 Report #11

---

### Current Week – Activities

- . Install Underground Plumbing
- . Continue Underground Electric
- . Backfill Building Sub Grade
- . Install Slab Membrane and Insulation
- . Install Column Box Outs
- . Install Slab Reinforcement
- . Anchor Bolt and Plate Survey
- . Excavate for Permanent Power
- . Install Secondaries and Concrete
- . Pre-Steel Erection Conference
- . Underground Plumbing Installation
- . Underground Plumbing Inspection
- . Underground Electric Installation
- . Underground Electric Inspection
- . Pre-Steel Erection Conference

### Next Week – Activities

- . Backfill Electric Duct Bank
- . Receive Steel Joists
- . Install Slab Membrane
- . Install Slab Reinforcement
- . 1<sup>st</sup> Floor Slab Placement
- . 1<sup>st</sup> Floor Slab Finishing
- . Give Thanks

Subcontractor	Trade	# of Workers Onsite
Briggs Engineering	Soil Testing	01
Titan Contractors Inc.	Site Work	04
Reed Land Surveying	Engineering	02
Federal Concrete	Foundations	07
Griffin Electric	Electrical	03
G.P East Steel	Steel Erector	01
S.M. Lorusso	Structural Fill	02
United Site Services	Site Sanitary	01
LaPan Mechanical	Plumbing	02
Dynamic	Dumpster	0
Tresca	Concrete	1
GP East Steel	Structural Steel	02
Colantonio	Carpenter	01
BKA	Architect	02
Daedalus	Owner Representative	02
Colantonio Inc.	Construction Manager	03
TOTAL # Onsite This Week		34

### Safety

- Safety Orientation for New Jobsite Workers Performed First Day of Work. Total Number of Onsite Workers/Visitors Orientated = 40
- All Workers Wear 100% Hard Hats and Reflective Clothing.
- Colantonio Inc. Site Specific Safety Officer on Site Full Time.
- Stone Laid Down at Bradford St. Entrance for Tracking
- Weekly Toolbox Talks are Conducted Within Each Trade And a Copy is Submitted to Colantonio Inc.
- Each Contractor Completes a Daily Work Report which Is Kept On File
- Construction Progress Meeting are Held Tuesday at 1PM.
- 57 Days With Zero Worker Accident
- 57 Days Without a Lost Time Accident

### Quality Control

- Materials Delivered To The Site Cross Referenced Against Drawings, Submittals and Specifications prior to installation.
- Colantonio Inc and Subcontractor Review of Drawings and Specification Compliance Prior to Work Commencing
- 61 Random Quality Control Inspection Reports have been completed, of those: 1 remain as “Open” and “Non-Conforming”

### Miscellaneous

- Additional Unknown Soils Stored On Site in locked Container.
- No Parking During Construction Time Posted on Bradford Avenue
- Pre-Steel Erection Meeting Concluded on Tuesday Nov. 13<sup>th</sup>
- Briggs On Site for Concrete, Compaction and Rebar inspections





**Secondary Conduit**



**Electrical Duct Bank**




**Vapor Barrier Install**




**Slab Reinforcement Install**



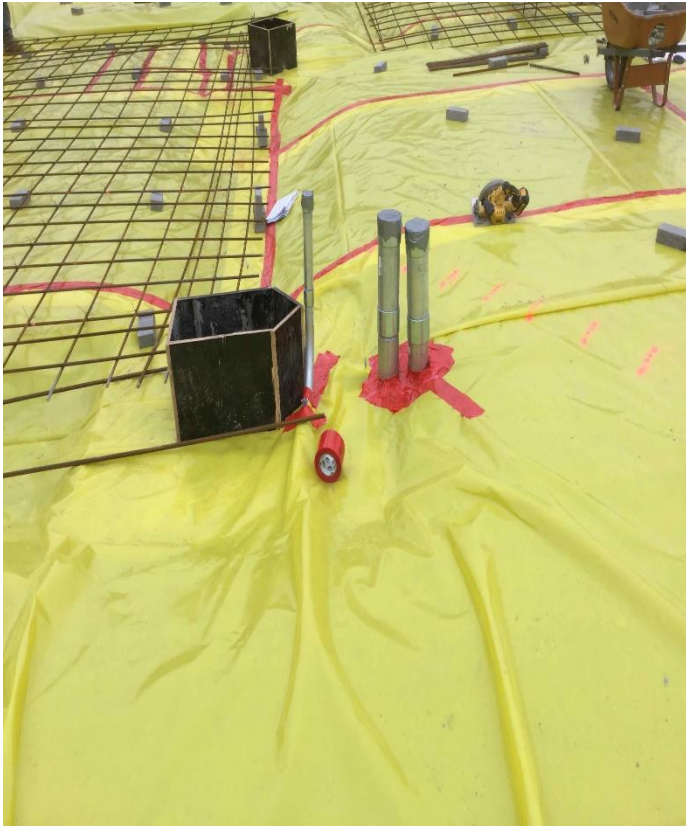

**Under Slab Electric**

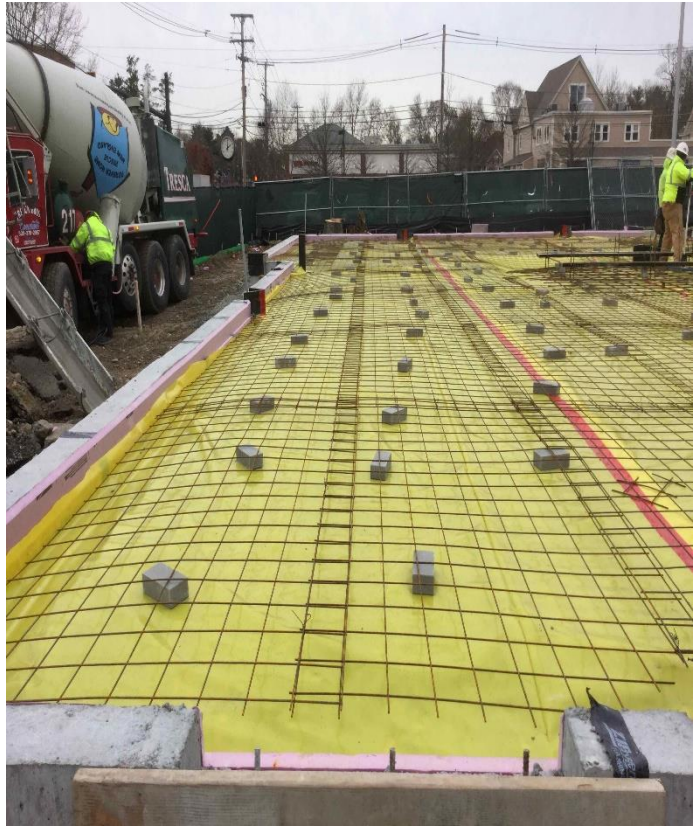

**Slab Reinforcement**



**Roof Drain Piping**



**Underground Plumbing**
