

Sharon Town Hall Sharon, MA



COLANTONIO INC.
PROJECT # 18-3835

BKA

ARCHITECTS



DAEDALUS

samiotes



ARCHITECTURAL
ENGINEERS

TRAVERSE
landscape architects

The Sharon Standing Building Committee

COLANTONIO
40 YEARS OF BUILDING RELATIONSHIPS

Weekly Activity Update Friday December 07, 2018 Report #14

Current Week – Activities

- . Shake Out Steel
- . Receive Sequence 3
- . Begin Steel Erection
- . Build Temp Electric Dog house
- . Investigate Temp Electric Routing
- . Install Stone Road – West Side

Next Week – Activities

- . Continue Sequence 2 Steel
- . Begin Sequence 3 Steel
- . Begin Roof Deck Installation
- . Field Measure Exterior Framing

Subcontractor	Trade	# of Workers Onsite
Briggs Engineering	Soil Testing	00
Titan Contractors Inc.	Site Work	01
Reed Land Surveying	Engineering	00
Federal Concrete	Foundations	02
Griffin Electric	Electrical	01
G.P East Steel	Steel Erector	05
Colantonio Inc.	Carpenter	01
United Site Services	Site Sanitary	01
Police	Detail	01
BJA	Architect	02
Daedalus	Owner Representative	01
Colantonio Inc.	Construction Manager	03
TOTAL # Onsite This Week		18

Safety

- Safety Orientation for New Jobsite Workers Performed First Day of Work. Total Number of Onsite Workers/Visitors Orientated = 57
- All Workers Wear 100% Hard Hats and Reflective Clothing.
- Fencing and Scrim Reviewed Each Week for Safety and Appearance
- Stone Road Created on West Side for Access
- Weekly Toolbox Talks are Conducted Within Each Trade And a Copy is Submitted to Colantonio Inc.
- Each Contractor Completes a Daily Work Report which Is Kept On File
- Construction Progress Meeting are Held Tuesday at 1PM.
- 72 Days With Zero Worker Accident
- 72 Days Without a Lost Time Accident

Quality Control

- Materials Delivered To The Site Cross Referenced Against Drawings, Submittals and Specifications prior to installation.
- Colantonio Inc and Subcontractor Review of Drawings and Specification Compliance Prior to Work Commencing
- 75 Random Quality Control Inspection Reports have been completed, of those: 1 remain as “Open” and “Non-Conforming”

Miscellaneous

- No Parking During Construction Time Posted on Bradford Avenue
- 1st Floor Slab Placement Completed. FF/FL – 36/27



Shake Out Steel



Steel Grouping




Shake Out Steel



Shake Out Steel



Column Erection – Seq. 1

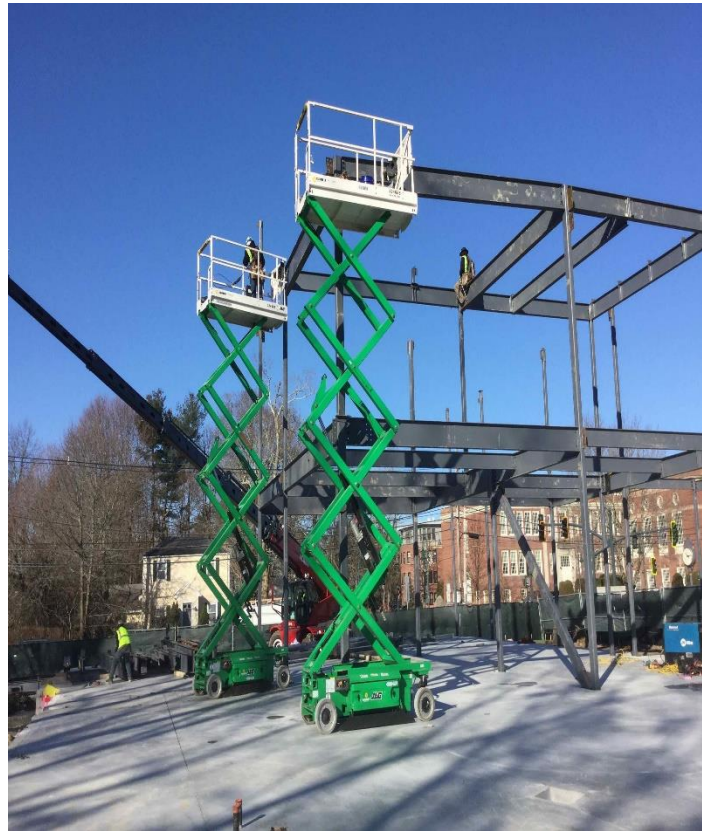

Sequence 1 Columns and Beams



Sequence 1 Steel Erection



Sequence 1 Steel Erection
