

Sharon Town Hall Sharon, MA



COLANTONIO INC.
PROJECT # 18-3835

BKA

ARCHITECTS



DAEDALUS

samiotes



ARCHITECTURAL
ENGINEERS

TRAVERSE
landscape architects

The Sharon Standing Building Committee

COLANTONIO
40 YEARS OF BUILDING RELATIONSHIPS

Weekly Activity Update Saturday December 15, 2018 Report #15

Current Week – Activities

- . Continue Sequence 3 Steel
- . Install Lower Canopy Framing
- . Plumb Sequence 3
- . Weld Brace Frames Sequence 2
- . Snap Bolts 2nd Floor Framing
- . Install Joists
- . Begin Sloped Roof Framing

Next Week – Activities

- . Install Roof Decking
- . Install 2nd Floor Decking
- . Continue Detail of Steel Framing
- . Run Temporary Power to Building
- . Structural Steel Inspection

Weekly Activity Update Saturday December 15,2018 Report #15

Subcontractor	Trade	# of Workers Onsite
Briggs Engineering	Soil Testing	00
Titan Contractors Inc.	Site Work	00
Reed Land Surveying	Engineering	00
Federal Concrete	Foundations	00
Griffin Electric	Electrical	01
G.P East Steel	Steel Erector	05
Colantonio Inc.	Carpenter	01
United Site Services	Site Sanitary	01
BJA	Architect	02
Daedalus	Owner Representative	02
Colantonio Inc.	Construction Manager	03
TOTAL # Onsite This Week		15

Safety

- Safety Orientation for New Jobsite Workers Performed First Day of Work. Total Number of Onsite Workers/Visitors Orientated = 57
- All Workers Wear 100% Hard Hats and Reflective Clothing.
- Fencing and Scrim Reviewed Each Week for Safety and Appearance
- Stone Road Created on West Side for Access
- Weekly Toolbox Talks are Conducted Within Each Trade And a Copy is Submitted to Colantonio Inc.
- Each Contractor Completes a Daily Work Report which Is Kept On File
- Construction Progress Meeting are Held Tuesday at 1PM.
- 78 Days With Zero Worker Accident
- 78 Days Without a Lost Time Accident

Quality Control


- Materials Delivered To The Site Cross Referenced Against Drawings, Submittals and Specifications prior to installation.
- Colantonio Inc and Subcontractor Review of Drawings and Specification Compliance Prior to Work Commencing
- 75 Random Quality Control Inspection Reports have been completed, of those: 1 remain as “Open” and “Non-Conforming”

Miscellaneous

- No Parking During Construction Time Posted on Bradford Avenue
- 1st Floor Slab Placement Completed. FF/FL – 36/27
- Steel Weld/Bolt Inspection – Monday December 17, 2018



Steel Sequence 1

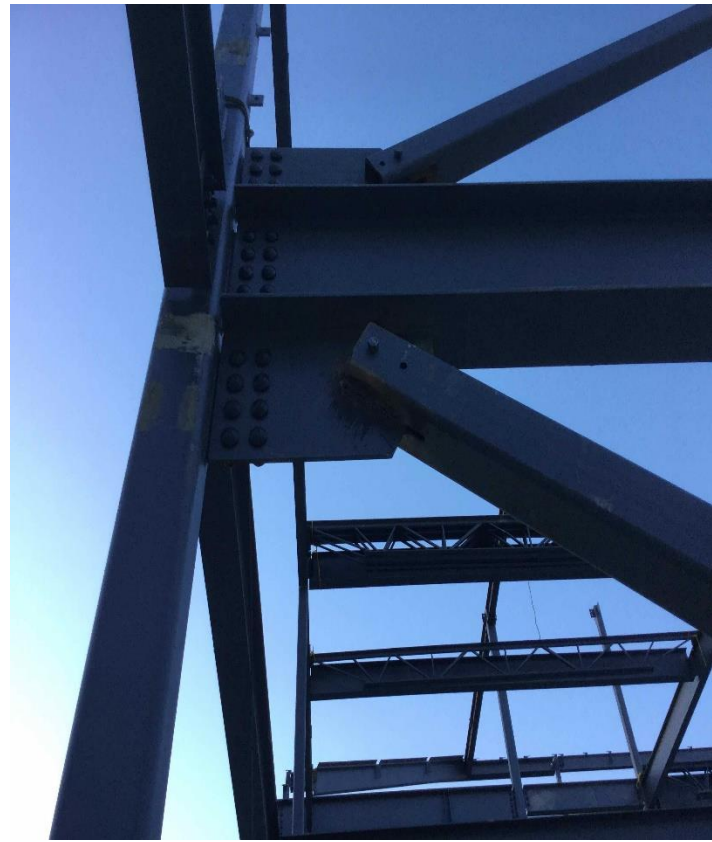

Steel Bolted Connection



Sequence 2 Steel



Roof Framing



Column Erection – Seq. 1



Sequence 1 Columns and Beams



Joist Installation



Sequence 3 with Joists
