

# Sharon Town Hall

## Sharon, MA



**COLANTONIO INC.**  
**PROJECT # 18-3835**

**BKA**

ARCHITECTS



**DAEDALUS**

**samiotes**



ARCHITECTURAL  
**ENGINEERS**

**TRAVERSE**  
landscape architects

## The Sharon Standing Building Committee

**COLANTONIO**  
40 YEARS OF BUILDING RELATIONSHIPS

Weekly Activity Update Saturday December 29, 2018 Report #17

---

### Current Week – Activities

- . Continue Roof Deck
- . Build Access Stairs to 2<sup>nd</sup> Floor
- . Install Sloped Roof Framing
- . Install 2<sup>nd</sup> Floor Decking
- . Install Roof Frame Supports
- . Install Temporary Electric

### Next Week – Activities

- . Build Access Stair to 2<sup>nd</sup> Floor
- . Install Temporary Lighting
- . Continue Roof Deck
- . Install Pour Stop
- . Install Perimeter Safety Cable
- . Receive Winter Protection Materials
- . Slab on Deck Pre-Pour Conference
- . Deck Installation Inspection

## Weekly Activity Update Saturday December 29,2018 Report #17

<b>Subcontractor</b>	<b>Trade</b>	<b># of Workers Onsite</b>
<b>Briggs Engineering</b>	<b>Soil Testing</b>	<b>00</b>
<b>Titan Contractors Inc.</b>	<b>Site Work</b>	<b>00</b>
<b>Reed Land Surveying</b>	<b>Engineering</b>	<b>00</b>
<b>Federal Concrete</b>	<b>Foundations</b>	<b>00</b>
<b>Griffin Electric</b>	<b>Electrical</b>	<b>02</b>
<b>G.P East Steel</b>	<b>Steel Erector</b>	<b>05</b>
<b>Colantonio Inc.</b>	<b>Carpenter</b>	<b>02</b>
<b>United Site Services</b>	<b>Site Sanitary</b>	<b>01</b>
<b>BKA</b>	<b>Architect</b>	<b>00</b>
<b>Daedalus</b>	<b>Owner Representative</b>	<b>01</b>
<b>Colantonio Inc.</b>	<b>Construction Manager</b>	<b>02</b>
<b>TOTAL # Onsite This Week</b>		<b>13</b>

### **Safety**

- Safety Orientation for New Jobsite Workers Performed First Day of Work. Total Number of Onsite Workers/Visitors Orientated = 57
- All Workers Wear 100% Hard Hats and Reflective Clothing.
- Fencing and Scrim Reviewed Each Week for Safety and Appearance
- Weekly Toolbox Talks are Conducted Within Each Trade And a Copy is Submitted to Colantonio Inc.
- Each Contractor Completes a Daily Work Report which Is Kept On File
- Construction Progress Meeting are Held Tuesday at 1PM.
- 88 Days With Zero Worker Accident
- 88 Days Without a Lost Time Accident

### **Quality Control**

- Materials Delivered To The Site Cross Referenced Against Drawings, Submittals and Specifications prior to installation.
- Colantonio Inc and Subcontractor Review of Drawings and Specification Compliance Prior to Work Commencing
- 75 Random Quality Control Inspection Reports have been completed, of those: 2 remain as “Open” and “Non-Conforming”


### **Miscellaneous**

- No Parking During Construction Time Posted on Bradford Avenue
- 2<sup>nd</sup> Floor Slab on Deck Pre-Placement Meeting January 2<sup>nd</sup>
- Roof Deck Inspection
- Tentative Slab on Deck Placement – Week of January 14<sup>th</sup>, 2019





**Roof Deck**

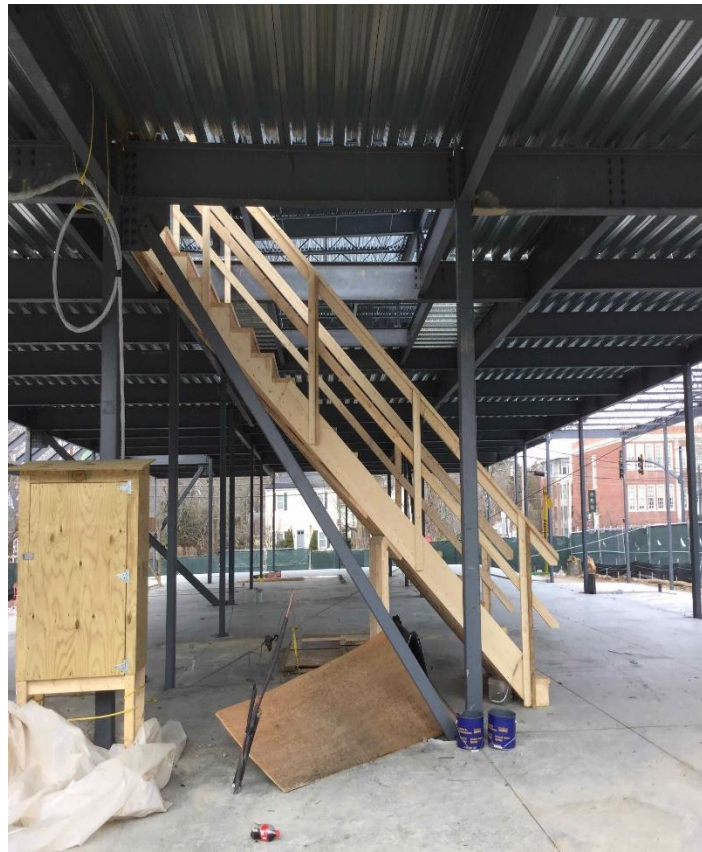

**Roof Deck**



**Frame and Deck**



**Joists and Deck**






**2<sup>nd</sup> Floor Framing**



**2<sup>nd</sup> Floor Framing**



**Underground Temp. Electric**

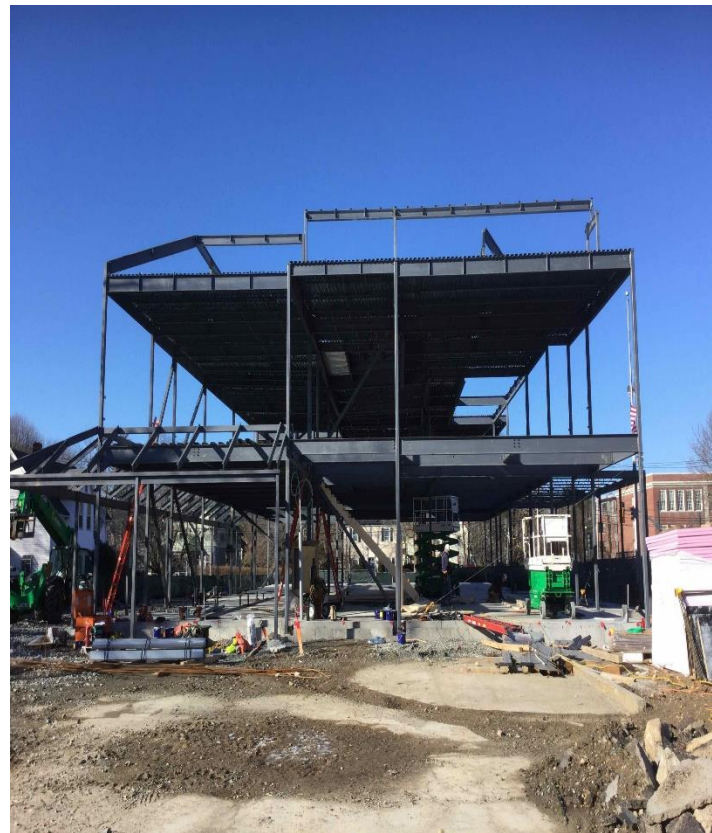

**Temporary Electric**
