

Sharon Town Hall

Sharon, MA



COLANTONIO INC.
PROJECT # 18-3835

BKA

ARCHITECTS



DAEDALUS

samiotes



ARCHITECTURAL
ENGINEERS

TRAVERSE
landscape architects

The Sharon Standing Building Committee

COLANTONIO
40 YEARS OF BUILDING RELATIONSHIPS

Weekly Activity Update

Friday January 18, 2019 Report #18

Current Week – Activities

- . Place Second Floor Slab
- . Continue Exterior Farming 1st Floor
- . Receive Roof Sheathing
- . Begin Roof Sheathing Installation
- . Receive Exterior Framing – 2nd Floor
- . Begin Framing Parapet Walls
- . Receive Exterior Sheathing

Next Week – Activities

- . Begin Second Floor Layout
- . Continue Roof Sheathing
- . Begin Second Floor Exterior Framing
- . Begin Winter Protection Removal
- . Begin Exterior Sheathing Installation
- . MEP Trades Mobilize

Subcontractor	Trade	# of Workers Onsite
Briggs Engineering	Concrete Testing	02
Titan Contractors Inc.	Site Work	01
Reed Land Surveying	Engineering	02
Federal Concrete	Foundations	14
Griffin Electric	Electrical	00
G.P East Steel	Steel Erector	01
Colantonio Inc.	Carpenter	02
United Site Services	Site Sanitary	01
Colony Drywall	Framing	05
BJA	Architect	02
Daedalus	Owner Representative	02
Colantonio Inc.	Construction Manager	03
TOTAL # Onsite This Week		35

Safety

- **Safety Orientation for New Jobsite Workers Performed First Day of Work. Total Number of Onsite Workers/Visitors Orientated = 62**
- **All Workers Wear 100% Hard Hats and Reflective Clothing.**
- **Fencing and Scrim Reviewed Each Week for Safety and Appearance**
- **Weekly Toolbox Talks are Conducted Within Each Trade And a Copy is Submitted to Colantonio Inc.**
- **Each Contractor Completes a Daily Work Report which Is Kept On File**
- **Construction Progress Meeting are Held Tuesday at 1PM.**
- **103 Days With Zero Worker Accident**
- **103 Days Without a Lost Time Accident**

Quality Control


- **Materials Delivered To The Site Cross Referenced Against Drawings, Submittals and Specifications prior to installation.**
- **Colantonio Inc and Subcontractor Review of Drawings and Specification Compliance Prior to Work Commencing**
- **83 Random Quality Control Inspection Reports have been completed, of those: 3 remain as “Open” and “Non-Conforming”**

Miscellaneous

- **No Parking During Construction Time Posted on Bradford Avenue**
- **Walk Through of Building with Sharon Fire Department**
- **All Roof Material Removed Prior to “Storm”**




2nd Floor Slab Placement

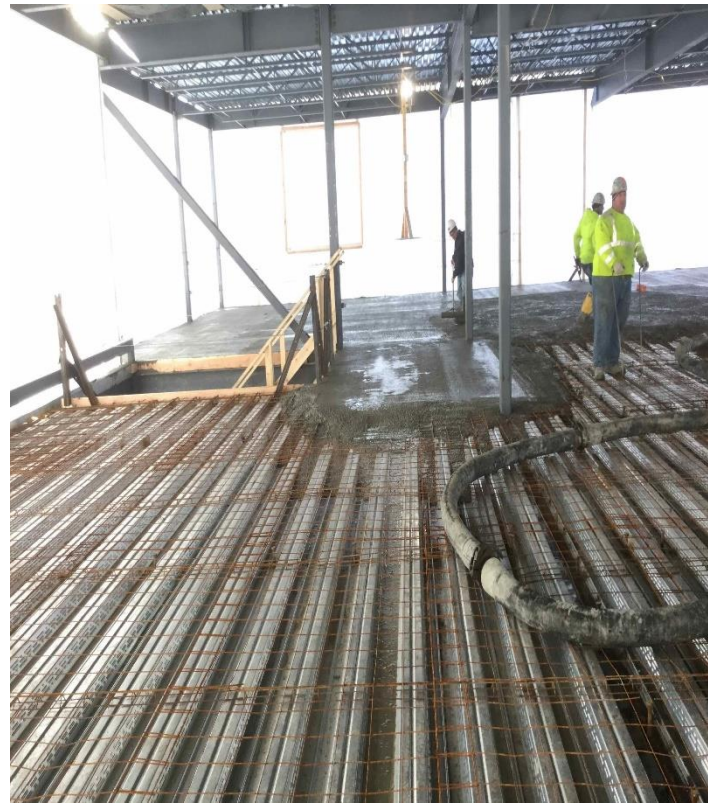

2nd Floor Slab Placement



2nd Floor Slab Finishing

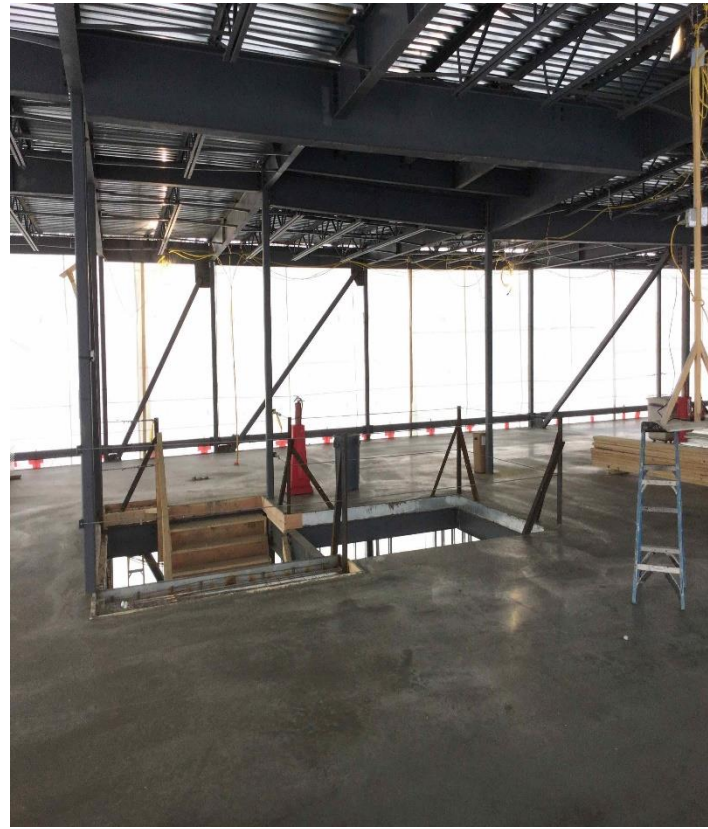

2nd Floor Slab Finish



Signed Beam In Place



Roof Sheathing



Roof Framing



Roof Sheathing
