

Sharon Town Hall

Sharon, MA



COLANTONIO INC.
PROJECT # 18-3835

BKA

ARCHITECTS



DAEDALUS

samiotes



ARCHITECTURAL
ENGINEERS

TRAVERSE
landscape architects

The Sharon Standing Building Committee

COLANTONIO
40 YEARS OF BUILDING RELATIONSHIPS

Weekly Activity Update

Friday February 16, 2019 Report #21

Current Week – Activities

- . Complete Exterior Sheathing
- . Continue Tyvek Installation
- . Continue Framing Gutter West Elevation
- . Continue Roof Drain Piping
- . Install Carriers – 2nd Floor
- . Install Carriers – 1st Floor
- . Continue Interior Framing – 2nd Floor
- . Continue Layout First Floor
- . Begin Vertical Roof Membrane
- . Begin Water Proof Angle Flashing
- . Begin Sheet Metal Dimensioning

Next Week – Activities

- . Begin Exterior Trim
- . Continue Gutter Blocking West Elevation
- . Continue Bathroom Rough
- . Continue Roof Drain Piping
- . Continue Roof Installation
- . Install Ice and Water Membrane
- . Receive Drainage Structures 1 – 4
- . Begin Drainage Installation
- . Begin Electrical Layout
- . Continue Water proof Angle Flashing
- . Receive Fan Coil Units (Shop)

Subcontractor	Trade	# of Workers Onsite
Briggs Engineering	Concrete Testing	00
Titan Contractors Inc.	Site Work	01
Reed Land Surveying	Engineering	00
Marmello	Masonry	04
Griffin Electric	Electrical	00
G.P East Steel	Steel Erector	00
Colantonio Inc.	Carpenter	03
United Site Services	Site Sanitary	01
Colony Drywall	Framing	08
Colantonio	Labor	01
LaPan Mechanical	Plumbing	02
Division 15	HVAC	01
Greenwood Industries	Roofing	03
BKA	Architect	02
Daedalus	Owner Representative	02
Colantonio Inc.	Construction Manager	03
TOTAL # Onsite This Week		30

Safety

- **Safety Orientation for New Jobsite Workers Performed First Day of Work. Total Number of Onsite Workers/Visitors Orientated = 74**
- **All Workers Wear 100% Hard Hats and Reflective Clothing.**
- **Fencing and Scrim Reviewed Each Week for Safety and Appearance**
- **Weekly Toolbox Talks are Conducted Within Each Trade And a Copy is Submitted to Colantonio Inc.**
- **Each Contractor Completes a Daily Work Report which Is Kept On File**
- **Construction Progress Meeting are Held Tuesday at 1PM.**
- **124 Days With Zero Worker Accident**
- **124 Days Without a Lost Time Accident**

Quality Control

- **Materials Delivered To The Site Cross Referenced Against Drawings, Submittals and Specifications prior to installation.**
- **Colantonio Inc and Subcontractor Review of Drawings and Specification Compliance Prior to Work Commencing**
- **90 Random Quality Control Inspection Reports have been completed, of those: 2 remain as “Open” and “Non-Conforming”**

Miscellaneous

- **No Parking During Construction Time Posted on Bradford Avenue**
- **Colantonio Inc. subcontractor meeting to be held on Tuesdays at 10AM**
- **Coordination Drawings – 75% Complete**



Low Roof Blocking



Angle Flashing Installation



West Elevation Roof Framing



South Elevation




Exterior Sheathing



Parapet Wall Membrane



Gutter Framing

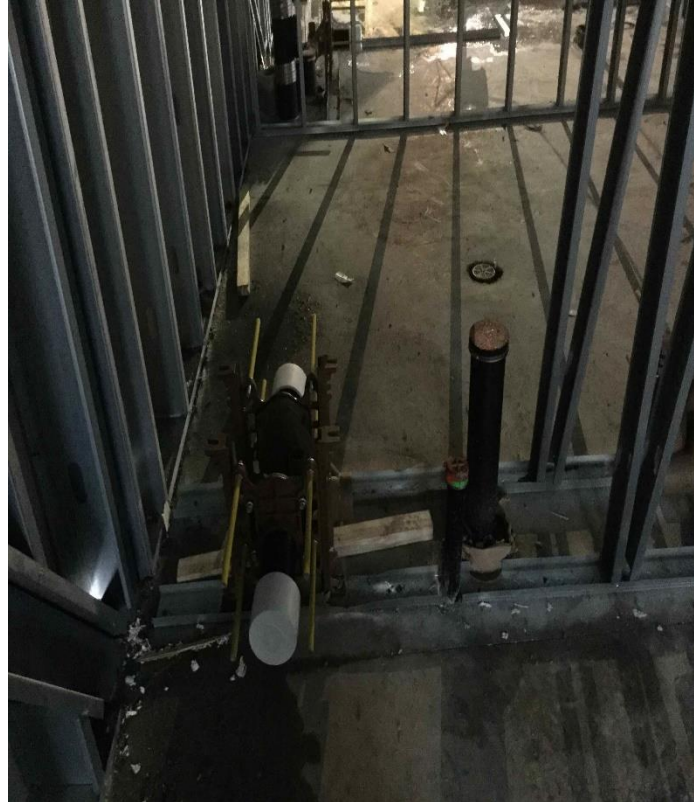

Plumbing Rough
