

Sharon Town Hall

Sharon, MA



COLANTONIO INC.
PROJECT # 18-3835

BKA

ARCHITECTS



DAEDALUS

samiotes



ARCHITECTURAL
ENGINEERS

TRAVERSE
landscape architects

The Sharon Standing Building Committee

COLANTONIO
40 YEARS OF BUILDING RELATIONSHIPS

Weekly Activity Update

Friday February 23, 2019 Report #22

Current Week – Activities

- . Install Trim North Elevation
- . Install trim West Elevation
- . Continue Rain Gutter Framing
- . Continue Trim Blocking
- . Complete Exterior Sheathing
- . Complete Tyvek
- . Complete RFI #87 Angle
- . Install Flat Roof Framing/Plywood
- . Begin Flat Roof EPDM Installation
- . Install Sloped Roof Ice and Water Shield
- . Receive Drainage Structures
- . Receive Drainage Piping
- . Continue 2nd Floor Framing
- . Continue 2nd Floor Layout
- . Continue 1st Floor Framing

Next Week – Activities

- . Continue Exterior Trim West Elevation
- . Begin North Drainage
- . Continue EPDM Installation
- . Continue Ice and Water Shield Install
- . Frame Cupola Base
- . Continue 2nd Floor Framing
- . Receive Windows and Flashing
- . Begin Electrical Pipe and Boxes)
- . Continue Plumbing Rough
- . Complete Coordination Drawings
- . Install Stair #2
- . Patch Tyvek Openings
- .

Subcontractor	Trade	# of Workers Onsite
Briggs Engineering	Concrete Testing	01
Titan Contractors Inc.	Site Work	01
Reed Land Surveying	Engineering	00
Marmello	Masonry	00
Griffin Electric	Electrical	01
G.P East Steel	Steel Erector	00
Colantonio Inc.	Carpenter	08
United Site Services	Site Sanitary	01
Colony Drywall	Framing	06
Colantonio	Labor	01
LaPan Mechanical	Plumbing	02
Division 15	HVAC	00
Greenwood Industries	Roofing	12
BKA	Architect	02
Daedalus	Owner Representative	02
Colantonio Inc.	Construction Manager	02
TOTAL # Onsite This Week		39

Safety


- Safety Orientation for New Jobsite Workers Performed First Day of Work. Total Number of Onsite Workers/Visitors Orientated = 78
- All Workers Wear 100% Hard Hats and Reflective Clothing.
- Fencing and Scrim Reviewed Each Week for Safety and Appearance
- Weekly Toolbox Talks are Conducted Within Each Trade And a Copy is Submitted to Colantonio Inc.
- Each Contractor Completes a Daily Work Report which Is Kept On File
- Construction Progress Meeting are Held Tuesday at 1PM.
- 130 Days With Zero Worker Accident
- 130 Days Without a Lost Time Accident

Quality Control


- Materials Delivered To The Site Cross Referenced Against Drawings, Submittals and Specifications prior to installation.
- Colantonio Inc and Subcontractor Review of Drawings and Specification Compliance Prior to Work Commencing
- 94 Random Quality Control Inspection Reports have been completed, of those: 2 remain as “Open” and “Non-Conforming”

Miscellaneous

- No Parking During Construction Time Posted on Bradford Avenue
- Colantonio Inc. subcontractor meeting to be held on Tuesdays at 10AM
- Coordination Drawings – 75% Complete
- Hydraulic Spill reported, contained and cleaned up
- Briggs Engineering On Site for Roofing Inspection

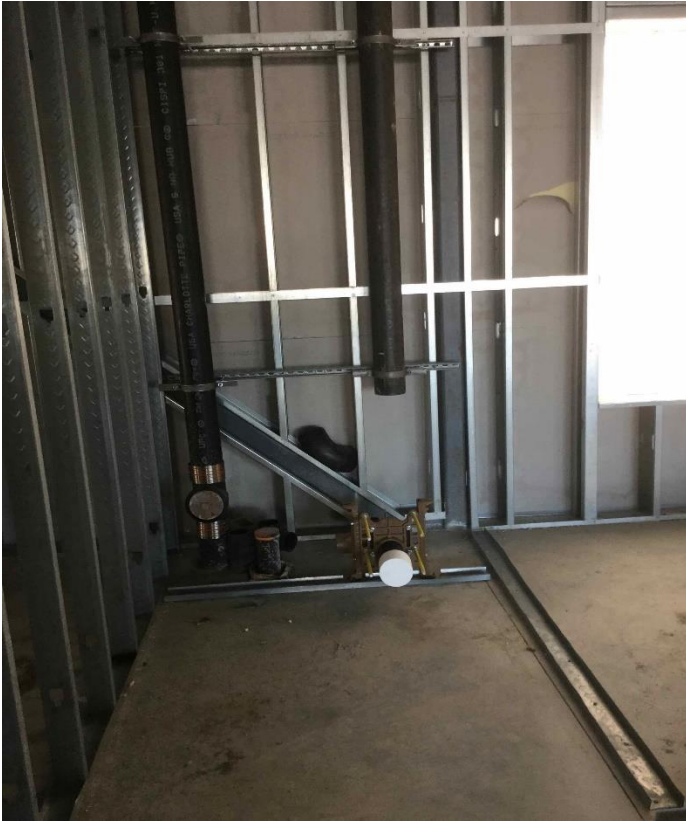

Rough Plumbing

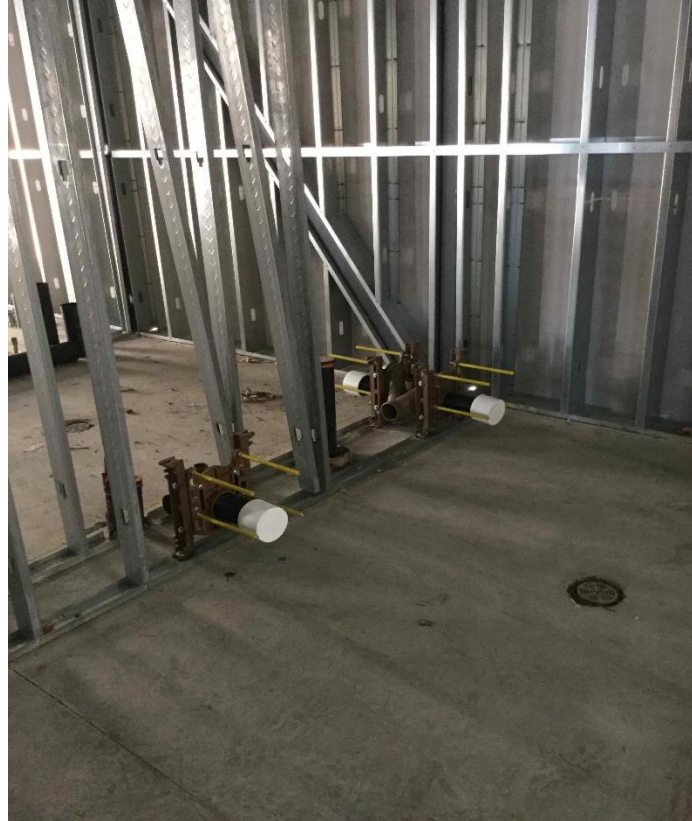

Rough Plumbing



Mechanical Blocking



Trim Installation - North



South Elevation



Roof Insulation Installation



Protection Board Install



EPDM Installation
