

# Sharon Town Hall

## Sharon, MA



**COLANTONIO INC.**  
**PROJECT # 18-3835**

**BKA**

ARCHITECTS



**DAEDALUS**

samiotes



ARCHITECTURAL  
**ENGINEERS**

**TRAVERSE**  
landscape architects

## The Sharon Standing Building Committee

**COLANTONIO**  
40 YEARS OF BUILDING RELATIONSHIPS

Weekly Activity Update

Friday March 1, 2019 Report #23

### Current Week – Activities

- . Receive Windows
- . Continue Fascia and Soffit Trim
- . Begin Scupper Drain Installation
- . Tie In Roof Drain
- . Install DMH #1 - 4 and Piping
- . Install Low Canopy Roof Framing
- . Install Low Roof Sheathing
- . Receive 2<sup>nd</sup> Floor Duct (Partial)
- . Tie in Seams Upper Roof EPDM
- . Install Low Roof EPDM
- . Continue Stair #2 Installation
- . Receive Stair #1
- . Receive 2<sup>nd</sup> Floor Electric Rough

### Next Week – Activities

- . Continue Stair #2
- . Begin Stair #1
- . Continue Soffit and Fascia trim
- . Begin Window Installation
- . Install Foundation Membrane
- . Continue 2<sup>nd</sup> Floor Framing
- . Begin Electric Rough
- . Begin Mechanical Rough
- . Continue Lobby Layout and Framing
- . Continue Ice/Water Membrane
- . Snow Removal
- . Excavate for Primary Electric Service

Subcontractor	Trade	# of Workers Onsite
Briggs Engineering	Concrete Testing	00
Titan Contractors Inc.	Site Work	02
Reed Land Surveying	Engineering	00
Marmello	Masonry	00
Griffin Electric	Electrical	02
G.P East Steel	Steel Erector	00
Colantonio Inc.	Carpenter	06
United Site Services	Site Sanitary	01
Colony Drywall	Framing	06
Colantonio	Labor	01
LaPan Mechanical	Plumbing	02
Division 15	HVAC	02
Greenwood Industries	Roofing	04
Sharon Police	Detail	01
NE Foam	Insulation	02
BKA	Architect	02
Daedalus	Owner Representative	02
Colantonio Inc.	Construction Manager	02
<b>TOTAL # Onsite This Week</b>		<b>35</b>

### **Safety**

- **Safety Orientation for New Jobsite Workers Performed First Day of Work. Total Number of Onsite Workers/Visitors Orientated = 84**
- **All Workers Wear 100% Hard Hats and Reflective Clothing.**
- **Fencing and Scrim Reviewed Each Week for Safety and Appearance**
- **Weekly Toolbox Talks are Conducted Within Each Trade And a Copy is Submitted to Colantonio Inc.**
- **Each Contractor Completes a Daily Work Report which Is Kept On File**
- **Construction Progress Meeting are Held Tuesday at 1PM.**
- **135 Days With Zero Worker Accident**
- **135 Days Without a Lost Time Accident**


### **Quality Control**

- **Materials Delivered To The Site Cross Referenced Against Drawings, Submittals and Specifications prior to installation.**
- **Colantonio Inc and Subcontractor Review of Drawings and Specification Compliance Prior to Work Commencing**
- **96 Random Quality Control Inspection Reports have been completed, of those: 3 remain as “Open” and “Non-Conforming”**

### **Miscellaneous**

- **No Parking During Construction Time Posted on Bradford Avenue**
- **Colantonio Inc. subcontractor meeting to be held on Tuesdays at 10AM**
- **Coordination Drawings – 75% Complete**



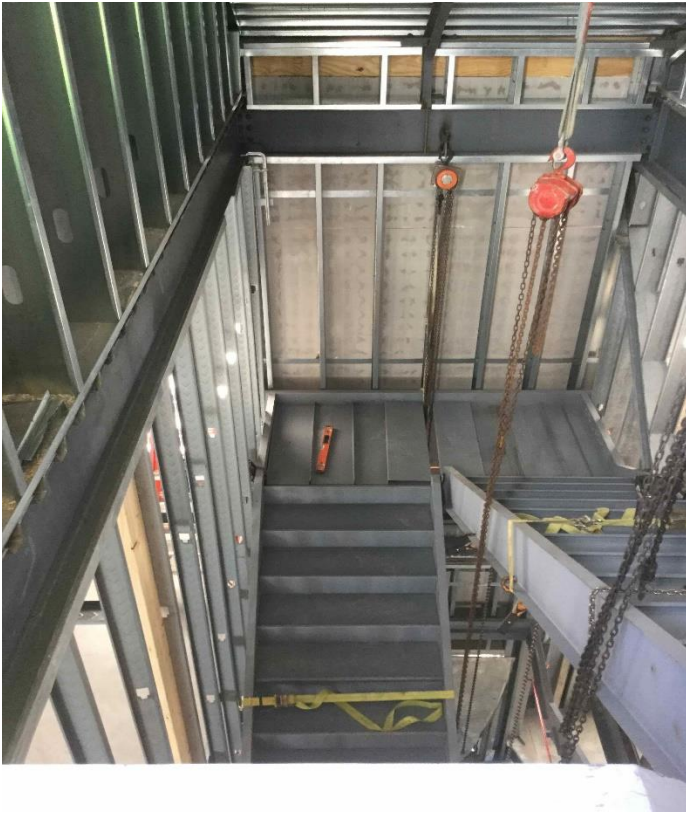


**Stair #2 Install**



**HVAC Delivery**



**DMH-3 Tie In**

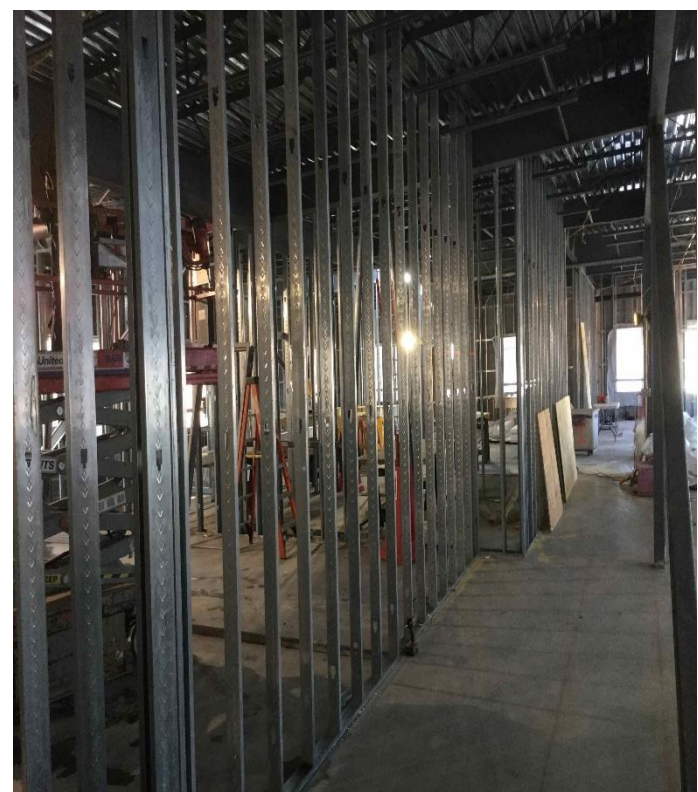


**2<sup>nd</sup> Floor Framing**





**South Elevation**

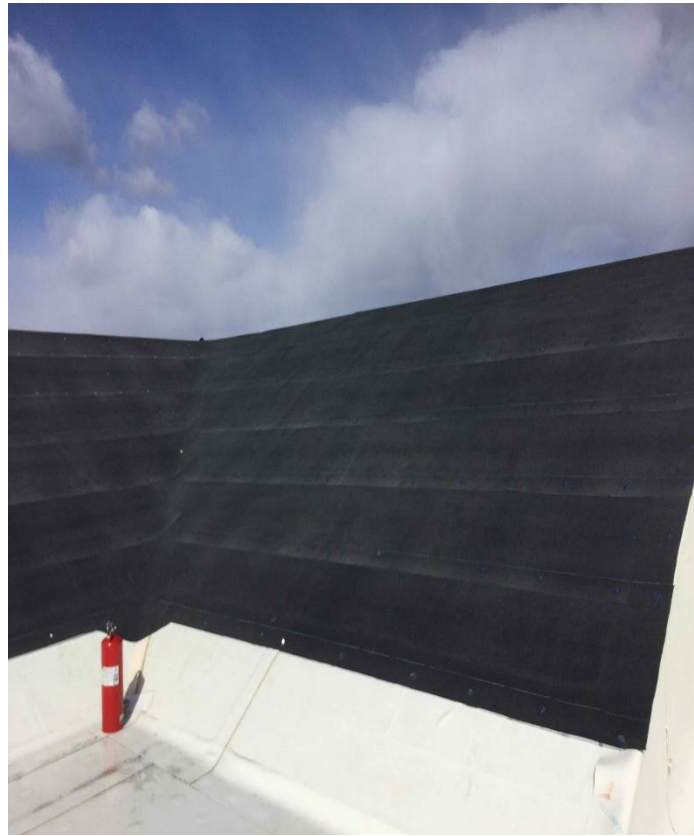

**Roof Installation**



**Low Roof Membrane**



**Low Roof EPDM**
