

# Sharon Town Hall Sharon, MA



**COLANTONIO INC.**  
**PROJECT # 18-3835**

**BKA**

ARCHITECTS



**DAEDALUS**

**samiotes**



ARCHITECTURAL  
**ENGINEERS**

**TRAVERSE**  
landscape architects

## The Sharon Standing Building Committee

**COLANTONIO**  
40 YEARS OF BUILDING RELATIONSHIPS

Weekly Activity Update

Saturday March 9, 2019 Report #24

### Current Week – Activities

- . Begin Window Installation
- . Repair TYVEK North and East Elevations
- . Install and Tie in Gutter Drains
- . Install Stair #2
- . Begin Layout Stair #1
- . Frame Cupola Base
- . Frame Cupola Peak
- . Continue Door Frame Installation
- . Begin Electric Rough- 2<sup>nd</sup> Floor
- . Continue Framing 2<sup>nd</sup> Floor
- . Frame Vestibule Area
- . Frame Clerk and File Area
- . Tie in Low Slope Drains
- . Set Up Ground Thaw for North Drainage
- . Walk Through With Sharon Fire
- . Walk Through With Building Inspector
- . EverSource Coordination Primary Service
- . Remove Snow Upper Sloped Roof
- . Dog Rescue

### Next Week – Activities

- . Install Shear Clips on Elevator Shaft
- . Receive Drywall
- . Continue Electric Rough
- . Continue HVAC Duct Rough
- . Begin Mechanical Piping
- . Continue Plumbing Rough
- . Install Foundation Membrane
- . Receive Metal Drip Edge
- . Receive Cement Siding
- . Receive Vaults
- . Continue Cupola Installation
- . Install DMH – 4 and Drain Piping
- . Excavate for Primary Service
- . Install Interior Wall – Electric Room
- . Receive Sprinkler Piping
- . Complete Fascia Trim
- . Continue Window Installation - West

Subcontractor	Trade	# of Workers Onsite
Briggs Engineering	Concrete Testing	00
Titan Contractors Inc.	Site Work	02
Reed Land Surveying	Engineering	00
Marmello	Masonry	00
Griffin Electric	Electrical	02
SMJ Inc	Misc. Metals	04
Colantonio Inc.	Carpenter	07
United Site Services	Site Sanitary	01
Colony Drywall	Framing	06
Colantonio	Labor	01
LaPan Mechanical	Plumbing	01
Division 15	HVAC	04
Greenwood Industries	Roofing	00
Sharon Police	Detail	00
NE Foam	Insulation	00
Andersen	Window Representative	01
BKA	Architect	02
Daedalus	Owner Representative	02
Colantonio Inc.	Construction Manager	02
<b>TOTAL # Onsite This Week</b>		<b>35</b>

### **Safety**

- **Safety Orientation for New Jobsite Workers Performed First Day of Work. Total Number of Onsite Workers/Visitors Orientated = 88**
- **All Workers Wear 100% Hard Hats and Reflective Clothing.**
- **Fencing and Scrim Reviewed Each Week for Safety and Appearance**
- **Weekly Toolbox Talks are Conducted Within Each Trade And a Copy is Submitted to Colantonio Inc.**
- **Each Contractor Completes a Daily Work Report which Is Kept On File**
- **Construction Progress Meeting are Held Tuesday at 1PM.**
- **141 Days With Zero Worker Accident**
- **141 Days Without a Lost Time Accident**

### **Quality Control**

- **Materials Delivered To The Site Cross Referenced Against Drawings, Submittals and Specifications prior to installation.**
- **Colantonio Inc and Subcontractor Review of Drawings and Specification Compliance Prior to Work Commencing**
- **101 Random Quality Control Inspection Reports have been completed, of those:1 remain as “Open” and “Non-Conforming”**


### **Miscellaneous**

- **No Parking During Construction Time Posted on Bradford Avenue**
- **Colantonio Inc. subcontractor meeting to be held on Tuesdays at 10AM**
- **Coordination Drawings – 80% Complete**
- **Sharon Fire Captains Tour of the Site**
- **Walk Through With Joe Kent and Deputy Chief Murphy**





**Interior Framing**

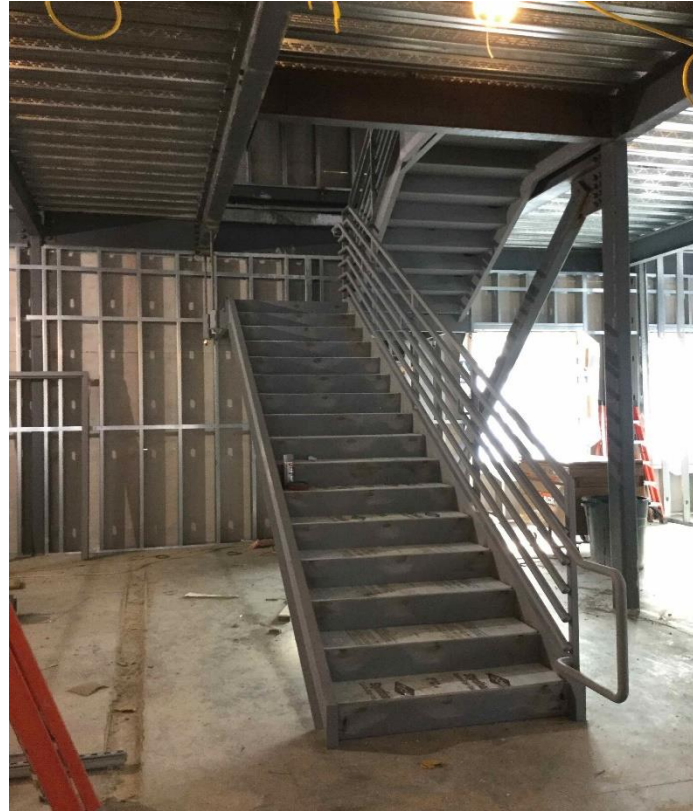

**Stair #2**



**Interior Framing**




**TYVEK Repair**





**Window Installation**

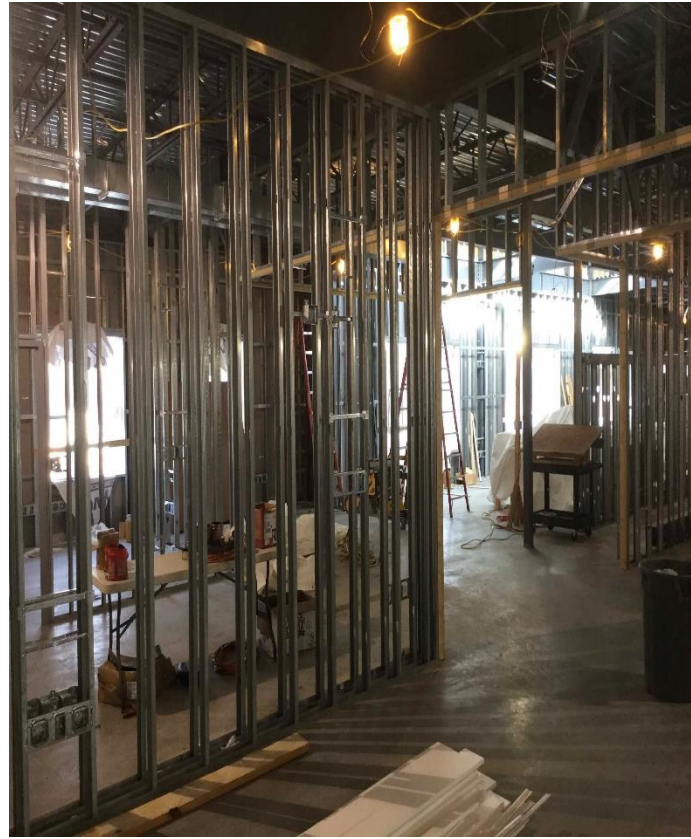

**Electric Rough**



**Seismic Clips**



**Dod Rescue and Return**
