

# Sharon Town Hall Sharon, MA



**COLANTONIO INC.**  
**PROJECT # 18-3835**

**BKA**

ARCHITECTS



**DAEDALUS**

samiotes

ARCHITECTURAL  
**ENGINEERS**

TRAVERSE  
landscape architects

## The Sharon Standing Building Committee

**COLANTONIO**  
40 YEARS OF BUILDING RELATIONSHIPS

Weekly Activity Update

Saturday March 16, 2019 Report #25

### Current Week – Activities

- . Continue Window Installation
- . Finish Fascia Trim and Moulding
- . Layout and Frame 1<sup>st</sup> Floor
- . Install Insulation
- . Install Poly and Drywall – Vault
- . Install Plywood – Electric Room
- . Install Door Frames
- . Continue 2<sup>nd</sup> Floor Electric Rough
- . Install Primary Conduit and Grounding
- . Continue Plumbing Rough- 2<sup>nd</sup> Floor
- . Install Foundation Waterproofing
- . Install Gutter Cant and Membrane
- . Install Shingles
- . Continue Frame of Cupola
- . Continue HVAC Rough – 2<sup>nd</sup> Floor
- . Install Stair #1
- . Install Drainage – East

### Next Week – Activities

- . Continue Window Installation
- . Continue Shingle Installation
- . Complete Primary Duct Bank
- . Install Transformer Pad
- . Deliver Clerk and Shared Vault
- . Begin Install of Clerk Vault
- . Begin Fire Alarm Rough – 2<sup>nd</sup> Floor
- . Continue Electric Rough – 2<sup>nd</sup> Floor
- . Continue Plumbing Rough – 2<sup>nd</sup> Floor
- . Continue HVAC Rough – 2<sup>nd</sup> Floor
- . Place Concrete Stair Treads - #1 and #2
- . Begin Installation of Electric Room
- . Window Testing

Subcontractor	Trade	# of Workers Onsite
Briggs Engineering	Testing	00
Titan Contractors Inc.	Site Work	02
Reed Land Surveying	Engineering	00
Marmello	Masonry	00
Griffin Electric	Electrical	04
SMJ Inc	Misc. Metals	04
Colantonio Inc.	Carpenter	05
United Site Services	Site Sanitary	01
Colony Drywall	Framing	06
Colantonio	Labor	01
LaPan Mechanical	Plumbing	02
Division 15	HVAC	02
Greenwood Industries	Roofing	04
Sharon Police	Detail	01
NE Foam	Insulation	01
Andersen	Window Representative	01
BKA	Architect	02
Daedalus	Owner Representative	02
Colantonio Inc.	Construction Manager	02
<b>TOTAL # Onsite This Week</b>		<b>40</b>

### **Safety**

- **Safety Orientation for New Jobsite Workers Performed First Day of Work. Total Number of Onsite Workers/Visitors Orientated = 94**
- **All Workers Wear Proper PPE At All Times**
- **Fencing and Scrim Reviewed Each Week for Safety and Appearance**
- **Weekly Toolbox Talks are Conducted Within Each Trade And a Copy is Submitted to Colantonio Inc.**
- **Each Contractor Completes a Daily Work Report which Is Kept On File**
- **Construction Progress Meeting are Held Tuesday at 1PM.**
- **147 Days With Zero Worker Accident**
- **147 Days Without a Lost Time Accident**


### **Quality Control**

- **Materials Delivered To The Site Cross Referenced Against Drawings, Submittals and Specifications prior to installation.**
- **Colantonio Inc and Subcontractor Review of Drawings and Specification Compliance Prior to Work Commencing**
- **112 Random Quality Control Inspection Reports have been completed, of those:03 remain as “Open” and “Non-Conforming”**

### **Miscellaneous**

- **No Parking During Construction Time Posted on Bradford Avenue**
- **Colantonio Inc. subcontractor meeting to be held on Tuesdays at 10AM**
- **Coordination Drawings – 2<sup>nd</sup> Floor 100%, 1<sup>st</sup> Floor 70%**
-



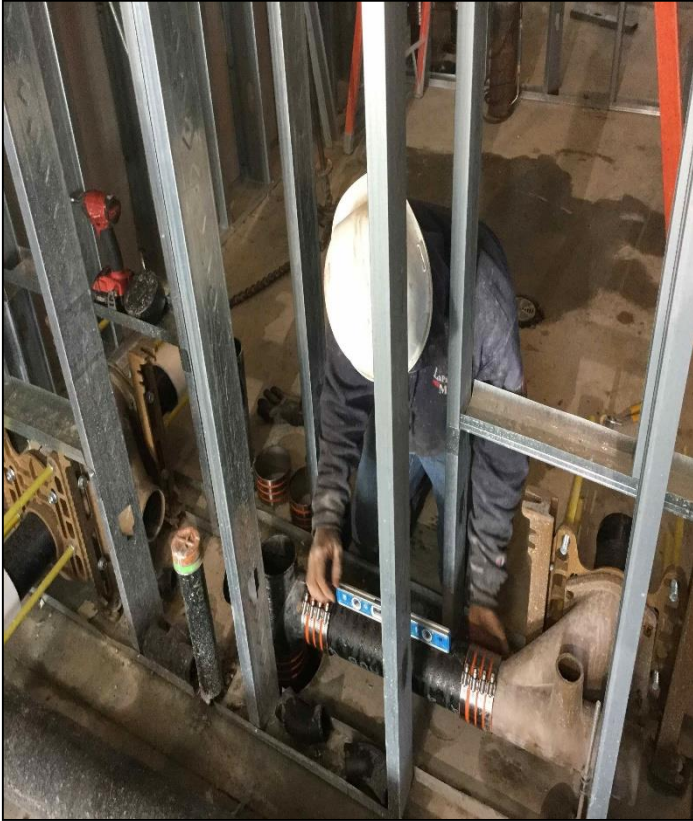


**Bathroom Rough Plumbing**



**Storm Drainage Install**



**Exterior Wall - Vault**

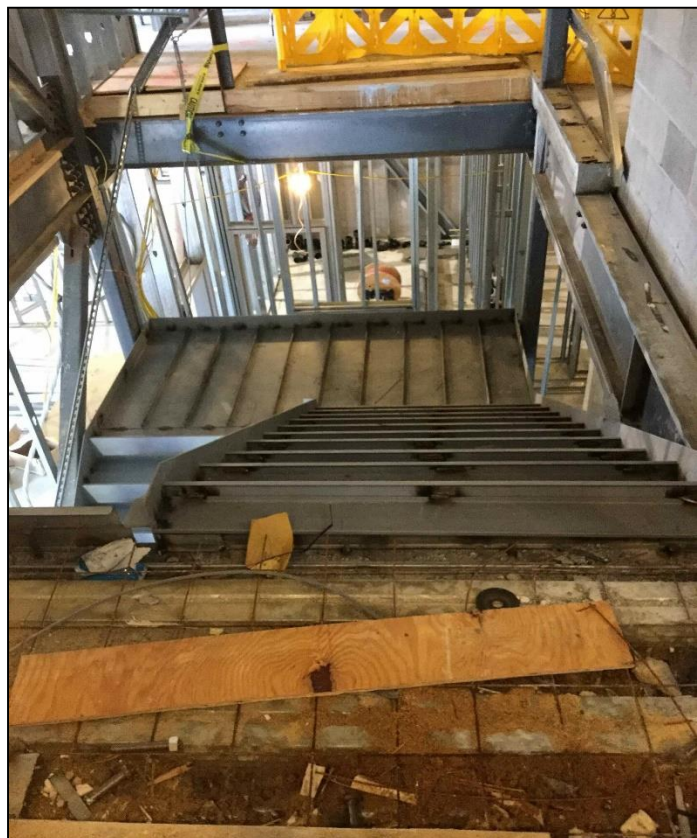


**Stair #1 Installation**





**Roof and Cupola**

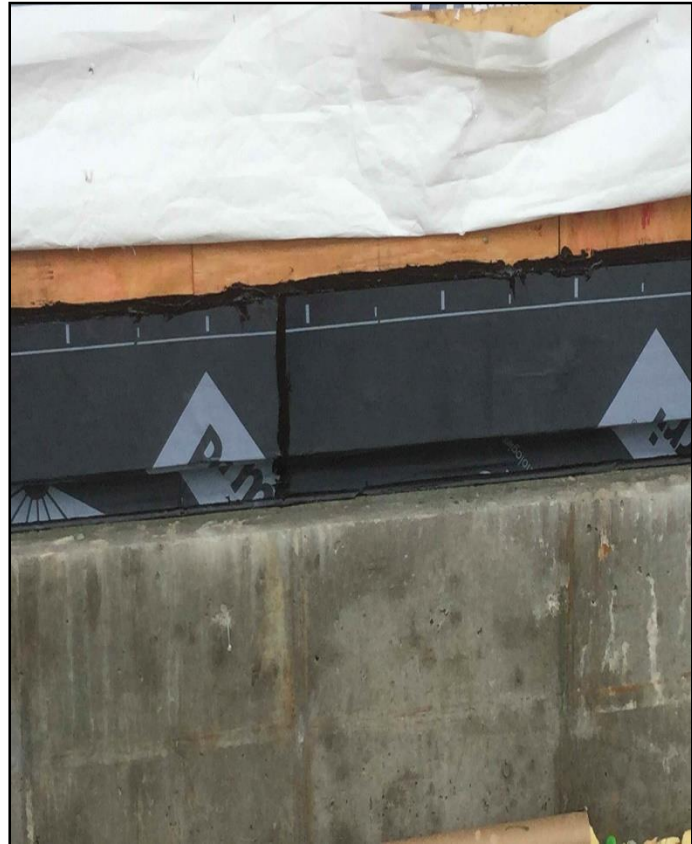

**Foundation Waterproofing**



**Transformer Grounding**



**Dod Rescue and Return**



