

# Sharon Town Hall Sharon, MA



**COLANTONIO INC.**  
**PROJECT # 18-3835**

**BKA**

ARCHITECTS



**DAEDALUS**

**samiotes**



ARCHITECTURAL  
**ENGINEERS**

**TRAVERSE**  
landscape architects

## The Sharon Standing Building Committee

**COLANTONIO**  
40 YEARS OF BUILDING RELATIONSHIPS

Weekly Activity Update

Saturday March 23, 2019 Report #26

### Current Week – Activities

- . Continue Window Installation
- . Perform Water Test of Windows
- . Continue Trim Board South
- . Install Corner Boards and Door Trim
- . Paint Main Electric Room
- . Continue 2<sup>nd</sup> Floor MEP Rough
- . Begin Framing Hard Ceilings
- . Install Gutter Membrane
- . Install Shingles
- . Frame Exterior Ceilings
- . Set Transformer Pad
- . Continue Fire Alarm Rough
- . Place Stair #1 and #2 Concrete
- . Begin Clerk Vault Installation
- . Clean Out Elevator Pit
- . Release Granite
- . Receive Shared Vault

### Next Week – Activities

- . Continue Window Installation
- . Begin Siding Installation
- . Continue MEP Rough 2<sup>nd</sup> Floor
- . Continue Fire Alarm Rough
- . Begin Fire protection Rough
- . Continue Clerk vault
- . Begin Shared Vault
- . Begin Main Electric Rough
- . Continue Frame Hard Ceilings
- . Continue Shingles
- . Continue Membrane Installation
- . Field Measure for Aluminum Frames
- . Continue In-Wall Blocking
- . Frame Stairwell Walls
- . Begin Top of Wall Drywall
- . Continue Attic Spray Foam

Subcontractor	Trade	# of Workers Onsite
InterTek	Window Testing	02
Titan Contractors Inc.	Site Work	01
Reed Land Surveying	Engineering	00
Marmello	Masonry	01
Griffin Electric	Electrical	04
SMJ Inc	Misc. Metals	00
Colantonio Inc.	Carpenter	05
United Site Services	Site Sanitary	01
Colony Drywall	Framing	06
Colantonio	Labor	01
LaPan Mechanical	Plumbing	02
Division 15	HVAC	02
Greenwood Industries	Roofing	04
Sharon Police	Detail	01
NE Foam	Insulation	02
Andersen	Window Representative	01
FireLock	Vault Installer	05
Color Concepts	Painting	02
BKA	Architect	02
Daedalus	Owner Representative	02
Colantonio Inc.	Construction Manager	02
<b>TOTAL # Onsite This Week</b>		<b>46</b>

### Safety

- Safety Orientation for New Jobsite Workers Performed First Day of Work. Total Number of Onsite Workers/Visitors Orientated = 99
- All Workers Wear Proper PPE At All Times
- Fencing and Scrim Reviewed Each Week for Safety and Appearance
- Weekly Toolbox Talks are Conducted Within Each Trade And a Copy is Submitted to Colantonio Inc.
- Each Contractor Completes a Daily Work Report which Is Kept On File
- Construction Progress Meeting are Held Tuesday at 1PM.
- 153 Days With Zero Worker Accident
- 153 Days Without a Lost Time Accident

### Quality Control

- Materials Delivered To The Site Cross Referenced Against Drawings, Submittals and Specifications prior to installation.
- Colantonio Inc and Subcontractor Review of Drawings and Specification Compliance Prior to Work Commencing
- 118 Random Quality Control Inspection Reports have been completed, of those:03 remain as “Open” and “Non-Conforming”

### Miscellaneous

- No Parking During Construction Time Posted on Bradford Avenue
- Colantonio Inc. subcontractor meeting to be held on Tuesdays at 10AM
- Coordination Drawings – 2<sup>nd</sup> Floor 100%, 1<sup>st</sup> Floor 70%
- Workers Utilizing Deb Sampson Parking Lot





**Window Installation**



**South Elevation**




**Exterior Trim Installation**




**Water Testing**



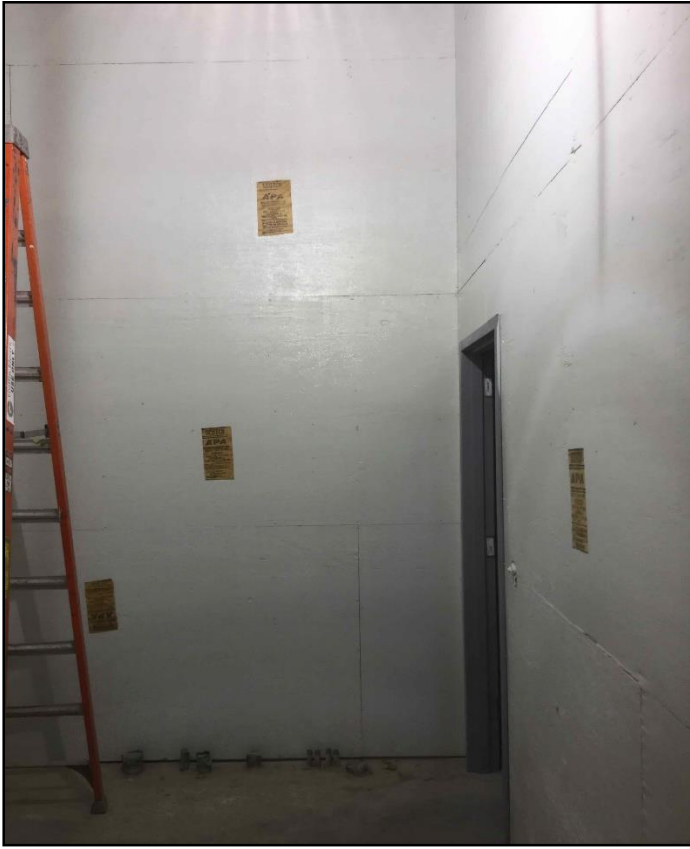


**Main Electric Room**

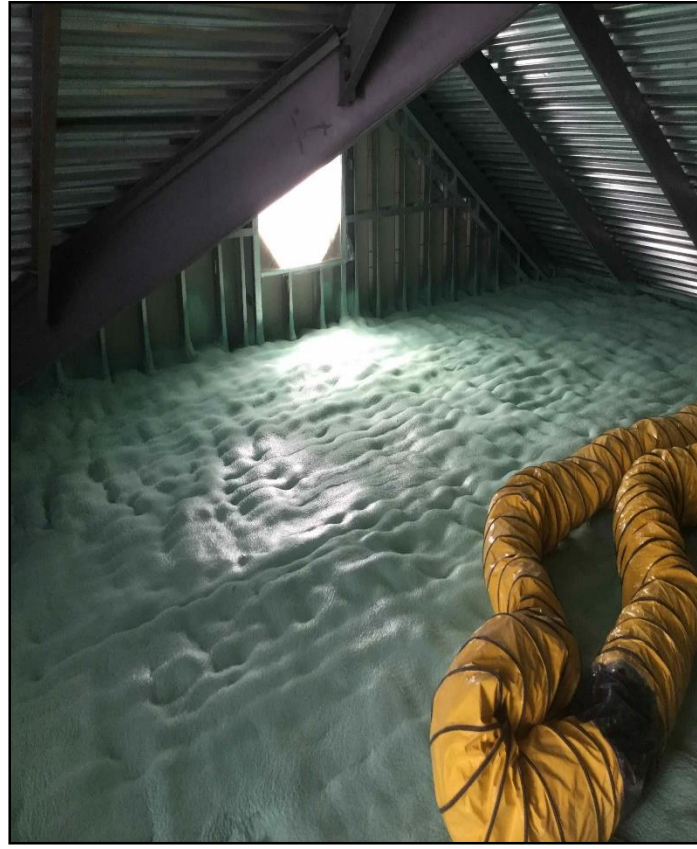

**Attic Spray Foam**



**Clerk Vault Installation**

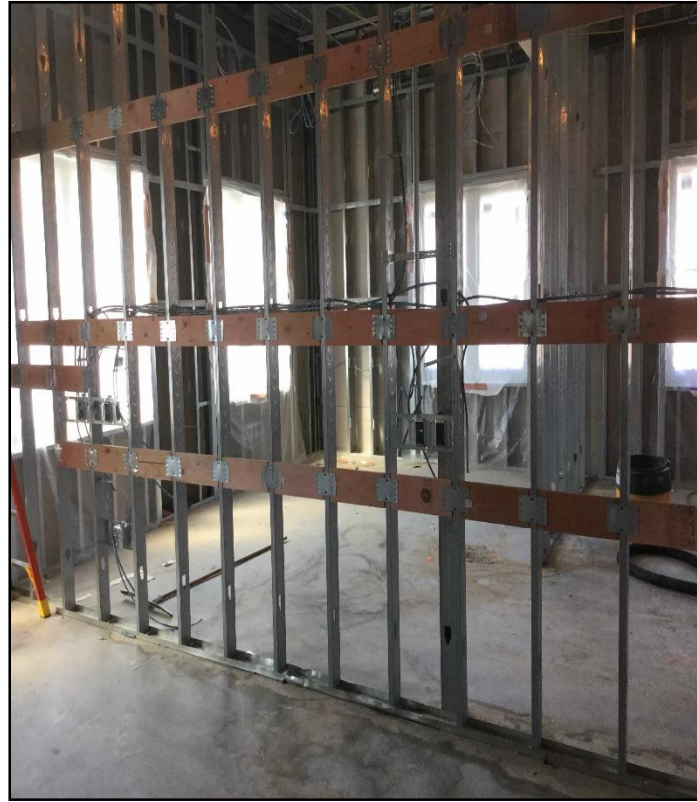

**In Wall Blocking**
