

# Sharon Town Hall Sharon, MA



**COLANTONIO INC.**  
**PROJECT # 18-3835**

**BKA**

ARCHITECTS



**DAEDALUS**

**samiotes**



ARCHITECTURAL  
**ENGINEERS**

**TRAVERSE**  
landscape architects

## The Sharon Standing Building Committee



### Weekly Activity Update

Friday April 19, 2019 Report #30

#### Current Week – Activities

- . 1<sup>st</sup> Floor Framing Inspection
- . UGE/UGP Inspection for Generator
- . Installation and Backfill of Septic Tanks
- . Install Shingle Siding West and South
- . Install Low Canopy Trim and Board
- . Begin Main Electric Room Build out
- . Plywood Mechanical Room
- . Complete 2<sup>nd</sup> Floor Pipe Insulation
- . Hang Durock/Green Board in Bathrooms
- . Continue Mud/Tape Drywall 2<sup>nd</sup> Floor
- . Continue Hang Drywall 2<sup>nd</sup> Floor
- . Insulate and Poly Exterior Walls – 1<sup>st</sup>
- . Install Blocking 1<sup>st</sup> Floor
- . Install Bench Brackets 2<sup>nd</sup> Floor
- . Continue Sprinkler Rough 1<sup>st</sup> Floor
- . Insulate Duct 2<sup>nd</sup> Floor

#### Next Week – Activities

- . Continue Shingle Siding Installation
- . Continue 2<sup>nd</sup> Floor Mud and Tape
- . Continue 2<sup>nd</sup> Floor Duct insulation
- . Continue 2<sup>nd</sup> Floor Control Wiring
- . Measure for Alum. Frames/Glass -2<sup>nd</sup> Floor
- . Measure for Storefront
- . Continue Main Electric Room Build Out
- . Continue Insulation and Poly 1<sup>st</sup> Floor
- . Install Drywall 1<sup>st</sup> Floor
- . Continue 1<sup>st</sup> Floor Sprinkler Installation
- . Paint Mechanical Room
- . Begin Mechanical Room Build Out
- . Continue Tel/Data Rough 2<sup>nd</sup> Floor

<b>Subcontractor</b>	<b>Trade</b>	<b># of Workers Onsite</b>
<b>Color Concepts</b>	<b>Painting</b>	<b>00</b>
<b>Titan Contractors Inc.</b>	<b>Site Work</b>	<b>01</b>
<b>Carlisle</b>	<b>Fire Protection</b>	<b>02</b>
<b>Marmello</b>	<b>Masonry</b>	<b>00</b>
<b>Griffin Electric</b>	<b>Electrical</b>	<b>05</b>
<b>General Insulation</b>	<b>Insulator</b>	<b>03</b>
<b>Colantonio Inc.</b>	<b>Carpenter</b>	<b>05</b>
<b>United Site Services</b>	<b>Site Sanitary</b>	<b>01</b>
<b>Colony Drywall</b>	<b>Framing</b>	<b>07</b>
<b>Colantonio</b>	<b>Labor</b>	<b>01</b>
<b>LaPan Mechanical</b>	<b>Plumbing</b>	<b>02</b>
<b>Division 15</b>	<b>HVAC</b>	<b>05</b>
<b>BKA</b>	<b>Architect</b>	<b>02</b>
<b>Daedalus</b>	<b>Owner Representative</b>	<b>02</b>
<b>Colantonio Inc.</b>	<b>Construction Manager</b>	<b>03</b>
<b>TOTAL # Onsite This Week</b>		<b>39</b>

### **Safety**

- **Safety Orientation for New Jobsite Workers Performed First Day of Work. Total Number of Onsite Workers/Visitors Orientated = 115**
- **All Workers Wear Proper PPE At All Times**
- **Fencing and Scrim Reviewed Each Week for Safety and Appearance**
- **Weekly Toolbox Talks are Conducted Within Each Trade And a Copy is Submitted to Colantonio Inc.**
- **Each Contractor Completes a Daily Work Report which Is Kept On File**
- **Construction Progress Meeting are Held Tuesday at 1PM.**
- **174 Days With Zero Worker Accident**
- **174 Days Without a Lost Time Accident**

### **Quality Control**

- **Materials Delivered To The Site Cross Referenced Against Drawings, Submittals and Specifications prior to installation.**
- **Colantonio Inc and Subcontractor Review of Drawings and Specification Compliance Prior to Work Commencing**
- **154 Random Quality Control Inspection Reports have been completed, of those: 02 remain as “Open” and “Non-Conforming”**

### **Miscellaneous**

- **No Parking During Construction Time Posted on Bradford Avenue**
- **Colantonio Inc. subcontractor meeting to be held on Tuesdays at 10AM**
- **Workers Utilizing Deb Sampson Parking Lot**
- **Tel/Data Coordination Meeting Thursday at 1PM.**





**2<sup>nd</sup> Floor Drywall**



**Mud/Tape 2<sup>nd</sup> Floor**



**2<sup>nd</sup> Floor Soffit Framing**




**Meeting Room**





**Drain Pipe Insulation**

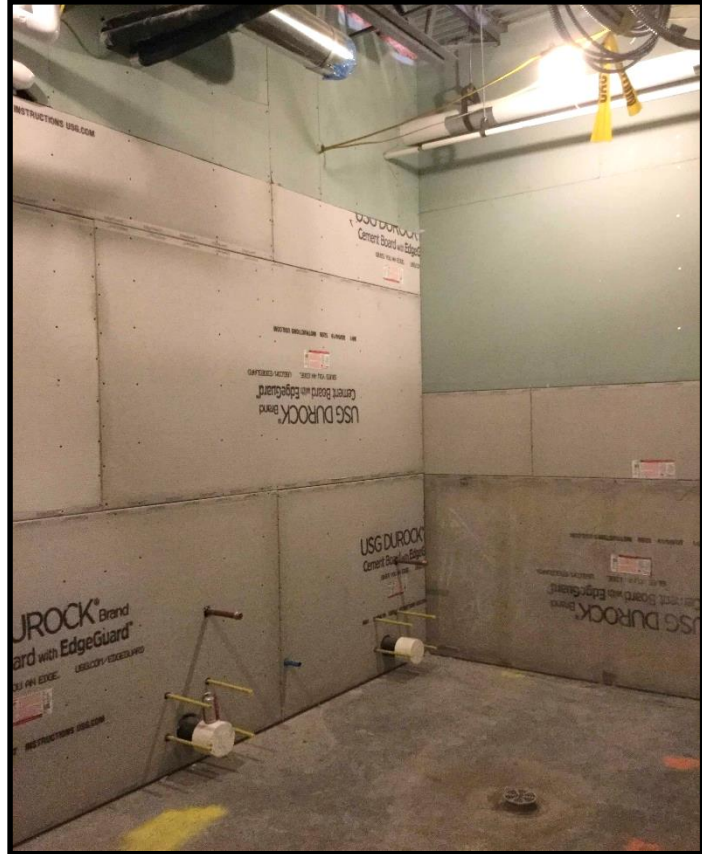

**Bathroom Durock**



**Septic Tank Backfill**



**West Elevation Siding**
