

Sharon Town Hall Sharon, MA



COLANTONIO INC.
PROJECT # 18-3835

BKA

ARCHITECTS



DAEDALUS

samiotes

ARCHITECTURAL
ENGINEERS

TRAVERSE
landscape architects

The Sharon Standing Building Committee

COLANTONIO
40 YEARS OF BUILDING RELATIONSHIPS

Weekly Activity Update

Friday April 26, 2019 Report #31

Current Week – Activities

- . Continue 1st Floor Drywall Install
- . Insulate, Poly and Board Stair #2
- . Insulate, Poly and Board Stair #1
- . Tel/Data Cable Rough Both Floors
- . Insulate Ductwork 2nd Floor
- . 2nd Coat and Begin 3rd Coat Drywall Mud
- . Install Ductwork 1st Floor
- . Continue Sprinkler Branch Lines 1st Floor
- . Build Out Main Electric Room
- . Begin Mechanical Room Rough
- . Install Acoustical Spray 2nd Floor
- . Install Smoke Barrier Spray 2nd Floor
- . Continue Shingle Siding – North
- . Install Column Wrap Blocking – South
- . Assemble Cupola Railings
- . Paint Mechanical and Network Rooms
- . Install Heat Pumps 2nd Floor
- . Field Measure Interior Aluminum Frames
- . Gas Line Markings Installed Bradford

Next Week – Activities

- . Continue Shingle Siding Installation
- . Finish Coat and Sand 2nd Floor Drywall
- . Begin Prime/Paint 2nd Floor
- . Begin 1st Coat Mud and Tape 1st Floor
- . Continue Drywall Installation Stair #2
- . Continue Drywall Install Stair #1
- . Install Spray Foam Stair #2
- . Begin Installation of Roof Metal
- . Continue Heat Pump Installation
- . Continue Main Electric Room Build Out
- . Begin Fire Alarm Build Out
- . Install Durock – 1st Floor Bathrooms
- . Tel/Data Coordination Meeting
- . Continue Meeting Room Build Out
- . Continue Control Wiring Installation
- . Continue Mechanical Piping Installation

| Subcontractor | Trade | # of Workers Onsite |
|---------------------------------|-----------------------------|----------------------------|
| Color Concepts | Painting | 02 |
| Titan Contractors Inc. | Site Work | 00 |
| Carlysle | Fire Protection | 02 |
| Marmello | Masonry | 00 |
| Griffin Electric | Electrical | 06 |
| General Insulation | Insulator | 00 |
| Colantonio Inc. | Carpenter | 05 |
| United Site Services | Site Sanitary | 01 |
| Colony Drywall | Framing | 09 |
| Colantonio | Labor | 01 |
| LaPan Mechanical | Plumbing | 02 |
| Division 15 | HVAC | 04 |
| Delta Beckwith | Elevator | 01 |
| Alum/Glass Concepts | Aluminum Openings | 01 |
| | | |
| | | |
| | | |
| | | |
| | | |
| | | |
| | | |
| | | |
| BKA | Architect | 02 |
| Daedalus | Owner Representative | 02 |
| Colantonio Inc. | Construction Manager | 03 |
| TOTAL # Onsite This Week | | 41 |

Safety

- **Safety Orientation for New Jobsite Workers Performed First Day of Work. Total Number of Onsite Workers/Visitors Orientated = 114**
- **All Workers Wear Proper PPE At All Times**
- **Fencing and Scrim Reviewed Each Week for Safety and Appearance**
- **Weekly Toolbox Talks are Conducted Within Each Trade And a Copy is Submitted to Colantonio Inc.**
- **Each Contractor Completes a Daily Work Report which Is Kept On File**
- **Construction Progress Meeting are Held Tuesday at 1PM.**
- **179 Days With Zero Worker Accident**
- **179 Days Without a Lost Time Accident**

Quality Control

- **Materials Delivered To The Site Cross Referenced Against Drawings, Submittals and Specifications prior to installation.**
- **Colantonio Inc and Subcontractor Review of Drawings and Specification Compliance Prior to Work Commencing**
- **160 Random Quality Control Inspection Reports have been completed, of those: 023 remain as “Open” and “Non-Conforming”**

Miscellaneous

- **No Parking During Construction Time Posted on Bradford Avenue**
- **Colantonio Inc. subcontractor meeting to be held on Tuesdays at 10AM**
- **Workers Utilizing Bradford Avenue due to carnival**
- **Tel/Data Coordination Meeting Tuesday April 30th at 1PM.**



South Lower Canopy




West Elevation



2nd Floor Bench Area



Main Electric Room Build out

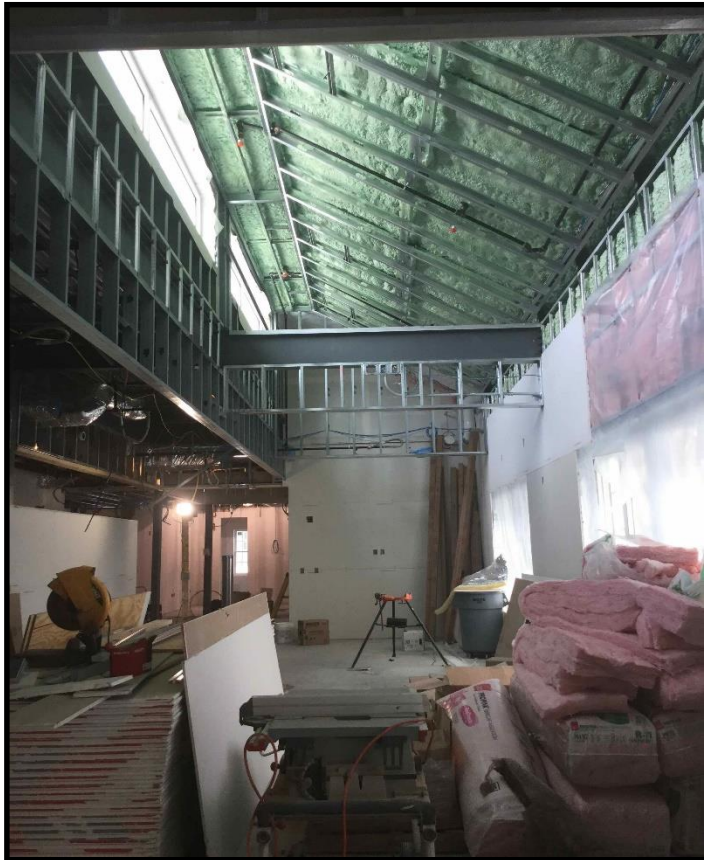

Meeting Room – 2nd Floor



Mechanical Piping



2nd Floor Bathroom



1st Floor Drywall
