

# Sharon Town Hall Sharon, MA



**COLANTONIO INC.**  
**PROJECT # 18-3835**

**BKA**

ARCHITECTS



**DAEDALUS**

**samiotes**

ARCHITECTURAL  
**ENGINEERS**

**TRAVERSE**  
landscape architects

## The Sharon Standing Building Committee

**COLANTONIO**  
40 YEARS OF BUILDING RELATIONSHIPS

### Weekly Activity Update

Friday May 10, 2019 Report #33

#### Current Week – Activities

- . Continue Mud/Tape – 2<sup>nd</sup> Floor
- . Install Meeting Room Walls/Ceilings
- . Prime/Paint Walls – 2<sup>nd</sup> Floor
- . Install ACT Ceilings – 2<sup>nd</sup> Floor
- . Frame Stair #1 Ceiling
- . Rough MEP Stair #1 Ceiling
- . Install Sprinkler Drops – 2<sup>nd</sup> Floor
- . Lighting Rough 2<sup>nd</sup> Floor
- . Mechanical Rough 2<sup>nd</sup> Floor
- . Layout Roof Top Condensers
- . Install Cupola Metal and Rails
- . Install Gutter Metal
- . Install Drywall – 1<sup>st</sup> Floor
- . Mud/Tape Walls – 1<sup>st</sup> Floor
- . Finish Sand Vault Walls and Ceilings
- . Prime/Paint Vault Walls and Ceiling
- . Continue Shingle Siding South Elevation
- . Set Eversource Transformer

#### Next Week – Activities

- . Continue Prime/Paint Walls – 2<sup>nd</sup> Floor
- . Continue ACT Ceilings – 2<sup>nd</sup> Floor
- . Mud/Tape/Sand – 2<sup>nd</sup> Floor Walls
- . Condenser Penetrations – Flat Roof
- . Install Sprinkler Heads – 2<sup>nd</sup> Floor
- . Mud/Tape Stair 1 and Stair 2
- . Install Entrance Windows and Trim
- . Continue Mud/Tape 1<sup>st</sup> Floor Walls
- . Deliver Elevator, Controller and Frames
- . Continue Heat Pump Install – 1<sup>st</sup> Floor
- . Excavate and Install Comcast Piping
- . Strip Curbing East
- . Prep Sidewalks and Grade North West
- . Set Transformer Meter Supports
- . Pull Secondaries to Transformer

<b>Subcontractor</b>	<b>Trade</b>	<b># of Workers Onsite</b>
<b>Color Concepts</b>	<b>Painting</b>	<b>01</b>
<b>Titan Contractors Inc.</b>	<b>Site Work</b>	<b>01</b>
<b>Carlisle</b>	<b>Fire Protection</b>	<b>02</b>
<b>Marmello</b>	<b>Masonry</b>	<b>02</b>
<b>Griffin Electric</b>	<b>Electrical</b>	<b>05</b>
<b>General Insulation</b>	<b>Insulator</b>	<b>00</b>
<b>Colantonio Inc.</b>	<b>Carpenter</b>	<b>05</b>
<b>United Site Services</b>	<b>Site Sanitary</b>	<b>01</b>
<b>Colony Drywall</b>	<b>Framing</b>	<b>09</b>
<b>Colantonio</b>	<b>Labor</b>	<b>01</b>
<b>LaPan Mechanical</b>	<b>Plumbing</b>	<b>00</b>
<b>Division 15</b>	<b>HVAC</b>	<b>05</b>
<b>Delta Beckwith</b>	<b>Elevator</b>	<b>01</b>
<b>Alum/Glass Concepts</b>	<b>Aluminum Openings</b>	<b>00</b>
<b>Greenwood</b>	<b>Roofing</b>	<b>04</b>
<b>Cheviot</b>	<b>Ceilings</b>	<b>02</b>
<b>BKA</b>	<b>Architect</b>	<b>02</b>
<b>Daedalus</b>	<b>Owner Representative</b>	<b>02</b>
<b>Colantonio Inc.</b>	<b>Construction Manager</b>	<b>03</b>
<b>TOTAL # Onsite This Week</b>		<b>46</b>

### **Safety**

- **Safety Orientation for New Jobsite Workers Performed First Day of Work. Total Number of Onsite Workers/Visitors Orientated = 123**
- **All Workers Wear Proper PPE At All Times**
- **Fencing and Scrim Reviewed Each Week for Safety and Appearance**
- **Weekly Toolbox Talks are Conducted Within Each Trade And a Copy is Submitted to Colantonio Inc.**
- **Each Contractor Completes a Daily Work Report which Is Kept On File**
- **Construction Progress Meeting are Held Tuesday at 1PM.**
- **189 Days With Zero Worker Accident**
- **189 Days Without a Lost Time Accident**

### **Quality Control**

- **Materials Delivered To The Site Cross Referenced Against Drawings, Submittals and Specifications prior to installation.**
- **Colantonio Inc and Subcontractor Review of Drawings and Specification Compliance Prior to Work Commencing**
- **170 Random Quality Control Inspection Reports have been completed, of those: 02 remain as “Open” and “Non-Conforming”**

### **Miscellaneous**

- **Colantonio Inc. subcontractor meeting to be held on Tuesdays at 10AM**
- **Controls Integration Meeting – Tuesday May 14, 2019 12PM**
-






**Second Floor Meeting Room**



**Second Floor Meeting Room**

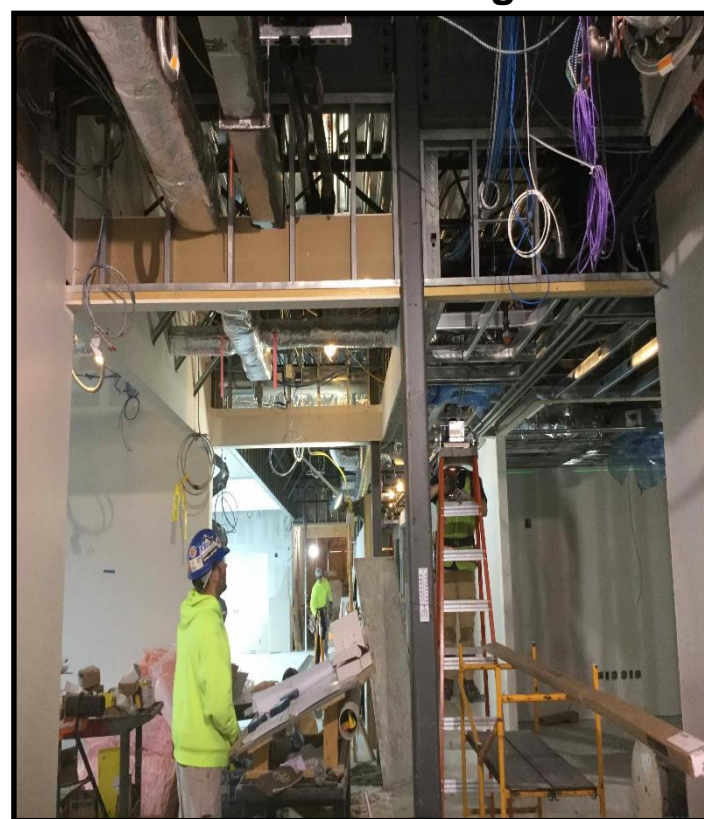

**Lighting Layout**



**First Floor MEP Rough**






**Cupola Railings**



**Vault Interior Walls**



**Ceiling Grid Installation**

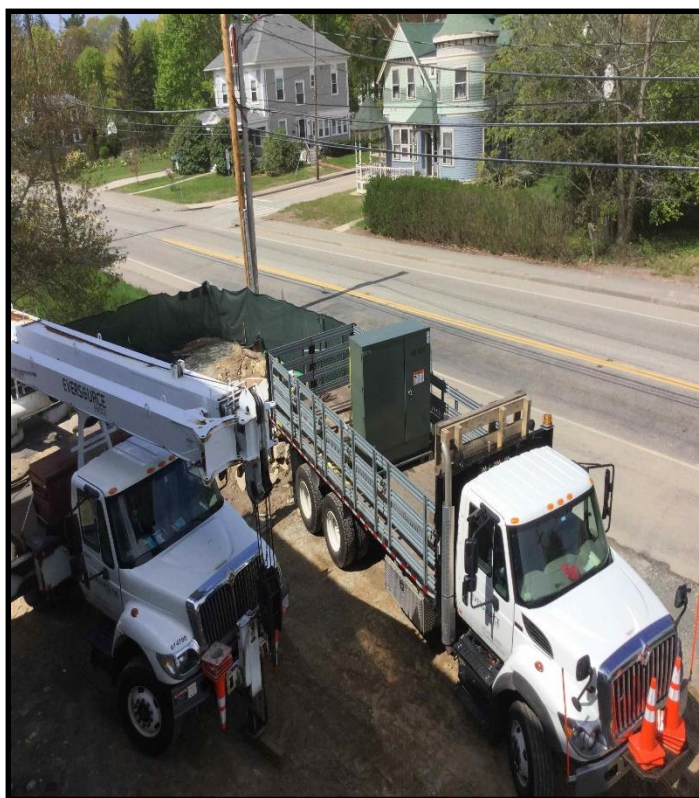

**Transformer Delivery**
