

Sharon Town Hall Sharon, MA



COLANTONIO INC.
PROJECT # 18-3835

BJA

ARCHITECTS



DAEDALUS

samiotes



ARCHITECTURAL
ENGINEERS

TRAVERSE
landscape architects

The Sharon Standing Building Committee

COLANTONIO
40 YEARS OF BUILDING RELATIONSHIPS

Weekly Activity Update

Friday May 24, 2019 Report #35

Current Week – Activities

- . Final Coat and Sand – 1st Floor
- . Second Coat Stair #1
- . Hoist ERV and ACCU 1 and 2
- . Mech/Elec Rough to Roof Top Units
- . Install Low Roof Edge Metal
- . Install Entrance Windows
- . Caulk Windows Exterior
- . Caulk Clerestory Windows
- . Inspection of Secondary Feeders
- . Inspection of Meter Socket
- . Subgrade for South Sidewalk
- . Subgrade for Dumpster/Generator Pad
- . Paint Meeting Room Ceiling and Walls
- . Install Ceiling Grid – 2nd Floor
- . Deliver Elevator Equipment
- . Deliver and Install Coiling Doors
- . Install Floor and Wall Tile – 2nd Floor
- . Install Electrical Devices – 2nd Floor
- . Prime/ Paint Door Frames

Next Week – Activities

- . Continue Prime/Paint Walls – 2nd Floor
- . Continue Prime/Paint Walls – 1st Floor
- . Continue ACT Grid – 2nd Floor
- . Begin ACT Grid - 1st Floor
- . Mud/Sand Stair #1
- . Sand Walls 1st Floor
- . Install Sprinkler Heads – ACT Ceiling
- . Install Coiling Doors
- . Install Low Roof Railing System
- . Mech/Elec Rough Roof Top Units
- . Begin Elevator Installation
- . Continue Subgrade for Dumpster Pad
- . Caulk Interior Windows and Doors
- . Caulk Exterior Siding
- . Install Shelving Rails – Vaults
- . Continue Fire Suppression install – Vaults
- . Continue Floor and Wall Tile

Subcontractor	Trade	# of Workers Onsite
Color Concepts	Painting	01
Titan Contractors Inc.	Site Work	02
Carlisle	Fire Protection	04
Marmello	Masonry	00
Griffin Electric	Electrical	05
General Insulation	Insulator	00
Colantonio Inc.	Carpenter	04
United Site Services	Site Sanitary	01
Colony Drywall	Framing	05
Colantonio	Labor	01
LaPan Mechanical	Plumbing	00
Division 15	HVAC	07
Delta Beckwith	Elevator	02
Alum/Glass Concepts	Aluminum Openings	00
Greenwood	Roofing	04
Cheviot	Ceilings	02
Superior	Caulking	03
BKA	Architect	02
Daedalus	Owner Representative	02
Colantonio Inc.	Construction Manager	03
TOTAL # Onsite This Week		48

Safety

- **Safety Orientation for New Jobsite Workers Performed First Day of Work. Total Number of Onsite Workers/Visitors Orientated = 123**
- **All Workers Wear Proper PPE At All Times**
- **Fencing and Scrim Reviewed Each Week for Safety and Appearance**
- **Weekly Toolbox Talks are Conducted Within Each Trade And a Copy is Submitted to Colantonio Inc.**
- **Each Contractor Completes a Daily Work Report which Is Kept On File**
- **Construction Progress Meeting are Held Tuesday at 1PM.**
- **199 Days With Zero Worker Accident**
- **199 Days Without a Lost Time Accident**

Quality Control

- **Materials Delivered To The Site Cross Referenced Against Drawings, Submittals and Specifications prior to installation.**
- **Colantonio Inc and Subcontractor Review of Drawings and Specification Compliance Prior to Work Commencing**
- **175 Random Quality Control Inspection Reports have been completed, of those: 02 remain as “Open” and “Non-Conforming”**

Miscellaneous

- **Colantonio Inc. subcontractor meeting to be held on Tuesdays at 11AM**
- **Wiring Inspection of Transformer Secondaries Completed**
- **Gas Service Street Opening Permit Released – No Date as of Yet**
- **Access Gate Relocation on Bradford Avenue – Week of 27th**




ERV Placement



Mech/Elec Rough




Floor Tile Installation

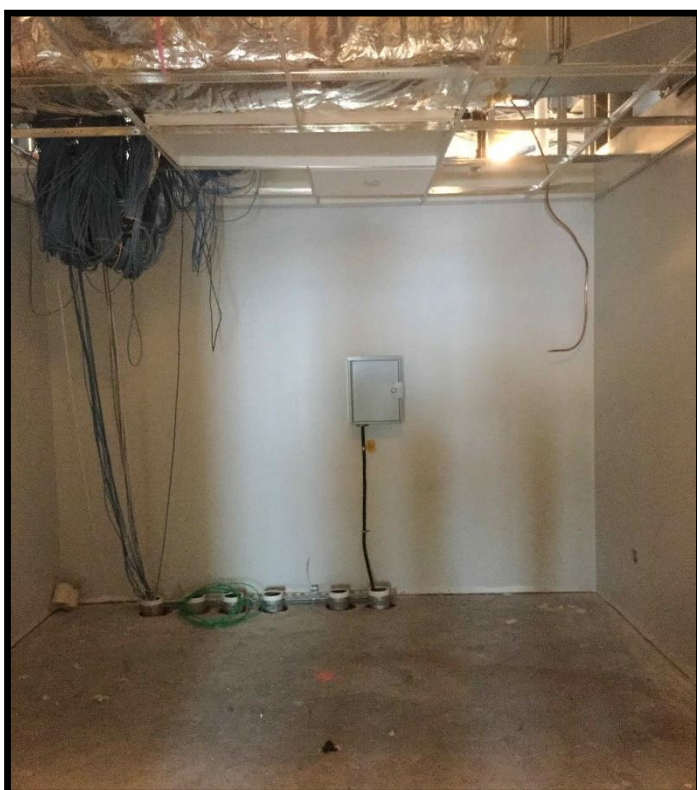

Comcast Installation



Fire Suppression Rough

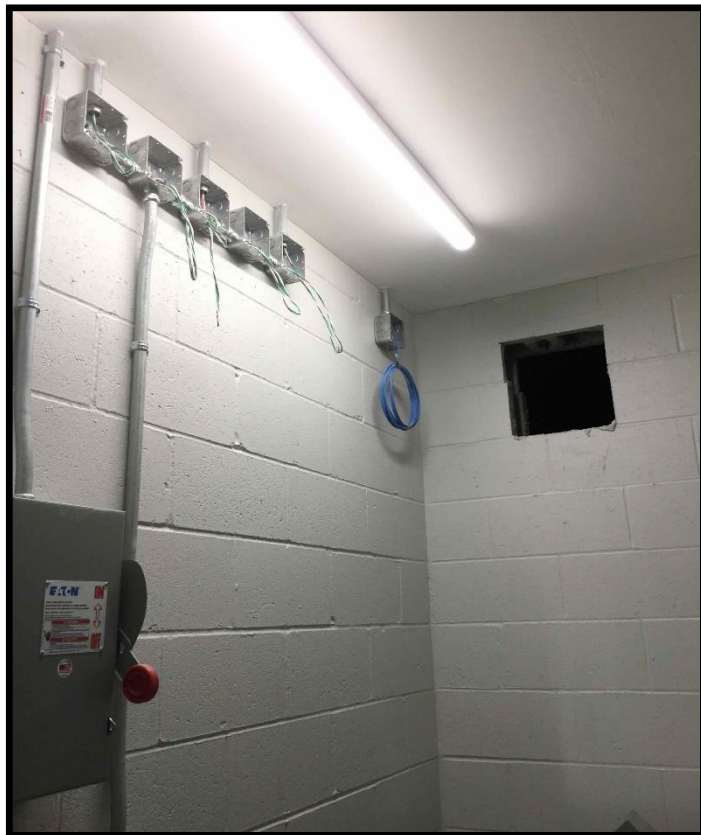

Elevator Machine Room



Meeting Room Finishes



Coiling Door Installation
