

# Sharon Town Hall Sharon, MA



**COLANTONIO INC.**  
**PROJECT # 18-3835**

**BKA**

ARCHITECTS



**DAEDALUS**

**samiotes**

ARCHITECTURAL  
**ENGINEERS**

**TRAVERSE**  
landscape architects

## The Sharon Standing Building Committee

**COLANTONIO**  
40 YEARS OF BUILDING RELATIONSHIPS

### Weekly Activity Update

Friday June 7, 2019 Report #36

#### Current Week – Activities

- . Final Coat and Sand – 1<sup>st</sup> Floor
- . Prime Paint – 1<sup>st</sup> Floor Walls
- . Paint Accent Walls – 2<sup>nd</sup> Floor
- . Receive Millwork and Countertops
- . Begin Millwork Install
- . Continue Ceiling Grid Installation
- . Continue Lighting Installation
- . Continue Elevator Installation
- . Install Elevator Doors and Controls
- . Continue Tile and Grout Bathrooms
- . Begin Excavation for Septic/Leach Field
- . Inspection of Excavation Depth
- . Receive Exterior Granite Blocks
- . Continue Entrance Framing
- . Begin East Elevation Window and Siding
- . Form and Place South Sidewalks
- . Begin Column Wraps South Sidewalk
- . Continue Heat Pump Install 1<sup>st</sup> Floor
- . Continue Fire Suppression Install - Vaults

#### Next Week – Activities

- . Continue Prime/Paint Walls – 2<sup>nd</sup> Floor
- . Continue Prime/Paint Walls – 1<sup>st</sup> Floor
- . Continue ACT Grid – 2<sup>nd</sup> Floor
- . Begin ACT Grid - 1<sup>st</sup> Floor
- . Prime/Paint Stair #2
- . Continue Elevator Installation
- . Continue Septic/Leach Field
- . Begin Installation of Granite Blocks
- . Continue Millwork – 2<sup>nd</sup> Floor
- . Continue East Elevation Siding
- . Excavate for Gas Service
- . Gas Service Installation
- . Install Water Heater – 1<sup>st</sup> Floor
- . Receive Bathroom Finishes – 2<sup>nd</sup> Floor
- . Continue Electric Devices – 1<sup>st</sup> Floor
- . Begin Installation of Aluminum Track

<b>Subcontractor</b>	<b>Trade</b>	<b># of Workers Onsite</b>
<b>Color Concepts</b>	<b>Painting</b>	<b>01</b>
<b>Titan Contractors Inc.</b>	<b>Site Work</b>	<b>03</b>
<b>Carlysle</b>	<b>Fire Protection</b>	<b>02</b>
<b>Marmello</b>	<b>Masonry</b>	<b>01</b>
<b>Griffin Electric</b>	<b>Electrical</b>	<b>02</b>
<b>General Insulation</b>	<b>Insulator</b>	<b>00</b>
<b>Colantonio Inc.</b>	<b>Carpenter</b>	<b>02</b>
<b>United Site Services</b>	<b>Site Sanitary</b>	<b>01</b>
<b>Colony Drywall</b>	<b>Framing</b>	<b>04</b>
<b>Colantonio</b>	<b>Labor</b>	<b>01</b>
<b>LaPan Mechanical</b>	<b>Plumbing</b>	<b>01</b>
<b>Division 15</b>	<b>HVAC</b>	<b>04</b>
<b>Delta Beckwith</b>	<b>Elevator</b>	<b>02</b>
<b>Alum/Glass Concepts</b>	<b>Aluminum Openings</b>	<b>00</b>
<b>Greenwood</b>	<b>Roofing</b>	<b>01</b>
<b>Cheviot</b>	<b>Ceilings</b>	<b>01</b>
<b>Superior</b>	<b>Caulking</b>	<b>00</b>
<b>Capital Carpet</b>	<b>Tile</b>	<b>03</b>
<b>A.P. Dailey</b>	<b>Millwork</b>	<b>01</b>
<b>Federal</b>	<b>Concrete</b>	<b>06</b>
<b>BJA</b>	<b>Architect</b>	<b>02</b>
<b>Daedalus</b>	<b>Owner Representative</b>	<b>02</b>
<b>Colantonio Inc.</b>	<b>Construction Manager</b>	<b>03</b>
<b>TOTAL # Onsite This Week</b>		<b>43</b>

### **Safety**

- **Safety Orientation for New Jobsite Workers Performed First Day of Work. Total Number of Onsite Workers/Visitors Orientated = 123**
- **All Workers Wear Proper PPE At All Times**
- **Fencing and Scrim Reviewed Each Week for Safety and Appearance**
- **Weekly Toolbox Talks are Conducted Within Each Trade And a Copy is Submitted to Colantonio Inc.**
- **Each Contractor Completes a Daily Work Report which Is Kept On File**
- **Construction Progress Meeting are Held Tuesday at 1PM.**
- **209 Days With Zero Worker Accident**
- **209 Days Without a Lost Time Accident**

### **Quality Control**

- **Materials Delivered To The Site Cross Referenced Against Drawings, Submittals and Specifications prior to installation.**
- **Colantonio Inc and Subcontractor Review of Drawings and Specification Compliance Prior to Work Commencing**
- **175 Random Quality Control Inspection Reports have been completed, of those: 02 remain as “Open” and “Non-Conforming”**

### **Miscellaneous**

- **Colantonio Inc. subcontractor meeting to be held on Tuesdays at 11AM**
- **Eversource On Site June 8<sup>th</sup> for Roadside Work**
- **Gas Service Street Opening Permit Released – Week of June 10<sup>th</sup>**
- **Generator Relocation – Friday June 21<sup>st</sup> at 12PM**
- **Excavated Soils Dumpster Hauled Off Site**






**Millwork Installation**



**Millwork Installation**

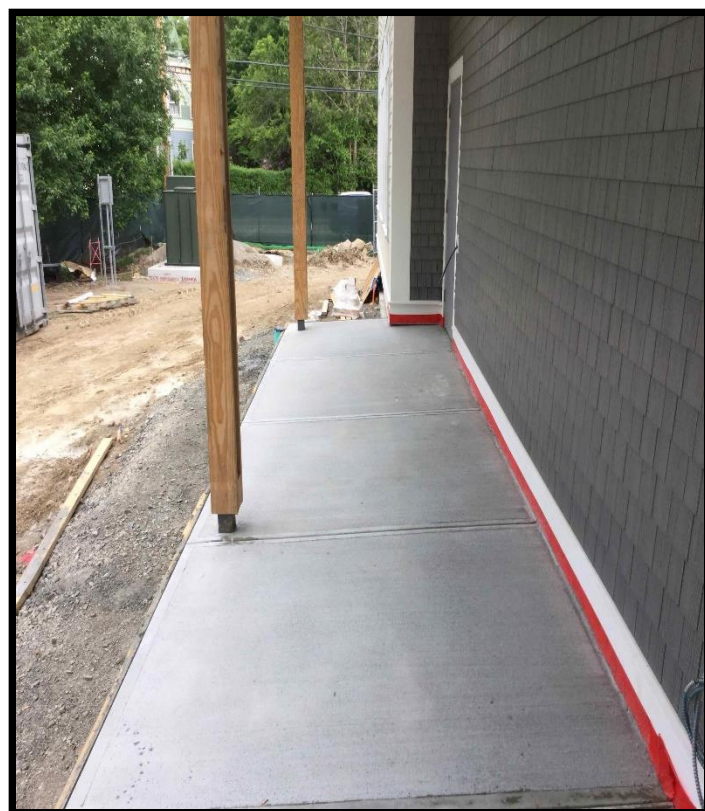

**Sidewalk Installation**



**Generator Pad**






**Leech Field**



**Leech Field**



**Exterior Granite Delivery**

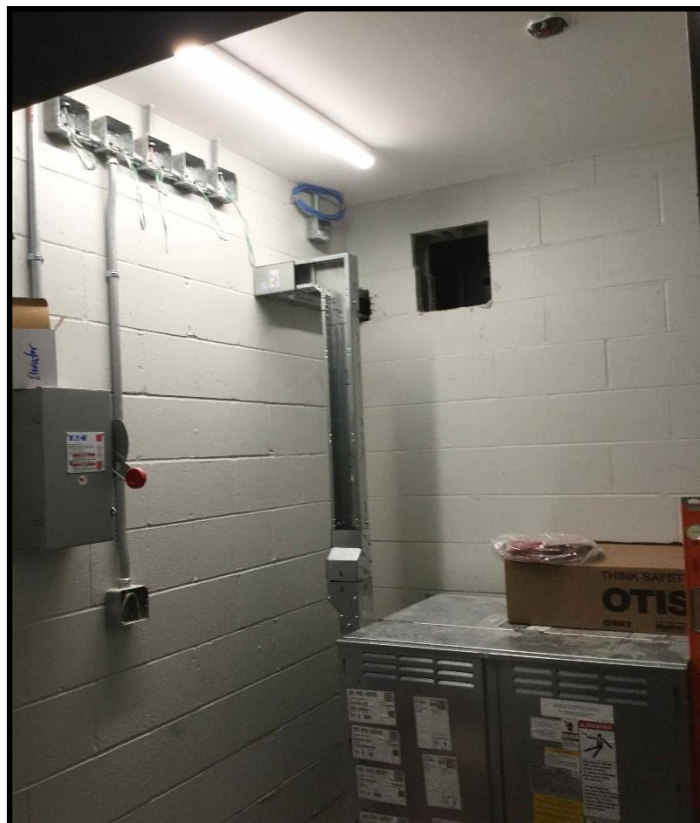

**Elevator Machine Room**
