

Sharon Town Hall Sharon, MA



COLANTONIO INC.
PROJECT # 18-3835

BKA

ARCHITECTS



DAEDALUS

samiotes

ARCHITECTURAL
ENGINEERS

TRAVERSE
landscape architects

The Sharon Standing Building Committee

COLANTONIO
40 YEARS OF BUILDING RELATIONSHIPS

Weekly Activity Update

Friday June 21, 2019 Report #38

Current Week – Activities

- . Continue Septic Leech Field
- . Install Granite
- . Install Window – East Elevation
- . Install Shingle Siding – East Elevation
- . Caulk Exterior Corner Boards
- . Relocate Generator
- . Install Lighting – 1st Floor
- . Install Lighting – 2nd floor
- . Continue Ceiling Grid – 2nd Floor
- . Continue Ceiling Grid – 1st Floor
- . Continue Mill work – 2nd Floor
- . Install Bathroom Counters and Sinks
- . Continue Prime/Paint 1st Floor
- . Begin Meeting Room Frame/Glass
- . Continue Network Rack Install
- . Install Mop Sinks and FRP
- . Complete Mechanical Piping – 2nd Floor
- . Complete ERV Tie In
- . Install Interior Window Sills

Next Week – Activities

- . Continue Prime/Paint Walls- 1st Floor
- . Complete Septic Leech Field
- . Continue Granite
- . Complete Exterior Corner Board Caulk
- . Continue Mechanical Piping – 1st Floor
- . Install Z- Mesh Conduit and Wiring
- . Above Ceiling Inspection
- . Install Ceiling Tile Cuts
- . Install Grilles and Diffusers
- . Continue Lighting Install
- . Complete Tile Installation – Bathrooms
- . Continue Interior Window Sill Install
- . Install Underground Gas Line
- . Grade Entrance and Sidewalks
- . Begin Mechanical Roof Piping
- . Permanent Power*
- . Continue Ceiling Grid 1st Floor

Subcontractor	Trade	# of Workers Onsite
Color Concepts	Painting	01
Titan Contractors Inc.	Site Work	02
Carlysle	Fire Protection	02
Marmello	Masonry	05
Griffin Electric	Electrical	07
General Insulation	Insulator	00
Colantonio Inc.	Carpenter	05
United Site Services	Site Sanitary	01
Colony Drywall	Framing	02
Colantonio	Labor	01
LaPan Mechanical	Plumbing	02
Division 15	HVAC	05
Delta Beckwith	Elevator	02
Alum/Glass Concepts	Aluminum Openings	03
Greenwood	Roofing	03
Cheviot	Ceilings	03
Superior	Caulking	00
Capital Carpet	Tile	00
A.P. Dailey	Millwork	01
BJA	Architect	02
Daedalus	Owner Representative	01
Colantonio Inc.	Construction Manager	03
TOTAL # Onsite This Week		51

Safety

- **Safety Orientation for New Jobsite Workers Performed First Day of Work. Total Number of Onsite Workers/Visitors Orientated = 127**
- **All Workers Wear Proper PPE At All Times**
- **Fencing and Scrim Reviewed Each Week for Safety and Appearance**
- **Weekly Toolbox Talks are Conducted Within Each Trade And a Copy is Submitted to Colantonio Inc.**
- **Each Contractor Completes a Daily Work Report which Is Kept On File**
- **Construction Progress Meeting are Held Tuesday at 1PM.**
- **219 Days With Zero Worker Accident**
- **219 Days Without a Lost Time Accident**

Quality Control

- **Materials Delivered To The Site Cross Referenced Against Drawings, Submittals and Specifications prior to installation.**
- **Colantonio Inc and Subcontractor Review of Drawings and Specification Compliance Prior to Work Commencing**
- **186 Random Quality Control Inspection Reports have been completed, of those: 02 remain as “Open” and “Non-Conforming”**

Miscellaneous

- **Colantonio Inc. subcontractor meeting held on Tuesdays at 11AM**
- **Colantonio Inc. in contact with Columbia Gas for Underground service**
- **Primary Electric Wires Connected at the Utility Pole**
- **Emergency Generator Relocation Complete**



Septic Leech Field



Meeting Room Glass



1st Floor Elevator Door




Millwork Installation



Generator Relocation



Granite Blocks

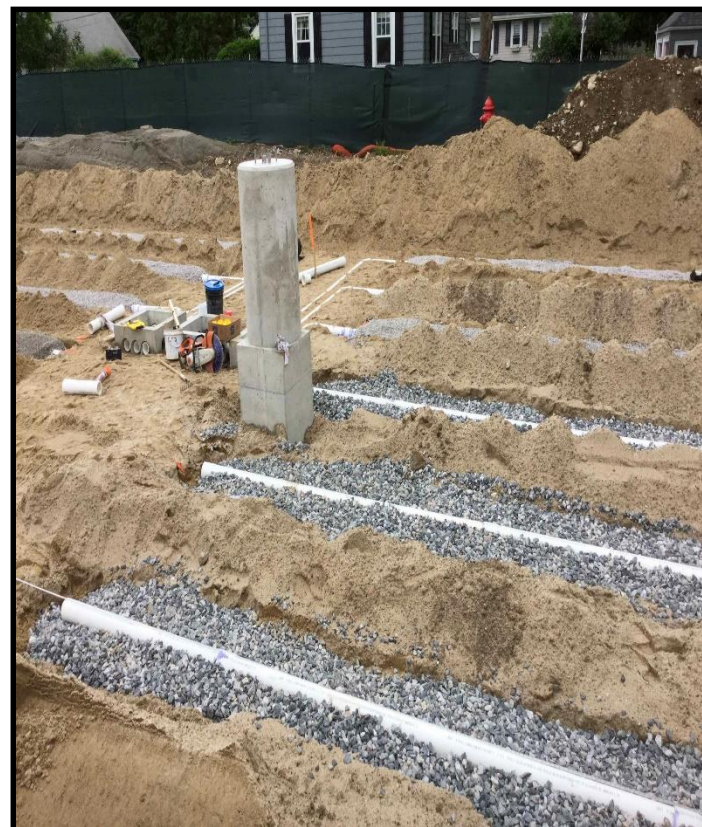

Light Pole Base Install



Meeting Room Lights
