

Sharon Town Hall Sharon, MA



COLANTONIO INC.
PROJECT # 18-3835

BKA

ARCHITECTS



DAEDALUS

samiotes

ARCHITECTURAL
ENGINEERS

TRAVERSE
landscape architects

The Sharon Standing Building Committee

COLANTONIO
40 YEARS OF BUILDING RELATIONSHIPS

Weekly Activity Update

Sunday August 04, 2019 Report #44

Current Week – Activities

- . Continue 1st Floor Carpet Tile
- . Template remaining Quartz Countertops
- . Complete Wood Ceilings
- . Install Window Shades
- . Install Gas Meter
- . Connect Generator Gas Feed and Inspect
- . Final Wiring Inspection – Building
- . Install Door Hardware – 1st Floor
- . Install South Column Enclosures
- . Finish Paint Patio Ceiling
- . Final Grade Parking Lot and Sidewalk
- . Place East Sidewalk
- . Install Asphalt Binder Course
- . Install Parking Lot Lighting
- . Build Exterior Door Frames
- . Install Granite Curbing
- . Take Down Fencing – Bradford Avenue
- . Subgrade South Planting Area

Next Week – Activities

- . Grade South Plantings Area
- . Temporary Stripe of Parking Lot
- . Turn on Gas Service to Building
- . Life Safety Testing – Fire/Building
- . Remove Fencing South
- . Install Porch Column Enclosures
- . Install Entrance Frames and Doors
- . Complete Carpet Floor Tile
- . Install Stair 1 Nosing and Carpet
- . Install Stair 2 Treads and Risers
- . Install Glass and Frames 2nd Floor
- . Caulk Aluminum Frames – 2nd Floor
- . Install Vestibule Ceiling
- . Install Wood Panels – 2nd Floor
- . Complete Rubber Base – 2nd Floor
- . Install South Gutter Downspouts

Subcontractor	Trade	# of Workers Onsite
Color Concepts	Painting	01
Titan Contractors Inc.	Site Work	07
Carlysle	Fire Protection	01
Labidini	Landscape	03
Griffin Electric	Electrical	06
General Insulation	Insulator	01
Colantonio Inc.	Carpenter	04
United Site Services	Site Sanitary	01
Colony Drywall	Framing	01
Colantonio	Labor	01
LaPan Mechanical	Plumbing	01
Division 15	HVAC	02
Delta Beckwith	Elevator	01
Alum/Glass Concepts	Aluminum Openings	02
Federal	Concrete	04
Cheviot	Ceilings	02
Superior	Caulking	02
Capital Carpet	Tile	01
Pavilion Floor	Carpet Tile	02
Briggs	Testing	02
BJA	Architect	02
Daedalus	Owner Representative	02
Colantonio Inc.	Construction Manager	03
TOTAL # Onsite This Week		52

Safety

- **Safety Orientation for New Jobsite Workers Performed First Day of Work. Total Number of Onsite Workers/Visitors Orientated = 141**
- **All Workers Wear Proper PPE At All Times**
- **Fencing and Scrim Reviewed Each Week for Safety and Appearance**
- **Weekly Toolbox Talks are Conducted Within Each Trade And a Copy is Submitted to Colantonio Inc.**
- **Each Contractor Completes a Daily Work Report which Is Kept On File**
- **Construction Progress Meeting are Held Tuesday at 1PM.**
- **253 Days With Zero Worker Accident**
- **253 Days Without a Lost Time Accident**

Quality Control

- **Materials Delivered To The Site Cross Referenced Against Drawings, Submittals and Specifications prior to installation.**
- **Colantonio Inc and Subcontractor Review of Drawings and Specification Compliance Prior to Work Commencing**
- **210 Random Quality Control Inspection Reports have been completed, of those: 00 remain as “Open” and “Non-Conforming”**

Miscellaneous

- **Colantonio Inc. subcontractor meeting held on Tuesdays at 11AM**
- **Life Safety Testing and Inspection – Wednesday August 7th, 2019**
- **Testing and Balancing Report Submitted – August 2nd, 2019**
- **Gas Inspection August 1st, 2019**
- **Final Wiring Inspection – August 1st, 2019**
- **Trailer Removal August 14th, 2019**



Parking Lot Subgrade



Parking Lot Asphalt Binder




South Column Enclosures



Temporary Walk



Porch Finish Trim

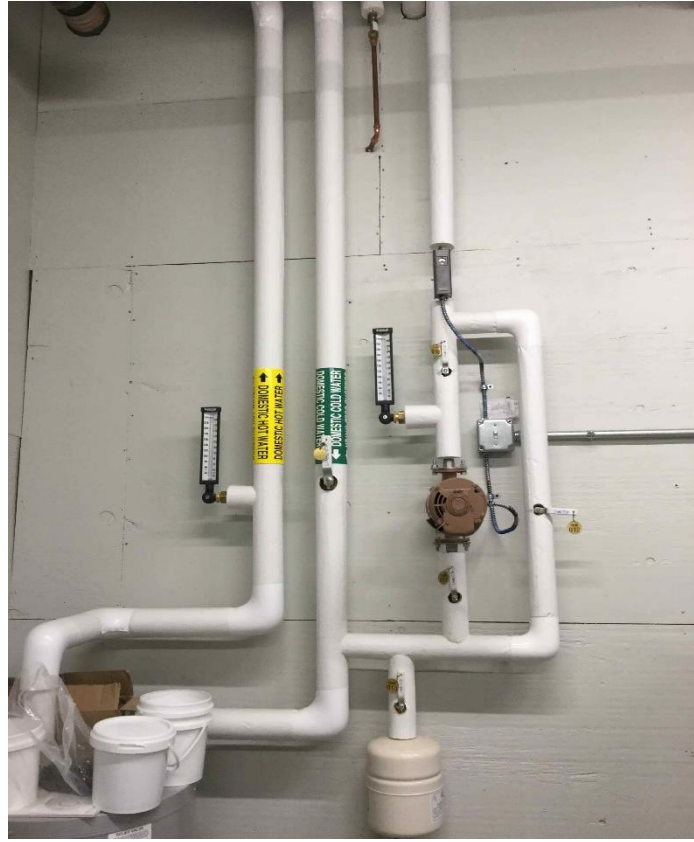

Valve Tags and Labels



Landscape Subgrade



Elevator Finishes
