

Sharon Town Hall Sharon, MA



COLANTONIO INC.
PROJECT # 18-3835

BAK

ARCHITECTS



samiotes

ARCHITECTURAL
ENGINEERS

TRAVERSE
landscape architects

The Sharon Standing Building Committee



Weekly Activity Update

Saturday August 10, 2019 Report #45

Current Week – Activities

- . Complete 1st Floor Carpet Tile
- . Install Vault Flooring
- . Install Rubber Base – 1st Floor
- . Install Rubber Treads – Stair #2
- . Install Rubber Nosings – Stair #1
- . Complete Fire Alarm Acceptance Test
- . Gas Service Turned On
- . Install Entrance Doors and Glass
- . Install Porch Railings
- . Continue Wood Panel Install – 2nd Floor
- . Install Wall Covering
- . Install Security Cameras and Readers
- . Install Angled Frame – Meeting Room
- . Install Glass Gasket – Both Floors
- . Adjust Elevator
- . Stripe Parking Lot
- . Remove South Fencing
- . Clean Windows – 2nd Floor
- . Install Office Glass Film

Next Week – Activities

- . Install Stair #1 Carpet
- . Install Vault Shelving
- . Install Quartz Countertops
- . Install Transaction Frames and Glass
- . Install Mirrors
- . Continue Wood Panels – 2nd Floor
- . Begin Wood Panels – 1st Floor
- . Caulk Frames – 1st and 2nd Floors
- . Touch Up Paint – 1st and 2nd Floors
- . Final Clean Seconds Floor
- . Clean Exterior Windows -1st Floor
- . Install Loam and South Landscaping
- . Generator Load Test
- . Continue Punch List
- . Remove Construction Trailers
- . Install Water Bubblers
- . Final plumbing Inspection

Subcontractor	Trade	# of Workers Onsite
Color Concepts	Painting	01
Titan Contractors Inc.	Site Work	03
Carlysle	Fire Protection	01
Labidini	Landscape	02
Griffin Electric	Electrical	05
General Insulation	Insulator	00
Colantonio Inc.	Carpenter	04
United Site Services	Site Sanitary	01
Colony Drywall	Framing	02
Colantonio	Labor	01
LaPan Mechanical	Plumbing	01
Division 15	HVAC	01
Delta Beckwith	Elevator	01
Alum/Glass Concepts	Aluminum Openings	04
Santangelo	Flooring	02
Cheviot	Ceilings	01
Superior	Caulking	00
Capital Carpet	Tile	00
Pavilion Floor	Carpet Tile	02
Briggs	Testing	00
BKA	Architect	02
Daedalus	Owner Representative	02
Colantonio Inc.	Construction Manager	03
TOTAL # Onsite This Week		39

Safety

- **Safety Orientation for New Jobsite Workers Performed First Day of Work. Total Number of Onsite Workers/Visitors Orientated = 143**
- **All Workers Wear Proper PPE At All Times**
- **Fencing and Scrim Reviewed Each Week for Safety and Appearance**
- **Weekly Toolbox Talks are Conducted Within Each Trade And a Copy is Submitted to Colantonio Inc.**
- **Each Contractor Completes a Daily Work Report which Is Kept On File**
- **Construction Progress Meeting are Held Tuesday at 1PM.**
- **259 Days With Zero Worker Accident**
- **259 Days Without a Lost Time Accident**

Quality Control


- **Materials Delivered To The Site Cross Referenced Against Drawings, Submittals and Specifications prior to installation.**
- **Colantonio Inc and Subcontractor Review of Drawings and Specification Compliance Prior to Work Commencing**
- **218 Random Quality Control Inspection Reports have been completed, of those: 02 remain as “Open” and “Non-Conforming”**

Miscellaneous

- **Colantonio Inc. subcontractor meeting held on Tuesdays at 11AM**
- **Generator Start Up and Load Test, August 16th, 2019**
- **Gas Service Turned On August 15th, 2019**
- **Trailer Removal August 14th, 2019**
- **Furniture Delivery August 19th, 2019**
- **Fencing Relocation August 22nd, 2019**




North Porch Railings

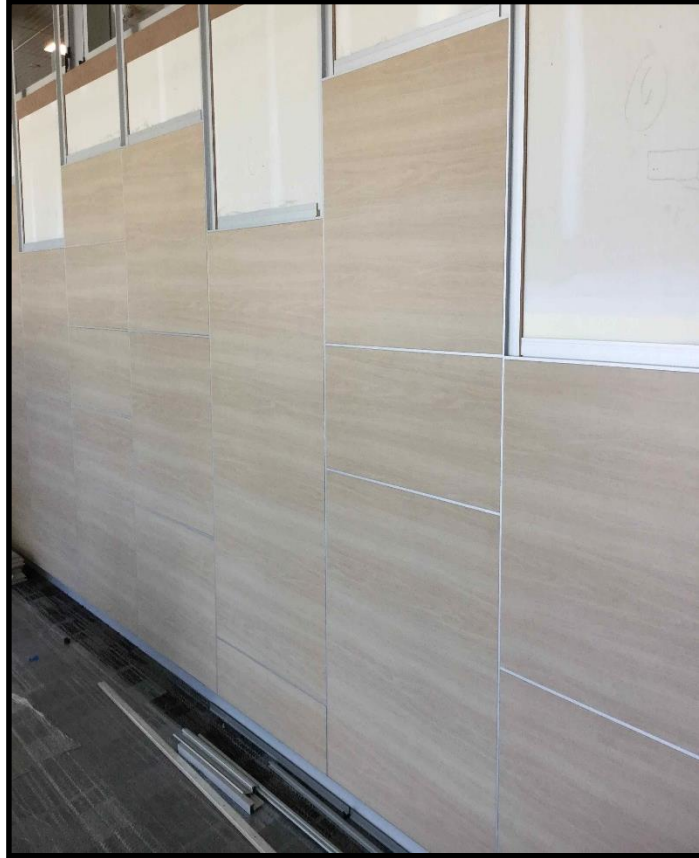

Meeting Room Wall Panels




Stair #2 Stair Treads

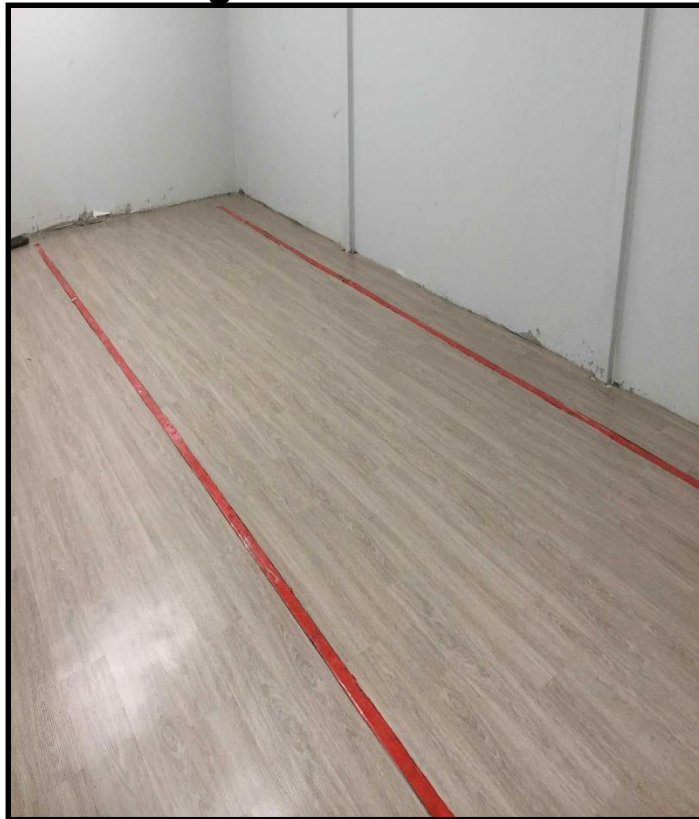

Vault Flooring



Wall Covering - 2nd Floor

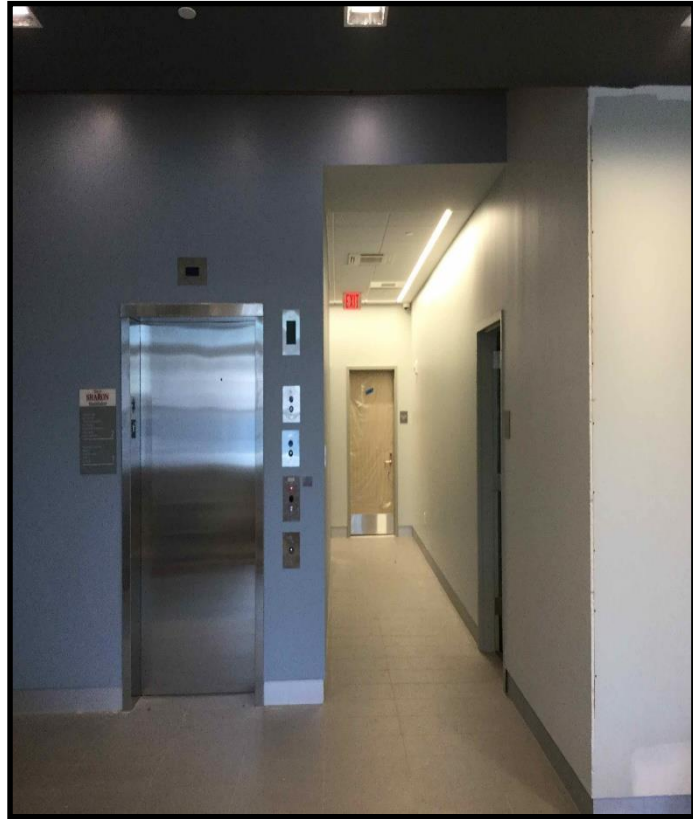

1st Floor Elevator



Entrance Door



Window Film Install
