

Sharon Town Hall Sharon, MA



COLANTONIO INC.
PROJECT # 18-3835

BJA

ARCHITECTS



samiotes

ARCHITECTURAL
ENGINEERS

TRAVERSE
landscape architects

The Sharon Standing Building Committee



Weekly Activity Update Friday September 20, 2019 Report #49

Current Week – Activities

- . Continue Punch List
- . Mow South lawn
- . Remove Granite Curbing – Old Town Hall
- . Clear and Grub – Old Town hall
- . Relocate Granite Curbing – Main Street
- . Finish Old Town hall Abatement
- . Receive Air Clearance – OTH Interior
- . Install Radio Box – IDF Room

Next Week – Activities

- . Install Granite Curbing Main Street
- . Prep Main Street Sidewalk for Concrete
- . Cut/Cap Water Connection East Chestnut
- . Cut/Cap Gas Connection Bradford Ave
- . Disconnect Electric Service Bradford Ave
- . File for Demolition Permit
- . Continue Punch list
- . Repair New Town Hall Site Lighting

Subcontractor	Trade	# of Workers Onsite
Color Concepts	Painting	01
Titan Contractors	Site	02
JR Vinagro	Abatement	10
Universal	Testing	01
Griffin Electric	Date/Electric	03
Aluminum Glass	Glass and Frames	01
Division 15	HVAC	01
Colantonio	Carpentry	01
BKA	Architect	02
Daedalus	Owner Representative	03
Colantonio Inc.	Construction Manager	03
TOTAL # Onsite This Week		28

Safety


- **Safety Orientation for New Jobsite Workers Performed First Day of Work. Total Number of Onsite Workers/Visitors Orientated = 153**
- **All Workers Wear Proper PPE At All Times**
- **Fencing and Scrim Reviewed Each Week for Safety and Appearance**
- **Weekly Toolbox Talks are Conducted Within Each Trade And a Copy is Submitted to Colantonio Inc.**
- **Each Contractor Completes a Daily Work Report which Is Kept On File**
- **Construction Progress Meeting are Held Tuesday at 1PM.**
- **293 Days With Zero Worker Accident**
- **293 Days Without a Lost Time Accident**

Quality Control

- **Materials Delivered To The Site Cross Referenced Against Drawings, Submittals and Specifications prior to installation.**
- **Colantonio Inc and Subcontractor Review of Drawings and Specification Compliance Prior to Work Commencing**
- **224 Random Quality Control Inspection Reports have been completed, of those: 00 remain as “Open” and “Non-Conforming”**

Miscellaneous


- **Tentative OTH Building Demolition Commence September 30,2019**
- **Sharon Fire Training in Old Town Hall Week of September 23, 2019**
- **Site Lighting to be Operational September 24, 2019**

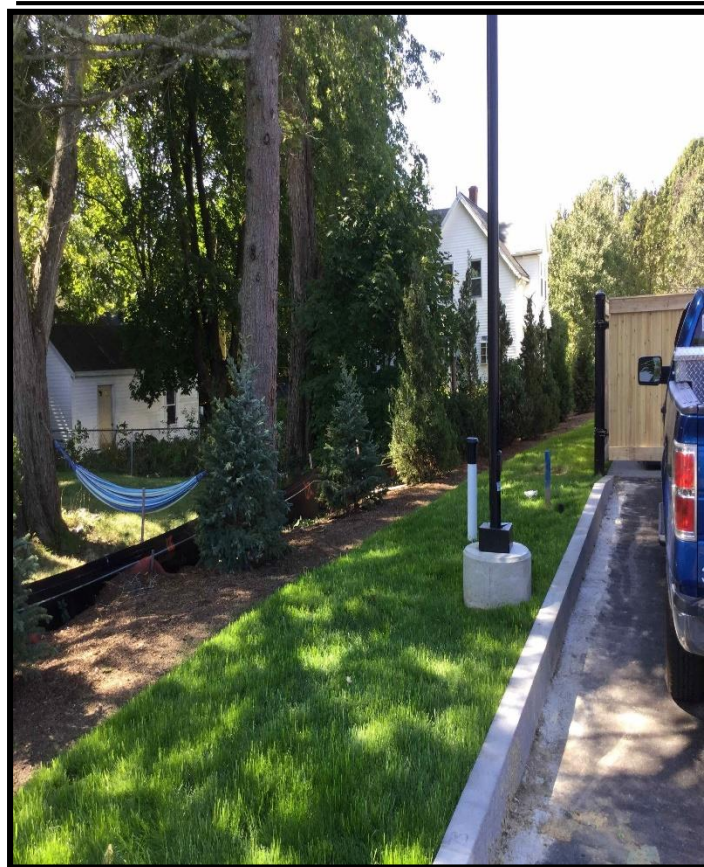


South Landscaping



Selective Demolition

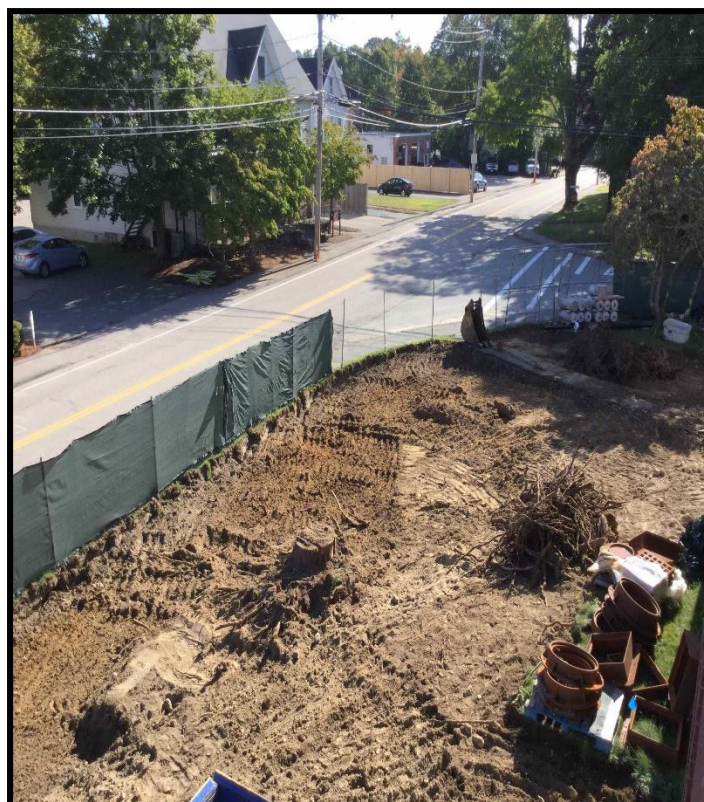

Clear and Grub

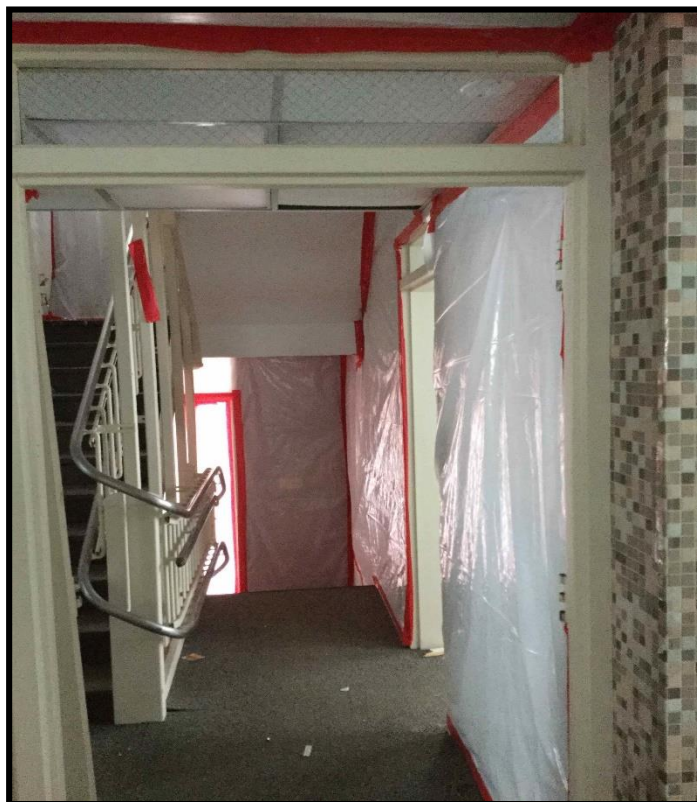

Abatement Prep
