

Sharon Town Hall Sharon, MA



COLANTONIO INC.
PROJECT # 18-3835

BJA

ARCHITECTS



samiotes

ARCHITECTURAL
ENGINEERS

TRAVERSE
landscape architects

The Sharon Standing Building Committee



Weekly Activity Update Friday September 27, 2019 Report #50

Current Week – Activities

- . Continue Punch List
- . Install granite Curbing – MainStreet
- . Prep for Sidewalks – Main Street
- . Load out Unsuitable Materials
- . Abatement Complete\
- . Building Clearance Letter
- . Cut and Cap Gas Service – Old Town Hall
- . Disconnect Elect. Service – Old Town Hall
- . Cut and Cap Water – Old Town Hall
- . Unload Ezra Schwartz Pavilion

Next Week – Activities

- . Form and Place Mai Street Sidewalks
- . Haul Materials Off Site
- . Cut and Cap Old 2" Water Feed
- . File for Demolition Permit
- . Begin Building Demolition

Subcontractor	Trade	# of Workers Onsite
Color Concepts	Painting	01
Titan Contractors	Site	04
JR Vinagro	Abatement	07
Universal	Testing	01
Griffin Electric	Date/Electric	02
Aluminum Glass	Glass and Frames	00
Division 15	HVAC	01
Colantonio	Labor	01
Columbia Gas	Utility	04
Eversource	Utility	03
BKA	Architect	02
Daedalus	Owner Representative	03
Colantonio Inc.	Construction Manager	03
TOTAL # Onsite This Week		32

Safety

- **Safety Orientation for New Jobsite Workers Performed First Day of Work. Total Number of Onsite Workers/Visitors Orientated = 153**
- **All Workers Wear Proper PPE At All Times**
- **Fencing and Scrim Reviewed Each Week for Safety and Appearance**
- **Weekly Toolbox Talks are Conducted Within Each Trade And a Copy is Submitted to Colantonio Inc.**
- **Each Contractor Completes a Daily Work Report which Is Kept On File**
- **Construction Progress Meeting are Held Tuesday at 1PM.**
- **298 Days With Zero Worker Accident**
- **298 Days Without a Lost Time Accident**

Quality Control


- **Materials Delivered To The Site Cross Referenced Against Drawings, Submittals and Specifications prior to installation.**
- **Colantonio Inc and Subcontractor Review of Drawings and Specification Compliance Prior to Work Commencing**
- **224 Random Quality Control Inspection Reports have been completed, of those: 00 remain as “Open” and “Non-Conforming”**

Miscellaneous

- **Tentative OTH Building Demolition Commence September 30,2019**
- **Sharon Fire Training in Old Town Hall Complete**
- **Site Lighting Operational**



Main Street Sidewalk Prep

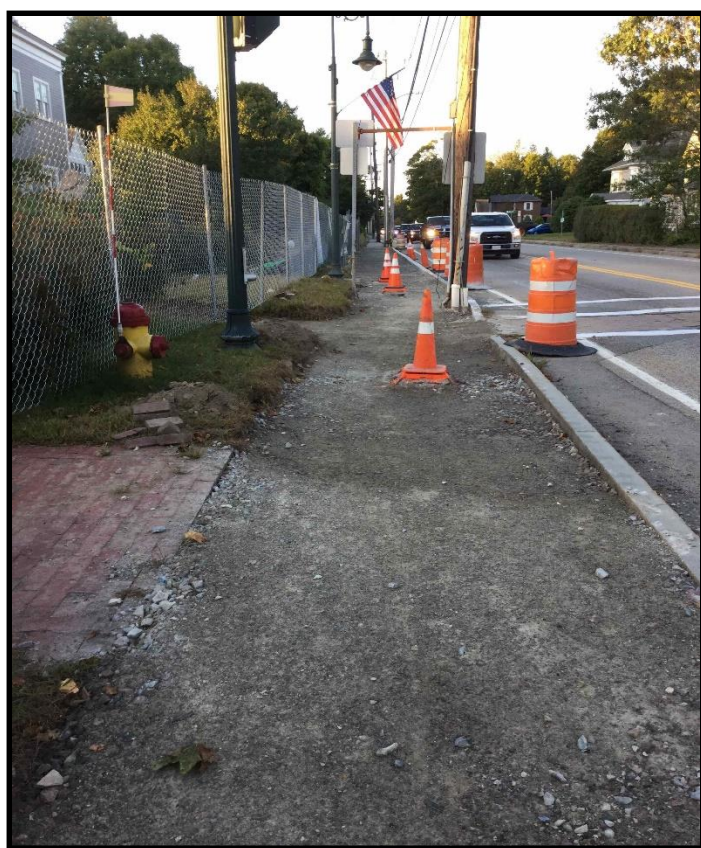

Sidewalk Prep



Ramp Removal



Excavate for Cut and Cap
