

# Sharon Town Hall Sharon, MA



**COLANTONIO INC.**  
**PROJECT # 18-3835**

**BKA**

ARCHITECTS



**DAEDALUS**

**samiotes**



ARCHITECTURAL  
**ENGINEERS**

**TRAVERSE**  
landscape architects

## The Sharon Standing Building Committee

**COLANTONIO**  
40 YEARS OF BUILDING RELATIONSHIPS

### Weekly Activity Update

December 07, 2019 Report #58

#### Current Week – Activities

- . Continue Paver Installation
- . Adjust Site Bollard Sensitivity
- . Receive Electronic Message Board
- . Site Clean Up

#### Next Week – Activities

- . Continue Brick Paver Installation
- . Install Main Street Building Sign
- . Install Electronic Message Board
- . Paint Porch Railings and Columns
- . Snow Melt Start Up
- . Clean Up

<b>Subcontractor</b>	<b>Trade</b>	<b># of Workers Onsite</b>
<b>Greenwood</b>	<b>Roofing</b>	<b>01</b>
<b>Federal</b>	<b>Concrete</b>	<b>05</b>
<b>Griffin</b>	<b>Electric</b>	<b>02</b>
<b>Labadini</b>	<b>Landscaping</b>	<b>05</b>
<b>BKA</b>	<b>Architect</b>	<b>02</b>
<b>Daedalus</b>	<b>Owner Representative</b>	<b>02</b>
<b>Colantonio Inc.</b>	<b>Construction Manager</b>	<b>03</b>
<b>TOTAL # Onsite This Week</b>		<b>20</b>

### **Safety**

- **Safety Orientation for New Jobsite Workers Performed First Day of Work. Total Number of Onsite Workers/Visitors Orientated = 164**
- **All Workers Wear Proper PPE At All Times**
- **Fencing and Scrim Removed from Porch Railings**
- **Weekly Toolbox Talks are Conducted Within Each Trade And a Copy is Submitted to Colantonio Inc.**
- **Each Contractor Completes a Daily Work Report which Is Kept On File**
- **Construction Progress Meeting are Held Tuesday at 1PM.**
- **352 Days With Zero Worker Accident**
- **352 Days Without a Lost Time Accident**

### **Quality Control**

- **Materials Delivered To The Site Cross Referenced Against Drawings, Submittals and Specifications prior to installation.**
- **Colantonio Inc and Subcontractor Review of Drawings and Specification Compliance Prior to Work Commencing**
- **245 Random Quality Control Inspection Reports have been completed, of those: 01 remain as “Open” and “Non-Conforming”**


### **Miscellaneous**

- **Main Entrance Open to the Public**
- **Sidewalks 100% Open to Public on Roads and On Site**





**Paver Installation**

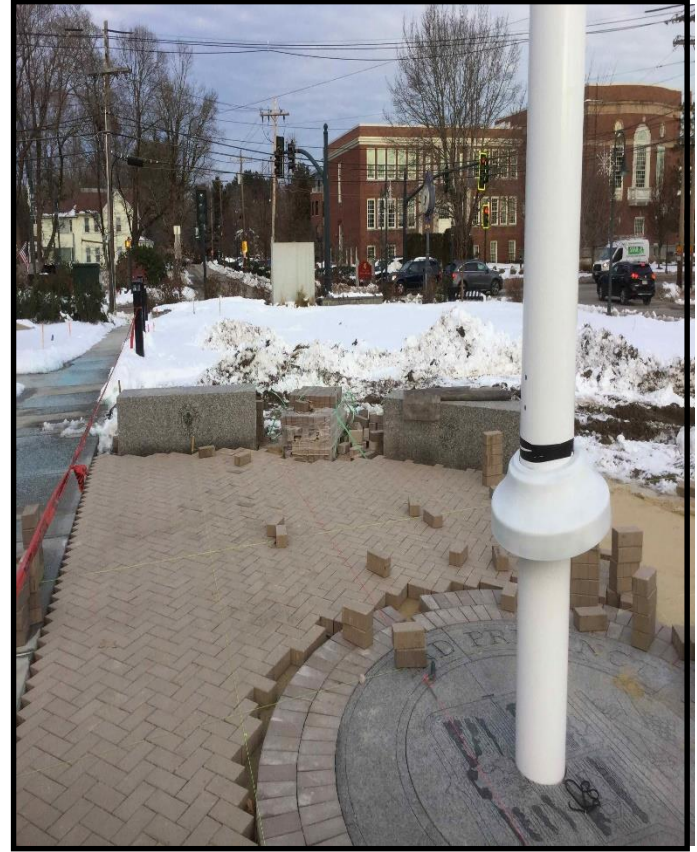

**Paver Installation**



**Sand and Paver Install**



**Center Medallion**
